केवल नागपुर कोर्ट के अधिकार में

Under Jurisdiction of Nagpur Court Only

वेस्टर्न कोलफील्ड्स लिमिटेड

WESTERN COALFIELDS LIMITED

(मिनीरत्न कंपनी) (A Miniratna Company)

(कोल इंडिया लि. की अनुषंगी कंपनी)

(A Subsidiary of Coal India Limited

एक कदम स्वच्छता की ओर

उपक्षेत्रिय प्रबन्धक का कार्यालय
घोंसा उपक्षेत्र

Ghonsa Sub Area,
Wani North Area
घोंसा उपक्षेत्र, वनी उत्तर क्षेत्र

Office of the Sub Area Manager
Ghonsa Sub Area.
www.westerncoal.nic.in

पंजी.का: पो.रासा, तह. वनी, जि. यवतमाल (महाराष्ट्र)-445304/ Regd. Off Po Rasa, Tah Wani , Dist. Yavatmal Mah- 445304

संदर्भ संख्या: वेकोलि/व.ना.क्षे./घो.उ.क्षे./उ.क्षे.प्र./2025-26/ 321 दिनांक : 26/05/2025

प्रति,

अपर मुख्य प्रधान वन संरक्षक,

पर्यावरण, वन और जलवायु परिवर्तन मंत्रालय,

क्षेत्रीय कार्यालय (पश्चिम केन्द्रीय क्षेत्र),

भूतल, ईस्ट विंग, न्यू सेक्रेटरीएट बिल्डिंग,

सिविल लाइन्स, नागपुर – 440 001 (महाराष्ट्र राज्य)

विषय:- Six Monthly Compliance Report of Conditions Stipulated in Environmental Clearance for **Ghonsa Opencast Coal Mine (0.60 MTPA)** of Wani North Area, WCL for the period **October'2024 to March'2025.**

महोदय,

With reference to above subject matter, please find enclosed herewith the Six Monthly Compliance Report of Conditions Stipulated in Environmental Clearance for **Ghonsa Opencast Coal Mine (0.60 MTPA)** of Wani North Area, WCL for the period **October'2024 to March'2025.**

For your kind information please.

Thanking you Sir.

भवदीय

उपक्षेत्रीय प्रबंधक
घोन्सा उपक्षेत्र

प्रतिलिपि:

1. क्षेत्रीय महाप्रबन्धक, वणी नार्थ क्षेत्र
2. महाप्रबंधक (पर्यावरण/विभागाध्यक्ष), वेस्टर्न कोलफील्ड्स लिमिटेड, मुख्यालय, नागपुर, महाराष्ट्र - 440 001
3. क्षेत्रीय अधिकारी, महाराष्ट्र प्रदूषण नियंत्रण बोर्ड, प्रथम तल, उद्योग भवन, स्टेशन रोड, चंद्रपुर, महाराष्ट्र – 442 401
4. क्षेत्रीय नोडल अधिकारी(पर्या.), वणी नॉर्थ क्षेत्र
5. कार्यालय प्रति

INDEX

Sr No	Contents
1	Environmental Clearance letter
2	Consent to operate
3	Data Sheet
4	Six Monthly Compliance Report of E. C. conditions
5	Environment Monitoring Reports of October 2024 to March 2025
6	Ground water level & Quality analysis Report
7	Land Restoration – Reclamation monitoring report (Based on satellite data)
8	Environment Audit Statement 2023-24

No.J-11015/165/2009-IA-II (M) pt. file
Government of India
Ministry of Environment, Forest and Climate Change
IA-II (Coal Mining) Division

Indira Paryavaran Bhawan,
Jorbagh Road, N Delhi-3
Dated: 8th June, 2017

To,

The General Manager (Environment),
M/s Western Coalfields Ltd,
Coal Estate, 9th Floor, Civil Lines.
Nagpur - 1 (Maharashtra)

Email: gmenvironment.wcl@nic.in; wclenv@yahoo.in

Sub: Expansion of Ghonsa OCP of capacity 0.60 MTPA of M/s Western Coalfields Ltd with increase in land area from 128.79 ha to 278.683 ha located in District Yavatmal (Maharashtra) - Environmental Clearance - reg.

Sir,

This is with reference to your letter No. WCL/ENV/HQ/11-B/95 dated 10.03.2016, online proposal No. IA/MH/CMIN/61865/2013 and subsequent letters/email dated 27.04.2016, 07.05.2016, 13.05.2016, 21.09.2016, 23.09.2016, 05.10.2016, 31.01.2017, 20.03.2017, 18.04.2017 and 27.04.2017 for grant of environmental clearance to the above-mentioned project.

2. The Ministry of Environment, Forest and Climate Change has considered the application. It is noted that the proposal is for grant of environmental clearance to the expansion of Ghonsa OCP of capacity 0.60 MTPA of M/s Western Coalfields Ltd with increase in land area from 128.79 ha to 278.683 ha located in District Yavatmal (Maharashtra)

3 The proposal was considered in its 55th EAC meeting held on 11-13 May, 2016, 4th reconstituted EAC meeting held on 30-31 January, 2017 and 9th meeting held on 27-28 April, 2017. The details of the proposal, as per the documents submitted by the project proponent, and also as informed during the meeting, are reported to be as under:-

(i) EC was granted vide letter no J-11015/165/2009-IA-II (M) dated 29th February, 2012 for Phase-I of Ghonsa OC for 0.45 MTPA in an area of 128.79 ha. EC was further granted under 7(ii) of EIA notification 2006 vide letter no J-11015/165/2009-IA-II (M) dated 8th December, 2014 for expansion in production capacity from 0.45 MTPA to 0.60 MTPA within same mine lease area of 128.79 ha.

(ii) The latitude and longitude of the project are 19° 57'11" to 19° 58'35" N and 78° 49'30" to 78° 50' 25" E respectively.

(iii) Joint Venture: There is no Joint venture

(iv) Coal Linkage: Thermal power plants of MAHAGENCO & Miscellaneous consumers.

(v) Employment generated / to be generated: Required Manpower for the project is 108 Nos.

(vi) Benefits of the project: This project will thus bridge the gap to the extent of the peak production capacity of the project) between demand & supply of non – coking coal for power plants& other bulk consumers from Western as well as Southern part of the country.

(vii) The land usage of the project will be as follows:

Pre-Mining:

Agriculture Land	204.443 ha
Forest Land	24 0 ha
Waste land	50.240 ha

Post- Mining:

S. No	Land use post mining	Land use (ha)				
		Plantation	Water Body	Public use	Undis-turbed	Total
1	External OB Dump	29.35	0	0	0	29.35
2	Excavation Area	80	46.84	0	8.28	135.12
3	Infrastructure like Sub-station, CHP Service Buildings etc.	4	0	11	0	15
4	Diverted Road	0.25	0	1.25	0	1.5
5	Blasting Zone (including rationalization Area)	20	0	0	32.333	52.333
6	Future Extn. & Plain Land Plantation	0.76	0	0	14.24	15
7	Embankment	0	0	30.38	0	30.38
	Total	134.36	46.84	42.63	54 853	278 683

(viii) Total geological reserve is 20 50 MT The mineable reserve 4 90 MT, extractable reserve is 4.90 MT (balance as on 1.04.2016). The per cent of extraction would be 100 %.

(ix) The coal grade is GCV – 4684 Kcal/kg, G9 The stripping ratio is 1: 5.77 m3/t. The average Gradient is 1 in 12 to 1 in 7.5. There will be three seams.

(x) Thickness of the Seam:

Seam/Parting	Depth Range (floor) (m)		Thickness Range (m)	
	Min.	Max	Min	Max
Seam-II	8.95	84.30	2 80	6.30
Parting	12.30 m - 19.27 m			
Seam-I	11.25	107.20	0.85	3.50
Parting	6 95 m to 8.41 m			
Local Seam	-	-	[0.20]	1.10

Ghonsa OCP Expn n area from 128.79 ha to 276.68 ha by M/s WCL

(xi) Total estimated water requirement is 130 KLD.
(xii) The Method of mining would be Opencast with Shovel – Dumper Combination
(xiii) There is one external OB dump with Quantity of 3.27 Mm3(As on 01.04.2016) in an area of 29.35 ha ha with height of 60 meter above the surface level and one internal dump with Quantity of 25.85 Mm3 in an area of 88 28 ha (maximum height 30 m above ground level) .
(xiv) The final mine void would be in 46.84 ha with depth upto 75.m and the Total quarry area is 135.12 Ha. Backfilled quarry area of 80 Ha shall be reclaimed with plantation (and 8.28 ha of backfilled area shall remain as undisturbed). A void of 46.84 ha ha with depth varying upto 75 m which is proposed to be converted into a water body.
(xv) ForInightly environmental monitoring as per Existing EC is being carried out
(xvi) The life of mine is 9 Years
(xvii) Transportation: Coal transportation in pit by dumpers. Surface to siding by Tippers and loading at siding by pay loaders
(xviii) There is no R & R involved
(xix) Cost: Total capital cost of the project is Rs.102.47 crore (Existing Capital Rs.5 23 Crores & Additional Capital requirement Rs 97.24 Crores). CSR Cost: The fund for the CSR will be allocated based on 2% of the average net profit of the Company for the three immediate preceding financial years or Rs 2.00 per tonne of coal production of the previous year whichever is higher R&R Cost Nil. Environmental Management Cost: Capital Cost Rs 0.60 crores and Recurring cost Rs.6.00 per tonne.
(xx) Water body : The main drainage of the area is controlled by Vidharbha River which flows in south-westerly direction passing along the Central and Southern property and finally meets with Penganga River. A few small seasonal nalfahs passing through the property drain into Vidharbha River during rainy season.
(xxi) Approvals: Application submitted to CGWA vide letter no. WCL/ENV/HQ/20-J&17-U/567 dated 26.12.16 Mining plan has been approved vide letter no. WCL/BD/SECTT/BM-267/2015/2241 on 21.08.2015 by WCL Board. Mine closure plan is an integral part of mining plan.
(xxii) Wildlife issues. There are no national Parks, wildlife sanctuary, biosphere reserves found in the 10 km buffer zone.
(xxiii) Forestry issues. 24.0 ha is the forest land for which Stage-I FC has been obtained.
(xxiv) Total afforestation plan shall be implemented covering an area of 134.36 ha at the end of mining Green Belt over an area of 20 Ha ha. Density of tree plantation 2500 trees/ ha of plants.
(xxv) There are no court cases/violation pending with the project proponent
(xxvi) Public Hearing was held on 09.08.2011. The issues raised in the PH include land compensation. air pollution control, plantation & disposal of OB, water sprinkling & CSR works.
(xxvii) Public notice: Public notice issued in three local newspapers (In English, Marathi and Hindi) for inviting comments. No comments were received.
(xxviii) The proposal for expansion of Ghonsa Opencast Coal Mine involving an increase in production capacity from 0.30 MTPA to 0.45 MTPA and ML area from 128 ha to 293.65 ha was earlier discussed in the EAC meeting held on 3-4 January, 2012. The mine lease area of 293 65 ha involved 24 ha of forest land, for which the stage-I FC was not available while considering the proposal for grant of EC at that stage. In order to meet the production target, the EC for enhancement was granted for 0.45 MTPA in the existing land area without forest land i.e. 128.79 ha as Phase-I. Regarding phase-II for production capacity 0.45 MTPA in the extended ML area of 293.65 ha, EAC recommended the project for EC, mentioning about the Public

Hearing (PH) conducted 9th August, 2011. The Stage-I Forestry Clearance has since been obtained vide MoEF's letter dated 8th March, 2016

(xxix) The latest status of compliance of PH along with details of CSR activities (from 2010-11 to 2013-14) taken up in the subject mine as well as various pollution control measures taken up in the surrounding operating mines of Wani North Area of WCL have been compiled in the form of a booklet. It may be seen that all the issues raised in the Public Hearing have been duly addressed and the work completed. Further, additional works beyond the works committed during PH have also been completed and listed in the booklet. As such, the Public Hearing has been duly completed for the mining area of 293 ha and the present area of 278.683 ha is within the same land area of 293 ha and there is no change in location, type of mining etc.

(xxx) Re-inspection by the Regional Office, MoEF&CC has been conducted and the fresh Regional Office's report as received vide no. 3-29/2012 (ENV) dated 7th September, 2016 The same was deliberated in the meeting.

(xxxi) The Mine Closure Plan (MCP) for the existing Mine vis-a-vis existing Environmental Clearance (EC) has been prepared and duly approved by WCL Board. Further, based on the existing EC and the Project Report, the Escrow Account details as well as details of Corpus have also been submitted along with the compliance report. As such, the final Mine Closure Plan vis-a-vis the existing mine / existing EC is not applicable, hence not prepared. However, the progressive Mine Closure Plan for the expansion project (with enhanced land area) as per Ministry of Coal's guidelines dated 07.01.2013 has been prepared and approved.

(xxxii) Fresh air quality and water quality data are monitored & submitted.

(xxxiii) The instant proposal is for grant of EC to Ghonsa OCP at its existing capacity of 0.60 MTPA, but in the mine lease area increased from 128.79 ha to 278.683 ha located in District Yavatmal (Maharashtra).

(xxxiv) Out of the total area of 278.683 ha, forest land involved is 24 ha, for which stage-I FC has been obtained on 8th March, 2016

(xxxv) As desired by the EAC in its meeting held on 31st January, 2017, public notice was issued on 22nd February, 2017 in three local newspapers in English, Hindi and Marathi inviting comments/suggestions from the locals/stakeholders within three weeks, and thus fulfilling the requirement of public consultations. There have been no comments/suggestions so far.

4. The EAC, after detailed deliberations on the proposal in the 9th meeting held on 27-28 April, 2017 decided for exempting the proposal from the requirement of fresh TOR and fresh Public Hearing, and recommended the proposal for grant of Environmental Clearance. The Ministry of Environment, Forest and Climate Change hereby accords Environmental Clearance to the **Expansion of Ghonsa OCP of capacity 0.60 MTPA of M/s Western Coalfields Ltd with increase in land area from 128.79 ha to 278.683 ha located in District Yavatmal (Maharashtra)** under the provisions of the Environment Impact Assessment Notification, 2006 and subsequent amendments/circulars thereto, subject to the compliance of the following terms and conditions and environmental safeguards mentioned below:

A. Specific Conditions

(i) The maximum production from the mine at any given time shall not exceed the limit as prescribed in the EC.

(ii) The validity of the EC is for the life of the Mine or as specified in the EIA Notification, 2006, whichever is earlier.

(iii) The project proponent shall obtain Consent to Establish/Operate under the Air Act, 1981 and the Water Act, 1974 from the State Pollution Control for the Ghonsa OCP of 0.60 MTPA in the mine lease area of 278.683 ha in District Yavatmal (Maharashtra).
(iv) Transportation of coal to be carried out through rail network or the covered trucks. Mitigative measures to be undertaken to control dust and other fugitive emissions all along the roads by providing water sprinklers.
(v) Continuous monitoring of occupational safety and other health hazards, and the corrective actions need to be ensured.
(vi) Controlled blasting technique should be adopted to control ground vibrations and fly rocks.
(vii) A progressive afforestation plan shall be implemented covering an area of 134.36 ha at the end of mining, which includes reclaimed External OB dump area 29.35ha, Internal OB dump area (80.0 ha) and Green belt (20 ha) and in township located outside the lease by planting native species in consultation with the local DFO/Agriculture Department. The density of the trees shall be around 2500 plants per ha. Massive plantation shall be carried out in open spaces in and around the mine and a 3-tier avenue plantation along the main approach roads to the mine.
(viii) An estimated total 29.12 Mm^3 of OB will be generated during the entire life of the mine. Out of which 3.27 Mm^3 of OB will be dumped in one external OB Dumps an earmarked area covering 29.35 ha of land. 25.85 Mm^3 of will be one internal OB dump in covering an area of 88.28 ha. The maximum height of internal OB dump will not exceed 30 m above ground level. The maximum slope of the dump shall not exceed 28 degrees. Monitoring and management of reclaimed dump sites shall continue till the vegetation becomes self- sustaining and compliance status shall be submitted to Regional Office on yearly basis.
(ix) Of the total quarry area of 135.12 ha, the backfilled quarry area of 80 ha shall be reclaimed with plantation and a void of 46.84 ha with maximum depth of 75 m is proposed to be converted into a water body shall be gently sloped and the upper benches shall be terraced and stabilised with plantation/afforestation by planting native plant species in consultation with the local DFO/Agriculture Department. The density of the trees shall be around 2500 plants per ha.

B. General Conditions

(a) Mining

(i) No change in mining technology and scope of work shall be made without prior approval of the Ministry of Environment, Forest and Climate Change. No change in the calendar plan including excavation, quantum of coal and waste should be made
(ii) Mining shall be carried out as per the approved mining plan, and also abiding by the relevant laws related to coal mining and the circulars issued by Directorate General Mines Safety (DGMS). An approved progressive Mine Closure Plan shall strictly be complied with and submitted.

(b) Land Reclamation

(i) Digital processing of the entire lease area using remote sensing technique shall be carried out regularly once in three years for monitoring land use pattern and report submitted to Ministry of Environment, Forest and Climate Change its Regional Office.

(ii) Final mine void depth should not be more than 40 m. The void area should be converted into water body. The remaining area should be back filled up to the ground level and covered with thick top soil. The land after mining should be restored for agriculture or forestry purpose
(iii) The top soil, if any, shall temporarily be stored at earmarked site(s) only and it should not be kept unutilized for long. The topsoil shall be used for land reclamation and plantation. The overburden dumps should be vegetated with suitable native species to prevent erosion and surface run off. The entire excavated area shall be backfilled and afforested in line with the approved Mine Closure Plan. Monitoring and management of rehabilitated areas should continue until the vegetation becomes self-sustaining Compliance status shall be submitted to the Ministry of Environment, Forest and Climate Change and its Regional Office on six monthly basis.
(iv) Greenbelt shall be developed all along the mine lease area in a phased manner. The width of the green belt along forest area should not be less than 7.5 m, and the total area covered by 3 tier green belt shall not be less than 100 ha. A 3-tier green belt comprising of a mix of native species shall be developed all along the major approach roads

(c) Emissions, Effluents, and Waste Disposal

(i) Transportation of coal by road should be carried out by covered trucks only. Effective measures such as regular water sprinkling shall be carried out in critical areas prone to air pollution and having high levels of PM_{10} and $PM_{2.5}$ such as haul road, loading and unloading point and transfer points. Fugitive dust emissions from all the sources shall be controlled regularly It shall be ensured that the Ambient Air Quality parameters conform to the norms prescribed by the Central/State Pollution Control Board in this regard.
(ii) Vehicular emissions shall be kept under control and regularly monitored. Project should obtain 'PUC' certificate for all the vehicles from authorized pollution testing centres.
(iii) Adequate ambient air quality monitoring stations shall be established in the core zone as well as in the buffer zone for monitoring of pollutants, namely PM_{10}, $PM_{2.5}$, SO_2 and NOx. Location of the stations shall be decided based on the meteorological data, topographical features and environmentally and ecologically sensitive targets in consultation with the State Pollution Control Board. Monitoring of heavy metals such as Hg, As, Ni, Cd, Cr, etc carried out at least once in six months.
(iv) Crusher/feeder and breaker material transfer points should invariably be provided with dust suppression system. Belt-conveyors should be fully covered to avoid air borne dust. Drills shall be wet operated or fitted with dust extractors.
(v) The project proponent shall not alter the major channels around the site. Appropriate embankment should be provided along the side of the river/nallah flowing near or adjacent to the mine. The embankment constructed along the river/nallah boundary should be of suitable dimensions and critical patches should be strengthened by stone pitching on the river front side and stabilised with plantation so as to withstand the peak water flow and prevent mine inundation.
(vi) Rainwater harvesting shall be implemented for conservation and augmentation of ground water resources in the area in consultation with Central Ground Water Board.
(vii) Catch drains and siltation ponds of appropriate size shall be constructed around the mine working, coal heaps and OB dumps to prevent run off of water and flow of sediments directly into the river and other water bodies. The water so collected should be utilized for watering the mine area, roads, green belt development etc The drains shall be regularly desilted particularly after monsoon and maintained properly. Sump capacity should provide

adequate retention period to allow proper settling of silt material. Dimension of the retaining wall to be constructed at the toe of the dumps and OB benches within the mine to check run-off and siltation should be based on the rainfall data

(viii) Industrial waste water (CHP, workshop and waste water from the mine) should be properly collected and treated so as to conform to the standards prescribed under the Environment (Protection) Act, 1986 and the Rules made there under, and as amended from time to time. Oil and grease trap should be installed before discharge of workshop effluents.

(d) Noise & Vibration Control

(i) Adequate measures shall be taken for control of noise levels below 85 dBA in the work environment. Workers engaged in blasting and drilling operations, operation of HEMM, etc shall be provided with ear plugs/muffs.

(ii) Controlled blasting techniques should be practiced with use of delay detonators to mitigate ground vibrations and fly rocks.

(e) Occupational Health & Safety

(i) Besides carrying out regular periodic health check-up of their workers, 20% of the workers identified from workforce engaged in active mining operations shall be subjected to health check-up for occupational diseases and hearing impairment, if any, through an specialised agency /institution within the District/State and the results reported to this Ministry and to DGMS.

(ii) Personnel working in dusty areas should wear protective respiratory devices and they should also be provided with adequate training and information on safety and health aspects. Supervisory staff shall be held responsible for ensuring compulsory wearing of dust mask

(iii) In case of outsourcing of work through MDO, the project proponent shall ensure the strict enforcement of the above conditions.

(f) Biodiversity

(i) The project proponent shall take all precautionary measures during mining operation for conservation and protection of endangered fauna, if any, spotted in the study area. Action plan for conservation of flora and fauna shall be prepared and implemented in consultation with the State Forest and Wildlife Department. A copy of action plan shall be submitted to the Ministry of Environment, Forest and Climate Change and its Regional Office.

(g) Implementation of Action Plan as per Public Hearing and CSR Activities

(i) Implementation of Action Plan on the issues raised during the Public Hearing shall be ensured. The Project Proponent shall complete all the tasks as per the Action Plan submitted with budgetary provisions during the Public Hearing. Land oustees should be compensated as per the norms laid out R&R Policy of the Company or the National R&R Policy or R&R Policy of the State Government, whichever is higher.

(ii) The Board of every company, shall ensure that the company spends, in every financial year, at least two per cent. of the average net profits of the company made during the three immediately preceding financial years, in pursuance of its Corporate Social Responsibility Policy

under Section 135 of the Companies Act, 2013, for the socio economic development of the neighbourhood.

(h) Corporate Environment Responsibility

(i) The Company should have a well laid down Environment Policy approved by the Board of Directors.
(ii) To have proper checks and balances, the Company should have a well laid down system of reporting of non-compliances/violations of environmental norms to the Board of Directors of the Company and/or shareholders or stakeholders at large.
(iii) A separate environmental management cell with suitable qualified personnel should be set-up under the control of a Senior Executive, who will report directly to the Head of the Organization.
(iv) The funds earmarked for environmental protection measures should not be diverted for other purpose. Year wise expenditure should be reported to the Ministry and its Regional Office.

(I) Statutory Obligations

(i) Environmental clearance is granted subject to final outcome of Hon'ble Supreme Court of India, Hon'ble High Court, NGT and any other Court of Law, if any, as may be applicable to the project.
(ii) This Environmental Clearance is subject to obtaining requisite NBWL Clearance from the Standing Committee of National Board for Wildlife, if any, as applicable to the project
(iii) The project proponent shall obtain Consent to Establish and Consent to Operate from the concerned State Pollution Control Board prior to increase in capacity of washery and effectively implement all the conditions stipulated therein.
(iv) Project Proponent shall obtain the necessary prior permission from the Central Ground Water Authority (CGWA) for drawl of water (surface and ground water).

(j) Monitoring of Project

(i) Regular monitoring of ground water level and quality shall be carried out in and around the mine lease by establishing a network of existing wells and constructing new piezometers during the mining operation. The monitoring shall be carried out four times in a year pre-monsoon (April-May), monsoon (August), post-monsoon (November) and winter (January) and the data thus collected may be sent regularly to Ministry of Environment, Forest and Climate Change and its Regional Office, Central Ground Water Authority and Regional Director, Central Ground Water Board.
(ii) The project proponent shall submit six monthly reports on the status of the implementation of the stipulated environmental safeguards to the Ministry of Environment, Forest and Climate Change, its Regional Office, Central Pollution Control Board and State Pollution Control Board
(iii) The Regional Office of this Ministry shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data/information/monitoring reports.
(iv) The activities pertaining to development of green belt/horticulture shall be reported to concerned Regional Office of MoEF&CC on six monthly basis from the date of commencement of mining operations.

(v) For half yearly monitoring reports, the data should be monitored for the period of April to September and October to March of the financial years and submitted to the concerned authorities within 2 months of the completion of periodicity of monitoring.

(k) Miscellaneous

(i) A copy of clearance letter will be marked to concerned Panchayat/local NGO, if any, from whom suggestion / representation has been received while processing the proposal
(ii) An electronic copy of the EC letter shall be marked to the concerned State Pollution Control Board, Regional Office, District Industry Sector and Collector's Office/Tehsildar Office for information in public domain within 30 days.
(iii) The EC letter shall be uploaded on the company's website. The compliance status of the stipulated EC conditions shall also be uploaded by the project authorities on their website and updated at least once every six months so as to bring the same in public domain. The monitoring data of environmental quality parameter (air, water, noise and soil) and critical pollutant such as PM_{10}, $PM_{2.5}$, SO_2 and NO_x (ambient) and critical sectoral parameters shall also be displayed at the entrance of the project premises and mine office and in corporate office and on company's website
(iv) The project authorities should advertise at least in two local newspapers widely circulated, one of which shall be in the vernacular language of the locality concerned, within 7 days of the issue of the clearance letter informing that the project has been accorded environmental clearance and a copy of the clearance letter is available with the State Pollution Control Board and also at web site of the Ministry of Environment, Forest and Climate Change at www.environmentclearance.nic.in and a copy of the same should be forwarded to the Regional Office.
(v) The Environmental Statement for each financial year ending 31 March in Form-V is mandated to be submitted by the PP for the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be uploaded on the Company's website along with the status of compliance of EC conditions and shall be sent to the respective Regional Offices of the MoEF&CC by e-mail

5. The project proponent shall abide by all the commitments and recommendations made in the EIA/EMP report and also that during their presentation to the EAC. The commitment made by the project proponent to the issue raised during Public Hearing shall be implemented by the proponent.

6. The project proponent shall obtain all necessary clearances/approvals that may be required before the start of the project. The Ministry or any other competent authority may stipulate any further condition for environmental protection.

7. The PP shall set up an Environment Audit cell with responsibility and accountability to ensure implementation of all the EC Conditions.

8. Concealing factual data or submission of false/fabricated data and failure to comply with any of the conditions mentioned above may result in withdrawal of this EC and attract action under the provisions of Environment (Protection) Act, 1986.

9. The above conditions will be enforced inter-alia, under the provisions of the Water (Prevention & Control of Pollution) Act, 1974, the Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986 and the Public Liability Insurance Act, 1991 along with their amendments and Rules and any other orders passed by the Hon'ble Supreme Court of India/High Courts and any other Court of Law relating to the subject matter. The PP shall ensure to undertake and provide for the costs incurred for taking up remedial measures in case of soil contamination, contamination of groundwater and surface water, and occupational and other diseases due to the mining operations.

10. Any appeal against this EC shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.

11. This EC supersedes the earlier EC granted vide letter No.J-11015/165/2009-IA-II(M) dated 8th December, 2014 for expansion in production capacity from 0.45 MTPA to 0.60 MTPA in ML area of 128.79 ha.

8/6/2017

(S. K. Srivastava)
Scientist E

Copy to:

1. The Secretary, Ministry of Coal, Shastri Bhawan, New Delhi.
2. The Secretary, Department of Environment, Government of Maharashtra, 15th Floor, New Admn. Bldg., Madam Cama Road, Mumbai - 32.
3. The APCCF, Ministry of Environment Forest and Climate Change, Regional Office (Western Central Zone), Ground Floor, East Wing, New Secretariat Building Civil Lines, Nagpur (Maharashtra)
4. The Member Secretary, Maharashtra State Pollution Control Board, Kalapataru Point, 3rd & 4th Floors Sion, Matunga Scheme Road No. 8, Opp. Cine Planet Cinema, Near Sion Circle, Sion (E), Mumbai – 400 002.
5. The Member Secretary, Central Pollution Control Board, CBD-cum-Office Complex, East Arjun Nagar, Delhi -110 032.
6. The Member-Secretary, Central Ground Water Authority, Ministry of Water Resources, Curzon Road Barracks, A-2, W-3 Kasturba Gandhi Marg, New Delhi.
7. The District Collector, Nagpur, Government of Maharashtra
8. Monitoring File 9. Guard File 10. Record File 11 Notice Board

8/6/2017

(S. K. Srivastava)
Scientist E

MAHARASHTRA POLLUTION CONTROL BOARD

Tel: 24010706/24010437
Fax: 24023516
Website: http://mpcb.gov.in
Email: cac-cell@mpcb.gov.in

Kalpataru Point, 2nd, 3rd and 4th floor, Opp. Cine Planet Cinema, Near Sion Circle, Sion (E), Mumbai-400022

RED/L.S.I (R35)
No:- Format1.0/CC/UAN No.MPCB-CONSENT-0000194377/CR/2504002667

Date: 24/04/2025

To,
M/s. Ghonsa Opencast Mine,
Western Coalfields Limited,
25/1,2,3,Ghonsa village, Po.- Rasa
Tal-Wani, Dist-Yavatmal.

Your Service is Our Duty

Sub: Renewal of consent to operate under Red Category

Ref:

1. Previous consent granted by Board vide No. Format1.0/CAC?UAN No. MPCB-CONSENT-0000107029/CR/2203000019, dtd. 01/03/2022, valid upto 31/03/2023.
2. Environmental Clearance granted by MoEF CC, GoI vide letter J-11015/165/2009- IA.II(M), dtd. 08.06.2017.
3. Show Cause Notice issued vide No. MPCB/JD(APC)/SCN/TB-0015, dated 13/11/2024.
4. Reply to SCN vide letter dated 19.11.2024
5. Minutes of 12th Consent Committee meeting of 2024-25 held on 12/12/2024.
6. Minutes of 15th Consent Committee meeting of 2024-25 held on 12/02/2025.

Your application No.MPCB-CONSENT-0000194377 Dated 14.01.2024

For: grant of Consent to Operate under Section 26 of the Water (Prevention & Control of Pollution) Act, 1974 & under Section 21 of the Air (Prevention & Control of Pollution) Act, 1981 and Authorization under Rule 6 and Rule 18(7) of the Hazardous & Other Wastes (Management & Transboundary Movement) Rules 2016 is considered and the consent is hereby granted subject to the following terms and conditions and as detailed in the schedule I, II, III & IV annexed to this order:

1. **The consent to renewal is granted for a period up to 31/03/2026**
2. **The capital investment of the project is Rs.123.5761 Crs. (As per undertaking submitted by pp (Existing Consented CI Rs.122.3544 Crs.+ Increased in CI by Rs. 1.2217 Crs.= Total CI Rs. 123.5761 Crs.)**
3. **Consent is valid for the manufacture of:**

Sr No	Product	Maximum Quantity	UOM
Products			
1	COAL Mining over mining lease area 278.683 Ha.	0.6	MTPA

4. **Conditions under Water (P&CP), 1974 Act for discharge of effluent:**

Sr No	Description	Permitted (in CMD)	Standards to	Disposal Path
1.	Trade effluent	4363	As per Schedule-I	Recycle for dust suppression, Fire Fighting, gardening and excess discharge into nearby nallah after confirming the prescribed consented norms.
2.	Domestic effluent	10	As per Schedule-I	On land for gardening

5. **Conditions under Air (P& CP) Act, 1981 for air emissions:**

Sr No.	Stack No.	Description of stack / source	Number of Stack	Standards to be achieved
NA				

6. **Non-Hazardous Wastes:**

Sr No	Type of Waste	Quantity	UoM	Treatment	Disposal
1	Overburden	1175000	m3/month	Landfill	Backfilling and Reclamation of Land

7. **Conditions under Hazardous & Other Wastes (M & T M) Rules 2016 for Collection, Segregation, Storage, Transportation, Treatment and Disposal of hazardous waste:**

Sr No	Category No./ Type	Quantity	UoM	Treatment	Disposal
1	5.1 Used or spent oil	25	KL/A	Recycle	Authorized Reprocessor/Recycler
2	5.2 Wastes or residues containing oil	6	MT/A	Incineration	CHWTSDF

8. The Board reserves the right to review, amend, suspend, revoke etc. this consent and the same shall be binding on the industry.
9. This consent should not be construed as exemption from obtaining necessary NOC/permission from any other Government authorities
10. The applicant shall comply with the conditions of the Environmental Clearance granted by MoEF CC, GoI vide letter J-11015/165/2009- IA.II(M) dtd. 08.06.2017.
11. PP shall install and commission CAAQMS arrangement and ensure the connectivity of the same to MPCB Server.
12. PP shall convert and operate existing water sprinkling arrangement into chemical fogging arrangement (MgCl2).
13. PP shall carry out over burden dump management as per CPCB guidelines.
14. PP shall carry out plantation as per EC condition before ensuing monsoon.
15. PP shall obtain valid NOC of CGWA and scrupulously follow the conditions of the same.
16. PP shall pay penal interest calculated as an actual for delay in submission of bank guarantee's within 01 month time period, failing which consent stands cancelled.
17. Consent is issued as per decision made in 15th Consent Committee meeting of 2024-25 held on 12/02/2025.

18. PP shall provide OCEMS at the outlet of discharge point and same shall be connected to the MPCB server.
19. The applicant shall make an application for renewal of consent 60 days prior to date of expiry of the consent.
20. The industry shall create an Environment Cell by appointing an Environmental Engineer OR Expert for looking after day-to-day activities related to Environment OR Pollution control.

This consent is issued on the basis of information/documents submitted by the Applicant/Project Proponent, if it has been observed that the information submitted by the Applicant/Project Proponent is false, misleading or fraudulent, the Board reserves its right to revoke the consent & further legal action will be initiated against the Applicant/Project Proponent.

35329a56
b41b826f
b1e3cca0
52ddef4a
c7be96c8
dae2cc25
1bb30123
c6e45adc

Signed by: Dr.Avinash Dhakne
Member Secretary
For and on behalf of
Maharashtra Pollution Control Board
ms@mpcb.gov.in
2025-04-24 12:07:25 IST

Received Consent fee of -

Sr.No	Amount(Rs.)	Transaction/DR.No.	Date	Transaction Type
1	974304.00	MPCB-DR-17013	30/01/2023	RTGS
2	3531896.00	MPCB-DR-33384	15/04/2025	RTGS
3	66976.00	MPCB-DR-33485	21/04/2025	NEFT

Copy to:

1. Regional Officer, MPCB, Chandrapur and Sub-Regional Officer, MPCB, Chandrapur
- They are directed to ensure the compliance of the consent conditions.
2. Chief Accounts Officer, MPCB,Sion, Mumbai
3. CC/CAC desk - for record & website updation purpose.

SCHEDULE-I

Terms & conditions for compliance of Water Pollution Control:

1. A] Mine water shall be treated in sedimentation tank of adequate capacity to achieve treated water quality within the prescribed consented norms.

   B] The Applicant shall operate the effluent treatment plant (ETP) to treat the trade effluent so as to achieve the following standards prescribed by the Board or under EP Act, 1986 and Rules made there under from time to time, whichever is stringent:

Sr.No	Parameters	Limiting concentration not to exceed in mg/l, except for pH
(1)	pH	5.5 to 9.0
(2)	Oil & Grease	10
(3)	BOD (3 days 27°C)	30
(4)	Total Suspended solids	100
(5)	Total Dissolved solids	2100
(6)	COD	250

   C] The treated effluent shall be recycled at maximum extent for dust suppression, Fire fighting and used on land for gardening and plantation in the mine lease area & excess if any shall be discharged into nearby local nalla after confirming the standards of outlet prescribed as above in the consent.

2. A] As per your application, you have provided Septic Tank followed by Soak pit for the treatment of 10 CMD of sewage.

   B] The Applicant shall operate the sewage treatment system to treat the sewage so as to achieve the following standards.

Sr.No	Parameters	Standards (mg/l)	
1	BOD (3 days 27°C)	Not to exceed	30 mg/l
2	COD	Not to exceed	100 mg/l
3	SS	Not to exceed	50 mg/l

   C] The treated sewage shall be discharged on land for gardening within premise after confirming above standards. In no case, sewage shall find its way to outside factory premises.

3. The Board reserves its rights to review plans, specifications or other data relating to plant setup for the treatment of waterworks for the purification there of & the system for the disposal of sewage or trade effluent or in connection with the grant of any consent conditions. The Applicant shall obtain prior consent of the Board to take steps to establish the unit or establish any treatment and disposal system or an extension or addition thereto.
4. The industry shall ensure replacement of pollution control system or its parts after expiry of its expected life as defined by manufacturer so as to ensure the compliance of standards and safety of the operation thereof.
5. The Applicant shall comply with the provisions of the Water (Prevention & Control of Pollution) Act, 1974 and as amended, by installing water meters and other provisions as contained in the said act:

Sr. No.	Purpose for water consumed	Water consumption quantity (CMD)
1.	Industrial Cooling, spraying in mine pits or boiler feed	652.00
2.	Domestic purpose	18.00
3.	Processing whereby water gets polluted & pollutants are easily biodegradable	0.00
4.	Processing whereby water gets polluted & pollutants are not easily biodegradable and are toxic	0.00
5.	Gardening	50

6. The Applicant shall provide Specific Water Pollution control system as per the conditions of EP Act, 1986 and rule made there under from time to time/ Environmental Clearance/ CREP guidelines.

SCHEDULE-II

Terms & conditions for compliance of Air Pollution Control:

1. As per your application, you have provided the Air pollution control (APC) system and erected following stack (s) to observe the following fuel pattern:

Stack No.	Source	APC System provided/proposed	Stack Height(in mtr)	Type of Fuel	Sulphur Content(in %)	Pollutant	Standard
NA	NA		0.00	-	-	NA	-

2. The Applicant shall provide Specific Air Pollution control equipments as per the conditions of EP Act, 1986 and rule made there under from time to time/ Environmental Clearance / CREP guidelines.
3. The Applicant shall obtain necessary prior permission for providing additional control equipment with necessary specifications and operation thereof or alteration or replacement/alteration well before its life come to an end or erection of new pollution control equipment.
4. The Board reserves its rights to vary all or any of the condition in the consent, if due to any technological improvement or otherwise such variation (including the change of any control equipment, other in whole or in part is necessary).
5. Control Equipments
   a. Coal handling plant shall be provided with GI sheet enclosures & automatic water sprinkler and shall be operated continuously.
   b. Scientific spraying of water on all working area, dump area, stock piles with the help of appropriate dust suppression system.
   c. Coal transportation shall be done by installing conveyors wherever possible & mechanically covered closed trucks shall be used for transportation. Overloading of dumpers shall be avoided to prevent spillages.
   d. The applicant shall carry out tree plantation along road side, around dumps or compulsory afforestation as per proposal approved by Forest Department. The tree plantation programme shall be taken up well in advance of the actual mining activity, so that green belt of sufficient width & height is developed between mining area/road and surrounding environment.
   e. Black topped metal roads shall be provided and shall be well maintained to prevent dust formation
   f. Slope of the over burden shall have slope not more than 28° to the horizontal. The overburden shall be covered by vegetation for stabilization.
   g. Correct type & quantity of explosive shall be used to avoid excess dust formation & vibration in the surrounding area.
6. Standards for Ambient Air Pollutants:

   The Suspended Particulate Matter (SPM), Respirable Particulate Matter (RPM), Sulphur dioxide (SO_2) and Oxides of Nitrogen (NO_x) concentration in downwind direction considering predominant wind direction, at a distance of 500 metres from the following dust generating sources shall not exceed the standards specified in the table given below:

   Dust Generating Sources:

   Loading or unloading, Haul Road, coal transportation road, Coal handling plant (CHP), Railway Sliding, Blasting, Drilling, Overburden dumps, or any other dust generating external sources like coke ovens (hard as well as soft), briquette industry, nearby road etc.

Pollutant	***Time weighted average***	***Concentration in Ambient Air***
Suspended Particulates Matter (SPM)	Annual Average	360 µg/m^3
	24 hours	500 µg/m^3
Respirable Particulate Matter (size less than 10 µm) (RPM)	Annual Average	180 µg/m^3
	24 hours	250 µg/m^3
Sulphur Dioxide (SO_2)	Annual Average	80 µg/m^3
	24 hours	120 µg/m^3
Oxides of Nitrogen as NO_x	Annual Average	80 µg/m^3
	24 hours	120 µg/m^3

i. In case of any residential or commercial or industrial place falls within 500 metres of any dust generating sources, the National Ambient Air Quality Standards notified vide MOEFCC GOI notification dtd 16.11.2009 as ammended shall be made applicable.

ii. The applicant shall provide minimum three ambient air quality monitoring stations within mining area which should be monitored for SPM, RSPM, SO_2, NOx, HC, CO etc. The Annual Arithmetic Mean of minimum 104 measurements in a year taken twice a week 24 hourly at uniform interval shall conform to the National Ambient Air Quality Standards prescribed under Air (Prevention and Control of Pollution) Act, 1981 and Environment (Protection) Act, 1986. The records of results of monitoring done shall be made available for inspection to the officers of the Board.

7. The applicant shall take adequate measures for control of noise levels from its own sources as follows:

Sr. No	***Location***	***Permissible Norms [in dB (A)]***	***Desired minimum thickness of green belt (m)***
1.	Along Road side	65 (Commercial Area)	20
2.	In colonies	55 (Residential Area)	20
3.	Near Opencast Mines	75 (Industrial Area)	10
4.	Near CHPs	75	30
5.	Near Shaft	75	20
6.	Near Mine exhaust fan	75	> 50

8. Other conditions:

i Whenever due to any accident or other unforeseen act or even, such emissions occur or is apprehended to occur in excess standards laid down, such information shall be forthwith reported to Board, concerned Police station, office of Directorate of Health services, Dept. of explosives, Inspectorate of Factories & Local Body. In case of failure of pollution control equipments, the production process connected to it shall be stopped.

SCHEDULE-III

Details of Bank Guarantees:

Sr. No.	Consent (C2E/ C2O /C2R)	Amt of BG Imposed	Submission Period	Purpose of BG	Compliance Period	Validity Date
1	C2R	Rs. 2.0 Lakh	15 days	Regular monitoring of ground water level and quality should be carried out by establishing the network of existing wells and constructing new piezometers during mining operations	Regular Activity	31/07/2026
2	C2R	Rs.5.0 Lakh	15 days	Catch drain and situation ponds of appropriate size should be constructed to arrest silt and sediment flow from soil, OB and mineral dumps. Water so collected should be utilized for watering of the mining area, roads green belt developers etc.	Regular Activity	31/07/2026
3	C2R	Rs.25.0 Lakh	15 days	Coal transportation shall be done by mechanically closed trucks. Overloading of shall be avoided to prevent spillages. 10% of total fleet available to be replaced every six month	Regular Activity	31/07/2026
4	C2R	Rs.5.0 Lakh	15 days	Coal Handling Plant (CHP) & loading / unloading area will be provided with Dust Collector and Automatic Water Sprinkler.	Regular Activity	31/07/2026
5	C2R	Rs.5.0 Lakh	15 days	Conversion and commissioning of existing water sprinkling arrangement into chemical fogging arrangement (M_gCI2)	Regular Activity	31/07/2026
6	C2R	Rs.10.0 Lakh	15 days	To provide tar road in the Mine area and to be well maintain to prevent dust formation	Regular Activity	31/07/2026
7	C2R	Rs.5.0 Lakh	15 days	Deploy mechanized sweepers which are automated suction sweeper for cleaning the coal dust from road.	Regular Activity	31/07/2026
8	C2R	Rs.5.0 Lakh	15 days	Adoption and installation of tyre wash system to mining transportation at entry and exit point of mining area.	Regular Activity	31/07/2026
9	C2R	Rs.5.0 Lakh	15 days	Use of toppers/binders/surfactants on the top surface of coal pile on trucks carrying coal on road to minimize spillage during transportation	Regular Activity	31/07/2026
10	C2R	Rs.5.0 Lakh	15 days	Installation and Commissioning of CAAQMS	Regular Activity	31/07/2026
11	C2R	Rs.5.0 Lakh	15 days	Install real time coal ash analyzer on pilot basis	Regular Activity	31/07/2026
12	C2R	Rs.5.0 Lakh	15 days	Over burden (OB) should be stacked at earmarked dumpsites only and should not be kept active for long period. Proper terracing of OB should be carried out so that the overall slope will come down to 28°. Over Burden shall be disposed by way of backfilling.	Regular Activity	31/07/2026
13	C2R	Rs.25.0 Lakh	15 days	Operation and Maintenance of pollution control system so as to maintain consented standards prescribed as per Air(Prevention & Control of pollution) Act, 1981, Water (Prevention & Control of Pollution) Act, 1974 & HW (MH & TM) Rules 2008 and also adhering to compliance of specific / general condition of Environment Clearance.	Regular Activity	31/07/2026

****Existing BG obtained for above purpose if any, may be extended for period of validity as above.**

If the above Bank Guarantee is not submitted within stipulated period, then 12% interest will be levied as a penalty as per circular dtd 29/02/2024 No. BO/MPCB/AS(T)/Circular/B-240229FTS0122

BG Forfeiture History

Srno.	Consent (C2E/C2O/C2R)	Amount of BG imposed	Submission Period	Purpose of BG	Amount of BG Forfeiture	Reason of BG Forfeiture
NA						

BG Return details

Srno.	Consent (C2E/C2O/C2R)	BG imposed	Purpose of BG	Amount of BG Returned
NA				

SCHEDULE-IV

General Conditions:

1. The applicant shall provide facility for collection of environmental samples and samples of trade and sewage effluents, air emissions and hazardous waste to the Board staff at the terminal or designated points and shall pay to the Board for the services rendered in this behalf.
2. If the MIDC pipeline is broken/ overflowing chamber, in such cases industry shall not discharge their treated effluent into MIDC drain, it shall be sent to CETP by tanker.
3. Industry should monitor effluent quality, stack emissions and ambient air quality monthly/quarterly.
4. The applicant shall provide ports in the chimney/(s) and facilities such as ladder, platform etc. for monitoring the air emissions and the same shall be open for inspection to/and for use of the Board's Staff. The chimney(s) vents attached to various sources of emission shall be designated by numbers such as S-1, S-2, etc. and these shall be painted/ displayed to facilitate identification.
5. Whenever due to any accident or other unforeseen act or even, such emissions occur or is apprehended to occur in excess of standards laid down, such information shall be forthwith Reported to Board, concerned Police Station, office of Directorate of Health Services, Department of Explosives, Inspectorate of Factories and Local Body. In case of failure of pollution control equipment, the production process connected to it shall be stopped.
6. The applicant shall provide an alternate electric power source sufficient to operate all pollution control facilities installed to maintain compliance with the terms and conditions of the consent. In the absence, the applicant shall stop, reduce or otherwise, control production to abide by terms and conditions of this consent.
7. The firm shall submit to this office, the 30th day of September every year, the Environmental Statement Report for the financial year ending 31st March in the prescribed Form-V as per the provisions of rule 14 of the Environment (Protection) (Second Amendment) Rules, 1992.
8. The industry shall recycle/reprocess/reuse/recover Hazardous Waste as per the provision contain in the H&OW(M&TM) Rules 2016, which can be recycled/processed/ reused/ recovered and only waste which has to be incinerated shall go to incineration and waste which can be used for land filling and cannot be recycled/ reprocessed etc. should go for that purpose, in order to reduce load on incineration and landfill site/environment.
9. The industry should comply with the Hazardous & Other Wastes (M & TM) Rules, 2016 and submit the Annual Returns as per Rule 6(5) & 20(2) of Hazardous & Other Wastes (M & TM) Rules, 2016 for the preceding year April to March in Form-IV by 30th June of every year.
10. An inspection book shall be opened and made available to the Board's officers during their visit to the applicant.
11. The applicant shall make an application for renewal of the consent at least 60 days before the date of the expiry of the consent.
12. Industry shall strictly comply with the Water (P&CP) Act, 1974, Air (P&CP) Act,1981 and Environmental Protection Act,1986 and industry specific standard under EP Rules 1986 which are available on MPCB website(www.mpcb.gov.in).
13. The industry shall constitute an Environmental cell with qualified staff/personnel/agency to see the day to day compliance of consent condition towards Environment Protection.
14. Separate drainage system shall be provided for collection of trade and sewage effluents. Terminal manholes shall be provided at the end of the collection system with arrangement for measuring the flow. No effluent shall be admitted in the pipes/sewers downstream of the terminal manholes. No effluent shall find its way other than in designed and provided collection system.
15. Neither storm water nor discharge from other premises shall be allowed to mix with the effluents from the factory.

16. The applicant shall install a separate meter showing the consumption of energy for operation of domestic and industrial effluent treatment plants and air pollution control system. A register showing consumption of chemicals used for treatment shall be maintained.
17. Conditions for D.G. Set
    a) Noise from the D.G. Set should be controlled by providing an acoustic enclosure or by treating the room acoustically.
    b) Industry should provide acoustic enclosure for control of noise. The acoustic enclosure/ acoustic treatment of the room should be designed for minimum 25 dB (A) insertion loss or for meeting the ambient noise standards, whichever is on higher side. A suitable exhaust muffler with insertion loss of 25 dB (A) shall also be provided. The measurement of insertion loss will be done at different points at 0.5 meters from acoustic enclosure/room and then average.
    c) Industry should make efforts to bring down noise level due to DG set, outside industrial premises, within ambient noise requirements by proper sitting and control measures.
    d) Installation of DG Set must be strictly in compliance with recommendations of DG Set manufacturer.
    e) A proper routine and preventive maintenance procedure for DG set should be set and followed in consultation with the DG manufacturer which would help to prevent noise levels of DG set from deteriorating with use.
    f) D.G. Set shall be operated only in case of power failure.
    g) The applicant should not cause any nuisance in the surrounding area due to operation of D.G. Set.
    h) The applicant shall comply with the notification of MoEFCC, India on Environment (Protection) second Amendment Rules vide GSR 371(E) dated 17.05.2002 and its amendments regarding noise limit for generator sets run with diesel.
18. The industry should not cause any nuisance in surrounding area.
19. The industry shall take adequate measures for control of noise levels from its own sources within the premises so as to maintain ambient air quality standard in respect of noise to less than 75 dB (A) during day time and 70 dB (A) during night time. Day time is reckoned in between 6 a.m. and 10 p.m. and night time is reckoned between 10 p.m. and 6 a.m.
20. The applicant shall maintain good housekeeping.
21. The applicant shall bring minimum 33% of the available open land under green coverage/ plantation. The applicant shall submit a yearly statement by 30th September every year on available open plot area, number of trees surviving as on 31st March of the year and number of trees planted by September end
22. The non-hazardous solid waste arising in the factory premises, sweepings, etc. be disposed of scientifically so as not to cause any nuisance / pollution. The applicant shall take necessary permissions from civic authorities for disposal of solid waste.
23. The applicant shall not change or alter the quantity, quality, the rate of discharge, temperature or the mode of the effluent/emissions or hazardous wastes or control equipment provided for without previous written permission of the Board. The industry will not carry out any activity, for which this consent has not been granted/without prior consent of the Board.
24. The industry shall ensure that fugitive emissions from the activity are controlled so as to maintain clean and safe environment in and around the factory premises
25. The industry shall submit official e-mail address and any change will be duly informed to the MPCB.
26. The industry shall achieve the National Ambient Air Quality standards prescribed vide Government of India, Notification dtd. 16.11.2009 as amended.

This certificate is digitally & electronically signed.

Ministry of Environment, Forests & Climate Change, Regional Office (WCZ), Nagpur

MONITORING PROFORMA: PART – I

Name of the Project	Expansion of Ghonsa OCP
Location and address	On Wani - Patan Main road at 3.00KM. At-Ghonsa , Po-Rasa, Tah- wani, Dist- Yavatmal, State- Maharashtra.
Address for correspondence	Office of the Sub Area Manager, Ghonsa Sub Area, Post-Rasa, Tah- Wani, Dist- Yavatmal, State- Maharashtra.
MoEF&CC Clearance Letter No. & Date	EC Letter No. J-11015/165/2009-IA.II(M) dated 8th June, 2017 Amended letter no. J/11015/165/2009-IA.II(M) Pt. date 10/01/2018
Period of Status Report	From **October 2024 to March 2025**
Date of commencement of the project Work	24-11-2008

STATUS OF LAND ACQUISITION:-

Type of Land	**Required as per EIA-EMP (ha)**	**Actual acquired (ha) As on 31.03.2025**
Agriculture	204.443	204.443
Forest Land	24.00	24.00
Waste Land (Govt. Land)	50.240	50.240
Total	278.683	278.683

STATUS OF LEGAL COMPLIANCES: -

a. Consent under Air (Prevention and control of Pollution) Act.	Consent to Operate has been granted by MPCB vide Consent Order No. RED/L.S.I (R35)No:- Format1.0/CAC/UAN No.MPCBCONSENT-0000194377/CR/2504002667 dated 24.04.2025 Valid upto 31.03.2026
b. Consent under Water (Prevention and Control of Pollution) Act.	
b. Consent under Water (Prevention and control of Pollution) Cess Act	
c. Environment (Protection) Act.	Environment Clearance accorded vide MoEF&CC, New Delhi vide EC Letter No. J-11015/165/2009-IA.II(M) dated 8th June, 2017. Environment Audit statement for the year **2023-24** has been submitted online on MPCB portal.
d. Forest (Conservation) Act	Forest Clearance accorded by RO(WCZ), MoEF&CC, Nagpur vide letter no.: F.No. 6-MHC-30/2014-BHO/2372 dated 7th September, 2017 for 24Ha forest land at Mauja Ghonsa.

PART –II
STATUS OF ENVIRONMENT

Air Pollution Control :-

a) No. of ambient air monitoring stations & frequency of monitoring	04 Nos. Ambient Air quality (Fortnightly Monitoring)
b) Name of the location	**Ambient Air Quality Monitoring Stations** 1.Project Manager Office(Ghonsa) : WNGOA-1 2.SAM Office/ Canteen: WNKUA-2 3.Ghonsa Village:WNGOA-3 4.GUEST HOUSE/COLONY : WNGOA-4
c) Ambient air quality status for the parameters prescribed by state pollution control board.	Location | SPM | PM10 | SO_x | NO_x | PM2.5 Reports of Environmental Monitoring for the period from **October 2024 to March 2025** has been enclosed

Water Pollution Control :-

a). No. of stations and frequency of monitoring	One, Fortnightly
b). Description of locations	1)Mine Water discharge: WNGOW-1
c). Average concentrations of major pollutants prescribed by State Pollution Control Board (fig. in mg/lit except pH)	Location | **pH** | **COD** | **TSS** | **O&G** Reports of Environmental Monitoring Report for the period from **October 2024 to March 2025** has been enclosed.
d). Quantity of effluent discharge to Local Water source from each Source in Cu.m./day	3711m3/day

Noise Pollution Control :-

a) No. of noise monitoring stations & frequency of monitoring	: 2 No.(Fortnightly)
b) Description of locations	1.MANAGER OFFICE : WNGON-1 2. COLONY (GHONSA) : WNGON-2
c) Noise level status prescribed by state pollution control board.	Location | Day | Night Reports of Environmental Monitoring Report for the period from **October 2024 to March 2025** are enclosed.

PART-III
STATUS OF IMPLEMENTATION OF PROVISIONS OF EMP

i)Land Use Status:

S.N.	Particulars	Current Period (October 2024 to March 2025)	Progressive up to 31.03.2025
1.	Area excavated (Ha)	0.54	128.390
2.	Top soil removed (MM^3)	0.167	1.690
3.	OB removed (MM^3) (Hard)	1.857	26.019
4.	OB back filled (MM^3)	1.857	19.472
5.	OB dumped (MM^3) (Hard)	1.857	25.912
6.	Area recovered for reclamation (physical reclamation)	Under process	Under process
7.	Area reclaimed biologically (tree plantation on backfilled area)	Nil	Nil

ii)Production:

Present Capacity/ Production: Previous years production figures are:

Year	Coal Production (Tons)
2020-21	**5,07,900.00**
2021-22	**4,26,100.00**
2022-23	**4,60,235.00**
2023-24	**6,00,000.00**
2024-25	**6,00,000.00**

iii) Afforestation: (Figures in Numbers)

S.N.	Locations	Current Period (October 2024 to March 2025)	Progressive up to 31.03.2025
1.	OB dump & embankments	Nil	10,250
2.	Safety Zones	Nil	1,200
3.	Backfilled Area	Nil	Nil
4.	Other area	Nil	Nil
	TOTAL	Nil	11,450

Number of plantation	11,450
No. of plants per Hectare.	2500
Species planted up to date	Sisum, Nilgiri,Neem

Rehabilitation and Resettlement:-

Sr.No.	Particulars		Status
1.	Total No. of Land oustees	:	47
2.	No. of Employment	:	32
3.	No. of monitory compensation against employment	:	15
4.	Nos. of land oustees under consideration	:	NIL

Organizational set up at Project level :-

Name and designation of the persons :

(1) Shri. Syed Nazimuddin, SAM, Ghonsa Sub Area
(2) Shri. G.D. Khobragade, Mine Manager, Ghonsa OCM
(3) Shri. Shridhar Dhakite, SOE(Civil)/ Nodal Officer(Env.), Ghonsa Sub Area
(4) Shri. Gopendra Kant, Survey Officer, Ghonsa OC Mine.

24/05/25
Survey Officer
Ghonsa OC Mine

25/05/2025
SOE(Civil)/N.O. (Env.)
Ghonsa Sub Area

25/5/25
Mine Manager
Ghonsa OC Mine

26/5
Sub Area Manager
Ghonsa Sub Area

EXPENDITURE STATEMENT(ENVIRONMENT HEAD)

CAPITAL HEAD:-

(Figure in Rs. Lakhs)

Account Head	Current Period FY24-25	Progressive up to 31.03.2025
1)Reclamation (HEMM) partly back filled	-	-
2) Air Pollution Control	-	14.86
3) Water Pollution Control	-	25.87
TOTAL	-	**40.73**

REVENUE HEAD:-

(Figures in Rs. Lakhs)

Account Head	Current Period FY24-25	Progressive up to 31st March 2025
1) Afforestation	-	6.745
2) Monitoring (JVS)	-	-
3) Legal expenses (Water Cess, Environment Statement, CGWA, consent)	61.81	161.61
4) Other (Pollution control measures)	-	82.58
TOTAL	-	250.935

SOE (Civil) /N.O. (Env.)
Ghonsa Sub Area

Sub Area Manager
Ghonsa Sub Area

SIX MONTHLY COMPLIANCE STATUS
OF COMPLIANCE OF ENVIRONMENTAL CLEARANCE CONDITIONS
(For the period October 2024 to March 2025)

Name of the Project: Expansion of Ghonsa OCP (0.60 MTPA)

EC Letter No.: MoEF & CC vide EC Letter No.: J-11015/165/2009-IA.II(M) dated 08th June, 2017

Amended letter no. J/11015/165/2009-IA.II(M) Pt. date 10/01/2018

Sl. No.	Conditions	Compliance Status
	A. Specific Conditions	
i.	The maximum production from the mine at any given time shall not exceed the limit as prescribed in the EC.	Noted, The Maximum production from Ghonsa OCM will not be exceed the limit of 0.60 MTPA as prescribed in the EC.
ii.	The validity of the EC is for the life of the Mine or as specified in the EIA Notification, 2006, whichever is earlier.	Noted.
iii.	The project proponent shall obtain Consent to Establish/Operate under the Air Act, 1981 and the Water Act, 1974 from the State Pollution Control for the Ghonsa OCP of 0.60 MTPA in the mine lease are of 278.683 ha in District Yavatmal (Maharashtra).	Consent to Operate has been granted by MPCB vide Consent Order No. RED/L.S.I (R35)No:-Format1.0/CAC/UAN No. MPCBCONSENT-0000194377/CR/2504002667 dated 24.04.2025 Valid upto 31.03.2026
iv.	Transportation of coal to be carried out through rail network or the covered trucks. Mitigative measures to be undertaken to control dust and other fugitive emissions all along the roads by providing water sprinklers.	Transportation of coal will be carried out by tarpaulin covered trucks. Mitigative measures will be undertaken to control dust and other fugitive emissions all along the roads by providing water sprinklers/water tankers.
v.	Continuous monitoring of occupational safety and other health hazards, and the corrective actions need to be ensured.	Continuous monitoring of occupational safety and other health hazards and the corrective actions will be ensured and complied.
vi.	Controlled blasting should be adopted to control ground vibration and fly rocks.	Controlled blasting is being done in day time only and the mitigative measures for control of ground vibrations and to arrest the fly rocks and boulders are implemented as per the permission given by DGMS. Design of holes and charging of holes are being done as per DGMS permission.
vii.	A progressive afforestation plan shall be implemented covering an area of 134.36 Ha at the end of mining, which includes reclaimed External OB dump area 29.35 ha, Internal OB dump area (80.0 ha) and Green belt (20 Ha) and in township located outside the lease by planting native species	Plantation Details: In 2010-11, 1500 nos. of plants have been planted in 0.60 Ha Area on embankment portion. In 2012-13, 8750 nos. of plants have been planted in 3.50 Ha Area on OB Dump. The plantation has been carried out through

	in consultation with the local DFO/Agriculture Department. The density of the trees shall be around 2500 plants per ha. Massive plantation shall be carried out in open spaces in and around the mine and a 3-tier avenue plantation along the main approach roads to the mine.	Forest Development Corporation of Maharashtra and the density of plantation is always maintained at 2500 plants per ha. A progressive afforestation plan will be implemented at the end of mining.
viii.	An estimated total 29.12 Mm^3 of OB will be generated during the entire life of the mine. Out of which 3.27 Mm^3 of OB will be dumped in one external OB dumps an earmarked area covering 29.35 Ha of land. 25.85 Mm^3 of will be one internal OB dump covering an area of 88.28 ha. The maximum height of internal OB dump will not exceed 30 m above ground level. Maximum slope of the dump shall not exceed 28 degrees. Monitoring and management of reclaimed dump sites shall continue till the vegetation becomes self-sustaining and compliance status shall be submitted to Regional Office on yearly basis.	Aforesaid overburden will dumped on earmarked area only. The maximum height of internal OB dump will not exceed 30 m above ground level. The maximum slope of the dump shall not exceed 28 degrees. Monitoring and management of reclaimed dump sites shall continue till the vegetation becomes self-sustaining and compliance status shall be submitted to MoEF and its Regional Office on yearly basis.
ix.	Of the total quarry area of 135.12 Ha, the backfilled quarry area of 80 ha shall be reclaimed with plantation and a void of 46.84 ha with maximum depth of 75 m shall be converted into a water body in conformity with the post mining land-use plan, which remains an integral part of the approved mining plan and the EIA/EMP submitted to this Ministry.	Of the total quarry area of 135.12 Ha, the backfilled quarry area of 80 ha shall be reclaimed with plantation and a void of 46.84 ha with maximum depth of 75 m shall be converted into a water body in conformity with the post mining land-use plan, which remains an integral part of the approved mining plan and the EIA/EMP submitted to MoEF&CC.
	B. General Conditions	
	a) Mining	
i.	No change in mining technology and scope of working shall be made without prior approval of the Ministry of Environment, Forest and Climate Change. No change in the calendar plan including excavation, quantum of coal and waste should be made.	Noted. No change in mining technology and scope of working will be made without prior approval of MoEF & CC. No change in the calendar plan including excavation, quantum of coal and waste should be made.
ii.	Mining shall be carried out as per the approved mining plan, and also abiding by the relevant laws related to coal mining and the circulars issued by Directorate General Mines Safety (DGMS). A approved	Mining will be carried out as per the approved mining plan, and also abiding by the relevant laws related to coal mining and the circulars issued by Directorate General Mines Safety (DGMS). A approved progressive Mine Closure Plan will

	progressive Mine Closure Plan shall strictly be complied with and submitted.	strictly be complied with.
	b) Land Reclamation	
i.	Digital processing of the entire lease area using remote sensing technique shall be carried out regularly once in three years for monitoring land use pattern and report submitted to Ministry of Environment, Forest and Climate Change its Regional Office.	Monitoring of land use pattern based on Satellite Data carried out by CMPDIL, Ranchi and report is regularly submitted to Regional Office, MoEF & CC Nagpur along with Six Monthly Compliance Report.
ii.	Final mine void depth of 75 m shall be in conformity with the post mining land-use plan, which remains an integral part of the approved mining plan and the EIA/EMP submitted to this Ministry.	Final mine void depth of 75m will be in conformity with the post mining land-use plan, which remains an integral part of the approved mining plan and the EIA/EMP submitted to MoEF & CC.
iii.	The top soil, if any shall temporarily be stored at earmarked site(s) only and it should not be kept unutilized for long. The topsoil shall be used for land reclamation and plantation. The overburden should be vegetated with suitable native species to prevent erosion and surface run off. The entire excavated area shall be backfilled and afforested in line with the approved Mine Closure Plan. Monitoring and Management of rehabilitated areas should continue until the vegetation becomes self-sustaining. Compliance status shall be submitted to the Ministry of Environment, Forest and Climate Change and its Regional Office on six monthly basis.	The top soil will be temporarily stored at earmarked site(s) only and it will not be kept unutilized for long. The topsoil will be used for land reclamation and plantation. The overburden will be vegetated with suitable native species to prevent erosion and surface run off. The entire excavated area will be backfilled and afforested in line with the approved Mine Closure Plan. Monitoring and Management of rehabilitated areas will continue until the vegetation becomes self-sustaining. Compliance status will be submitted to Regional Office, MoEF & CC Nagpur.
iv.	Greenbelt shall be developed all along the mine lease area in a phased manner. The width of the green belt along forest area should not be less than 7.5m and the total area covered by 3 tier green belt shall not be less than 100 ha. A 3-tier green belt comprising of a mix of native species shall be developed all along the major approach roads.	Greenbelt will be developed all along the mine lease area in a phased manner.
	(c) Emissions, Effluents and Waste Disposal	
i.	Transportation of coal by road should be carried out by covered trucks only. Effective measures such as regular water sprinkling shall be carried out in critical areas prone to air pollution and having high levels of PM10 and PM2.5 such as haul	Transportation of coal by road will be carried out by tarpaulin covered trucks only. Regular water sprinkling will be carried out along haul road, loading and unloading point and transfer points. Fugitive dust emissions from all the sources will be controlled regularly. It will be ensured that the

	road, loading and unloading point and transfer points. Fugitive dust emissions from all the sources shall be controlled regularly. It shall be ensured that the Ambient Air Quality parameters conform to the norms prescribed by the Central/State Pollution Control Board in this regard.	Ambient Air Quality parameters conform to the norms prescribed by the CPCB/MPCB.
ii.	Vehicular emissions shall be kept under control and regularly monitored. Project should obtain 'PUC' certificate for all the vehicles from authorized pollution testing centres.	Vehicular emissions will be kept under control and regularly monitored. Project will obtain 'PUC' certificate for all the vehicles from authorized pollution testing centres.
iii.	Adequate ambient air quality monitoring stations shall be established in the core zone as well as in the buffer zone for monitoring of pollutants, namely PM_{10}, $PM_{2.5}$, SO_2 and NO_x. Location of the stations shall be decided based on the meteorological data, topographical features and environmentally and ecologically sensitive targets in consultation with the State Pollution Control Board. Monitoring of heavy metals such as Hg, As, Ni, Cd, Cr, etc carried out at least once in six months.	Following four ambient air quality monitoring stations have been established in the core zone and buffer zone for PM_{10}, $PM_{2.5}$ SO_2 and NO_x monitoring: 1. Ghonsa village 2. Kumbharkhani Guest house/colony 3. SAM Office/ Canteen 4. Project Manager Office, Ghonsa Monitoring of heavy metals such as As, Pb, Ni, Cr & Cd is carried out once in six months. Reports of Environmental monitoring from **October 2024 to March 2025** has been enclosed.
iv.	Crusher/feeder and breaker material transfer points should invariably be provided with dust suppression system. Belt-conveyors should be fully covered to avoid air borne dust. Drills shall be wet operated or fitted with dust extractors	Crusher/feeder and breaker material transfer points will be invariably provided with dust suppression system. Drills will be fitted with dust extractors
v.	The project proponent shall not alter the major channels around the site. Appropriate embankment should be provided along the side of the river/nallah flowing near or adjacent to the mine. The embankment constructed along the river/nallah boundary should be of suitable dimensions and critical patches should be strengthened by stone pitching on the river front side and stabilised with plantation so as to withstand the peak water .flow and prevent mine inundation.	The major channels around the site will not be altered. Embankment of length 1.40 Km, width 30m and height 7-10m has been constructed along Vidharbha river as per permission given by DGMS. To arrest embankment erosion toe wall of stone masonry has been constructed as well as natural grass and plantation has been developed to stabilized embankment.
vi.	Rainwater harvesting shall be implemented for conservation and augmentation of ground water resources in the area in consultation with Central Ground Water Board.	Rain water harvesting measures have already been taken with due consultation with the concerned village Panchayat through de-silting/ deepening of existing pond in the following villages at a total cost of Rs. 12.48 lakhs:- (i) Sakhara Village; (ii) Rasa Village;

<table>
<tr><td></td><td></td><td>(iii) Sukanegaon Village.

In July 2015, deepening of pond at Rasa and Kumbharkhnai village has been done for ground water recharge.

At Kumbharkhani Village Pond:
Deepening size: (65m x 40.m x 1.08m)
Expenditure: 4.21 Lakh

At. Rasa Village Pond:
Deepening size: a. (50m x 50m x 0.60)
b.(40m x 20m x 0.94m)
c.(40m x 15m x 0.94m)
Expenditure: 4.47Lakh
The quantum of water will be stored 2700KL at Rasa & 2800KL Kumbharkhani village.</td></tr>
<tr><td>vii.</td><td>Catch drains and siltation ponds of appropriate size shall be constructed around the mine working, coal heaps and OB dumps to prevent run off of water and flow of sediments directly into the river and other water bodies. The water so collected should be utilized for watering the mine area, roads, green belt development etc. The drains shall be regularly desilted particularly after monsoon and maintained properly. Sump capacity should provide adequate retention period to allow proper settling of silt material. To check run off and siltation, retaining wall of adequate dimension to be constructed at the toe of OB dumps and OB benches, as applicable, based on rainfall data.</td><td>Catch drains of size 2.50m x 2.00m for a length of 2.00 Km is constructed around the mine. Two sumps of capacity 10.50 Million Gallon & capacity of 0.45 Million Gallon have been provided inside the mine to arrest silt and sediments of soil and OB. Garland drain of length 3.4 Km has been provided. Cleaning and desilting of garland drain is regularly being done.
Rainfall details at Ghonsa OCM:
<table>
<tr><th>Year</th><th>Total Rainfall (mm)</th><th>Date max. Rainfall (mm)</th><th>Max Rainfall</th></tr>
<tr><td>2013</td><td>1243</td><td>12/07/2013</td><td>96</td></tr>
<tr><td>2014</td><td>644.5</td><td>07/09/2014</td><td>108</td></tr>
<tr><td>2015</td><td>596</td><td>16/09/2015</td><td>172</td></tr>
<tr><td>2016</td><td>786</td><td>08/07/2016</td><td>64</td></tr>
<tr><td>2017</td><td>484</td><td>12/09/2017</td><td>64</td></tr>
<tr><td>2018</td><td>911</td><td>09/07/2018</td><td>113</td></tr>
<tr><td>2019</td><td>828</td><td>29/07/2019</td><td>071</td></tr>
<tr><td>2020</td><td>1158</td><td>22/07/2020</td><td>114</td></tr>
<tr><td>2021</td><td>1168</td><td>10/07/2021</td><td>98</td></tr>
<tr><td>2022</td><td>2110</td><td>11/07/2022</td><td>137</td></tr>
<tr><td>2023</td><td>1034</td><td>04/07/2023</td><td>66</td></tr>
<tr><td>2024</td><td>875</td><td>20/07/2024</td><td>62</td></tr>
</table>
Toe wall of size 82m x 1.8m x 0.6m has been constructed for arresting the silt against embankment to guide catchment water to settle.</td></tr>
<tr><td>viii.</td><td>Industrial waste water (CHP, workshop and waste water from the mine) should be properly collected and treated so as to conform to the standards prescribed under the Environment (Protection) Act, 1986 and the Rules made there under, and as amended from time to time. Oil and grease trap should be installed before discharge of workshop effluents.</td><td>Agreed.</td></tr>
</table>

	(d) Noise & Vibration Control	
i.	Adequate measures shall be taken for control of noise levels below 85 dBA in the work environment. Workers engaged in blasting and drilling operations, operation of HEMM, etc shall be provided with ear plugs/muffs.	Proper maintenance of HEMM will be done and plantation has been done to control noise levels below 85 dBA. Workers engaged in blasting and drilling operations will be provided with ear plugs/muffs.
ii.	Controlled blasting techniques should be practiced with use of delay detonators to mitigate ground vibrations and fly rocks.	Controlled blasting is being done with delay detonator in day time only. The mitigative measures for control of ground vibrations and to arrest the fly rocks and boulders are implemented as per the permission given by DGMS. Design of holes and charging of holes are being done as per DGMS permission.
	(e) Occupational Health & Safety	
i.	Besides carrying out regular periodic health check-up of their workers, 20% of the workers identified from workforce engaged in active mining operations shall be subjected to health check-up for occupational diseases and hearing impairment, if any, through an specialised agency /institution within the District/State and the results reported to this Ministry and to DGMS.	Periodical medical examinations of all workers are conducted in every Three years. If any occupational diseases and hearing impairment found, action is taken as per guidelines and complied. Medical examination of 10% of the workers identified from workforce engaged in active mining operations will be subjected to health check-up through specialized agency within the district (Govt. hospital).
ii.	Personnel working in dusty areas should wear protective respiratory devices and they should also be provided with adequate training and information on safety and health aspects. Supervisory staff shall be held responsible for ensuring compulsory wearing of dust mask.	Personnel working in dusty areas are given dust mask and training and information on safety and health aspects. Training and information on safety and health aspects is provided at GVTC.
iii.	In case of outsourcing of work through MDO, the project proponent shall ensure the strict compliance enforcement of the above conditions.	Strict compliance of enforcement of the above conditions will be ensured.
	(f) Biodiversity	
i.	The project proponent shall take all precautionary measures during mining operation for conservation and protection of endangered fauna, if any, spotted in the study area. Action plan for conservation of flora and fauna shall be prepared and implemented in consultation with the State Forest and Wildlife Department. A copy of action plan shall be submitted to the Ministry of Environment, Forest and Climate Change and its Regional Office.	All precautionary measures will be taken during mining operation for conservation and protection of endangered fauna, if any, spotted in the study area. Action plan for conservation of flora and fauna will be prepared and implemented in consultation with the State Forest and Wildlife Department.

	(g) Implementation of Action Plan as Per Public Hearing & CSR Activities	
i.	Implementation of Action Plan on the issues raised during the Public Hearing shall be ensured. The Project Proponent shall complete all the tasks as per the Action Plan submitted with budgetary provisions during the Public Hearing. Land oustees should be compensated as per the norms laid out R&R Policy of the Company or the National R&R Policy or R&R Policy of the State Government, whichever is higher.	Noted and will be complied.
ii.	The Board of every company, shall ensure that the company spends, in every financial year, at least two per cent, of the average net profits of the company made during the three immediately preceding financial years, in pursuance of its Corporate Social Responsibility Policy under Section 135 of the Companies Act, 2013, for the Socio Economic Development of the neighborhood.	As per CSR policy of Coal India Limited Rs. 2/tonne of coal produced or 2% of the average net profits of the company made during the three immediately preceding financial years whichever is more is spent on Corporate Social Responsibility works.
	(h) Corporate Environment Responsibility	
i.	The Company should have a well laid down Environment Policy approved by the Board of Directors.	Coal India Limited's Corporate Environment Policy approved by the board of director exists.
ii.	To have proper checks and balances, the Company should have a well laid down system of reporting of non-compliances/violations of environmental norms to the Board of Directors of the Company and/or shareholders or stakeholders at large.	To have proper checks and balances, the WCL have a well laid down system of reporting of non-compliances/violations of environmental norms to the Board of Directors of the WCL.
iii.	A separate environmental management cell with suitable qualified personnel should be set-up under the control of a Senior Executive, who will report directly to the Head of the Organization.	At unit level Environmental Management Cell is headed by Chief Manager (Civil) / Nodal Officer (Environment) who reports to Sub Area Manager. At Area level Environmental Management Cell is headed by Area Nodal Officer (Env.) and assisted by Asst. Manager(Env.) who report to Area General Manager. At company level Environmental Management Cell is headed by General Manager (Environment)/HOD assisted by qualified and experienced environmental engineers who directly report to the Director (Project & Planning), WCL.
iv.	The funds earmarked for environmental protection measures should not be diverted for other purpose. Year wise expenditure should be reported to the Ministry and its Regional Office.	Funds earmarked for Environment protection measures is not diverted for other purpose. Year wise expenditure under Environment Head is regularly report to Regional Office, MoEF & CC Nagpur along with Six Monthly EC Compliance Report.

	(i) Statutory Obligations	
i.	Environmental clearance is granted subject to final outcome of Hon'ble Supreme Court of India, Hon'ble High Court, NGT and any other Court of Law, if any, as may be applicable to this project.	Noted.
ii.	This Environmental Clearance is subject to obtaining requisite NBWL Clearance from the Standing Committee of National Board for Wildlife, if any, as applicable for this Mining project.	Not applicable for this project
iii.	The project proponent shall obtain Consent to Establish and Consent to Operate from the concerned State Pollution Control Board prior to increase in capacity of washery and effectively implement all the conditions stipulated therein.Consent to Operate has been granted by MPCB vide Consent Order No. RED/L.S.I (R35)No:-Format1.0/CAC/UAN No.MPCBCONSENT-0000107029/CR/2203000019 dated 01.03.2022. Valid upto 31.03.2023	Consent to Operate has been granted by MPCB vide Consent Order No. RED/L.S.I (R35)No:-Format1.0/CAC/UAN No. MPCBCONSENT-0000194377/CR/2504002667 dated 24.04.2025 Valid upto 31.03.2026
iv.	The project proponent shall obtain necessary prior permission of the competent authorities for drawl of requisite quantity of water (surface water and ground water) for the project.	Noted
v.	Project Proponent shall obtain the necessary prior permission from the Central Ground Water Authority (CGWA) for drawl of water (surface and ground water).	Noted
	(j) Monitoring of Project	
i.	Regular monitoring of ground water level and quality shall be carried out in and around the mine lease by establishing a network of existing wells and constructing new piezometers during the mining operation. The monitoring shall be carried out four times in a year pre- monsoon (April-May), monsoon (August),. post-monsoon (November) and winter (January) and the data thus collected may be sent regularly to Ministry of Environment, Forest and Climate Change and its Regional Office, Central Ground Water Authority and Regional Director, Central Ground Water Board.	Regular monitoring of ground water level and quality is being carried out four times in a year in pre-monsoon (May), monsoon (August), post-monsoon (November) and winter (January) and for quality in May. Report on Monitoring Ground Water Level and Quality Analysis is being sent regularly to MoEF & CC Delhi, RO MoEF & CC Nagpur, CGWA Delhi, Regional Director CGWB Nagpur and RO MPCB Chandrapur
ii.	The project proponent shall submit six monthly reports on the status of the	Six monthly compliance reports are being sent regularly to Regional Office, MoEF&CC, Nagpur

	implementation of the stipulated environmental safeguards to the Ministry of Environment, Forest and Climate Change, its Regional Office, Central Pollution Control Board and State Pollution Control Board.	and Regional Office, MPCB, Chandrapur.
iii.	The Regional Office of this Ministry shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data / information / monitoring reports.	All necessary co-operations will be extended to Regional Office, Nagpur.
iv.	The activities pertaining to development of green belt / horticulture shall be reported to concerned Regional Office of MoEF&CC on six monthly basis from the date of commencement of mining operations.	The activities pertaining to development of green belt / horticulture will be reported to Regional Office, MoEF & CC, Nagpur on six monthly basis.
v.	For half yearly monitoring reports, the data should be monitored for the period of April to September and October to March of the financial years and submitted to the concerned authorities within 2 months of the completion of periodicity of monitoring.	Agreed.
	(k) Miscellaneous	
i.	A copy of clearance letter will be marked to concerned Panchayat /local NGO, if any, from whom suggestion / representation has been received while processing the proposal.	A copy of EC Letter has been given to Gram Panchayat Ghonsa village on 10th June, 2017.
ii.	An electronic copy of the EC letter shall be marked to the concerned State Pollution Control Board, Regional Office, District Industry Sector and Collector's Office/Tehsildar Office for information in public domain within 30 days.	An electronic copy of the EC Letter has been emailed to Maharashtra Pollution Control Board, Regional Officer Chandapur, Collector Yavatmal, SDO Wani on 10th June, 2017.
iii.	The EC letter shall be uploaded on the company's website. The compliance status of the stipulated EC conditions shall also be uploaded by the project authorities on their website and updated at least once every six months so as to bring the same in public domain. The monitoring data of environmental quality parameter (air, water, noise and soil) and critical pollutant such as PM10, PM25, SO2 and NO (ambient) and critical sectoral parameters shall also be displayed at the entrance of the project premises and mine office and in corporate office and on company's website.	Environmental Clearance letter has been uploaded on WCL's website (www.westerncoal.gov.in) Link for EC letter: https://westerncoal.in/index1.php/StaticPage/154 Six Monthly Compliance Status of EC Conditions and monitoring data of environmental quality parameter (air, water, noise) is regularly uploaded on WCL's website.

iv.	The project authorities should advertise at least in two local newspapers widely circulated, one of which shall be in the vernacular language of the locality concerned, within 7 days of the issue of the clearance letter informing that the project has been accorded environmental clearance and a copy of the clearance letter is available with the State Pollution Control Board and also at web site of the Ministry of Environment, Forest and Climate Change at www.environmentclearance.nic.in and a copy of the same should be forwarded to the Regional Office.	A public notice regarding this information has been advertised in two local news papers: 1. तरुण भारत, आपलं यवतमाळ dated 15th June, 2017 on Page no. 13, Marathi Daily news paper 2. The Hitavada dated 15th June, 2017 on Page no. 3. English Daily news paper
v.	The Environmental Statement for each financial year ending 31 March in Form-V is mandated to be submitted by the PP for the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be uploaded on the Company's website along with the status of compliance of EC conditions and shall be sent to the respective Regional Offices of the MoEF&CC by e-mail.	Environmental Statement for each financial year ending 31st March in Form - V is submitted to Maharashtra Pollution Control Board. Environmental Statement-Form V for year **2023-24** has been submitted on online portal of MPCB.
5.	The project proponent shall abide by all the commitments and recommendations made in the EIA/EMP report and also that during their presentation to the EAC. The commitment made by the project proponent to the issue raised during Public Hearing shall be implemented by the proponent.	Noted.
6.	The project proponent shall obtain all necessary clearances/approvals that may be required before the start of the project. The Ministry or any other competent authority may stipulate any further condition for environmental protection.	Noted.
7.	The PP shall set up an Environment Audit cell with responsibility and accountability to ensure implementation of all the EC Conditions.	Environment Audit Cell has been setup with responsibility & accountability to ensure compliance of all the Environment Clearance conditions.
8.	Concealing factual data or submission of false/fabricated data and failure to comply with any of the conditions mentioned above may result in withdrawal of this EC and attract action under the provisions of Environment (Protection) Act, 1986.	Noted.
9.	The above conditions will be enforced inter-alia, under the provisions of the Water (Prevention & Control of Pollution) Act,	Noted.

	1974, the Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986 and the Public Liability Insurance Act, 1991 along with their amendments and Rules and any other orders passed by the Hon'ble Supreme Court of India/High Courts and any other Court of Law relating to the subject matter. The PP shall ensure to undertake and provide for the costs incurred for taking up remedial measures in case of soil contamination, contamination of groundwater and surface water, and occupational and other diseases due to the mining operations.	
10.	Any appeal against this EC shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.	Noted.
11.	This EC supersedes the earlier EC granted vide letter No.J-11015/165/2009-IA.II (M) dated 8th December, 2014 for expansion in production capacity from 0.45 MTPA to 0.60 MTPA in ML area of 128.79 ha.	Noted.

24/05/25
Survey Officer
Ghonsa OC Mine

25/05/2025
Nodal Officer (Env.)
Ghonsa Sub Area

24/5/25
Mine Manager
Ghonsa OC Mine

24/5
Sub Area Manager
Ghonsa Sub Area



STRICTLY RESTRICTED
FOR COMPANY USE ONLY
The information given in this report is not to be communicated either directly or indirectly to the press or to any person not holding an official position in the CIL / Government

ENVIRONMENTAL MONITORING REPORT

GHONSA OC

WANI NORTH AREA

WESTERN COALFIELDS LTD.

JOB NO. 4094423068

OCTOBER 2024

Environment Laboratory
NABL Accredited vide Cert. No. TC-7102
CMPDI
REGIONAL INSTITUTE-IV, KASTURBA NAGAR,
JARIPATKA, NAGPUR, PIN – 440 014

AN ISO 9001:2015 COMPANY

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	

TEST REPORT NO.	RIN/TR/OCT-24/23	DATE OF ISSUE		25.11.2024
NAME OF CUSTOMER	GM(ENV.), WCL(HQ), NAGPUR			
TEST REQUIRED	SPM: IS 5182 Part-4:1999(RA 2019), PM-10: IS-5182 Part 23:2006(RA 2017), PM2.5: USEPA Quality Assurance guidance document volume-II (part-II)-2.12:2016, NO2: IS 5182 Part-06:2006(2017), SO2:IS 5182 Part-2:2001(RA 2017)			
SAMPLE DESCRIPTION	AIR SAMPLE		SAMPLING PLAN :	LQR 47
SAMPLING METHOD : LSOP 4	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:			16-10-24 TO 15-11-24

PROJECT MANAGER OFFICE		WNGOA1					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	5	2	6	10	
07.10.2024	08.10.2024	314	225	36	16	13	CLEAR/MODERATE BREEZE
20.10.2024	21.10.2024	355	263	49	18	14	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

SAM OFFICE/ CANTEEN		WNKUA2					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	5	2	6	10	
07.10.2024	08.10.2024	289	193	33	14	10	CLEAR/MODERATE BREEZE
20.10.2024	21.10.2024	309	201	45	16	12	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

GHONSA VILLAGE		WNGOA3				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	2	6	10	
05.10.2024	06.10.2024	87	26	10	BDL	CLEAR/LIGHT BREEZE
06.10.2024	07.10.2024	70	19	8	BDL	CLOUDY/CALM
12.10.2024	13.10.2024	95	30	9	BDL	CLEAR/MODERATE BREEZE
13.10.2024	14.10.2024	69	18	8	BDL	CLOUDY/CALM
18.10.2024	19.10.2024	82	29	10	BDL	CLEAR/LIGHT BREEZE
19.10.2024	20.10.2024	77	25	10	BDL	CLOUDY / CALM
25.10.2024	26.10.2024	89	32	8	BDL	CLEAR/MODERATE BREEZE
26.10.2024	27.10.2024	65	18	7	BDL	CLEAR/LIGHT BREEZE
30.10.2024	31.10.2024	70	20	10	BDL	CLEAR/MODERATE BREEZE
31.10.2024	01.11.2024	80	24	10	BDL	CLEAR/LIGHT BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

GUEST HOUSE/ COLONY		WNGOA4				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	2	6	10	
05.10.2024	06.10.2024	92	34	10	BDL	CLEAR/LIGHT BREEZE
06.10.2024	07.10.2024	76	22	8	BDL	CLOUDY/CALM
12.10.2024	13.10.2024	93	30	9	BDL	CLEAR/MODERATE BREEZE
13.10.2024	14.10.2024	67	17	8	BDL	CLOUDY/CALM
18.10.2024	19.10.2024	74	24	9	BDL	CLEAR/LIGHT BREEZE
19.10.2024	20.10.2024	83	30	10	BDL	CLOUDY / CALM
25.10.2024	26.10.2024	79	28	9	BDL	CLEAR/MODERATE BREEZE
26.10.2024	27.10.2024	68	20	8	BDL	CLEAR/LIGHT BREEZE
30.10.2024	31.10.2024	74	24	8	BDL	CLEAR/MODERATE BREEZE
31.10.2024	01.11.2024	72	26	10	BDL	CLEAR/LIGHT BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	

SAMPLE DESCRIPTION	Water sample			
Test Required	pH: IS 3025 -Part 11:1983(RA 2017),TSS: IS 3025-Part 17:1984(RA 2017),COD: APHA (23rd Edition) 5220 C :2017,O &G: IS 3025-Part 39:1991(RA 2019) & BOD: IS 3025 (Part 44): 1993 (RA 2019)			
SAMPLING METHOD	LSOP 5	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-10-24 TO 15-11-24

MINE WATER DISCHARGE:	WNGOW1			
DATE OF SAMPLE COLLECTION	ANALYSIS RESULTS			
	pH	TSS (in mg/l)	COD(in mg/l)	O & G(in mg/l)
DETECTION LIMIT	2	10	4	2
15.10.2024	8.12	28	40	BDL
26.10.2024	8.03	22	36	BDL
STANDARDS FOR COAL MINE, GSR 742E, dt. 25/09/2000	5.5 - 9.0	100	250	10

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	

NOISE LEVEL MONITORING DATA

SAMPLE DESCRIPTION	NOISE SAMPLE
Test Required	CPCB PRDECOCOL FOR AMBIENT NOISE MEASUREMENT, OCT-2015
SAMPLING METHOD	LSOP 6

MANAGER OFFICE:	WNGON1		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
OCT'24	11.10.2024	57.7	56.4
OCT'24	26.10.2024	55.4	52.6
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**75**	**70**

COLONY (GHONSA)	WNGON2		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
OCT'24	11.10.2024	44.1	43.3
OCT'24	26.10.2024	44.3	41.4
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**55**	**45**

Amol Kamble
Reviewed by

Deepanshu Sahu
Authorised by

1. This report cannot be reproduced in part or full without written of the management.
2. Laboratory activities are performed at the Laboratory permanent facility that is ground floor, Environment Lab, CMPDI RI-IV, Nagpur.
3. This report refers to the values related to the items tested.

********** End of report **********



STRICTLY RESTRICTED
FOR COMPANY USE ONLY
The information given in this report is not to be communicated either directly or indirectly to the press or to any person not holding an official position in the CIL / Government

ENVIRONMENTAL MONITORING REPORT

GHONSA OC

WANI NORTH AREA

WESTERN COALFIELDS LTD.

JOB NO. 4094423068

NOVEMBER 2024

Environment Laboratory
NABL Accredited vide Cert. No. TC-7102
CMPDI
REGIONAL INSTITUTE-IV, KASTURBA NAGAR,
JARIPATKA, NAGPUR, PIN – 440 014

AN ISO 9001:2015 COMPANY

Environment Laboratory CMPDI RI-IV, NAGPUR	**Test Report**	

TEST REPORT NO.	RIN/TR/NOV-24/23	DATE OF ISSUE	24.12.2024
NAME OF CUSTOMER	GM(ENV.), WCL(HQ), NAGPUR		
TEST REQUIRED	SPM: IS 5182 Part-4:1999(RA 2019), PM-10: IS-5182 Part 23:2006(RA 2017), PM2.5: USEPA Quality Assurance guidance document volume-II (part-II)-2.12:2016, NO2: IS 5182 Part-06:2006(2017), SO2:IS 5182 Part-2:2001(RA 2017)		
SAMPLE DESCRIPTION	AIR SAMPLE	SAMPLING PLAN :	LQR 47
SAMPLING METHOD : LSOP 4	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-11-24 TO 15-12-24

PROJECT MANAGER OFFICE | WNGOA1

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	**PM_{10}**	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	5	2	6	10	
08.11.2024	09.11.2024	287	192	43	16	13	CLEAR/MODERATE BREEZE
22.11.2024	23.11.2024	299	212	49	17	15	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

SAM OFFICE/ CANTEEN | WNKUA2

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	**PM_{10}**	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	5	2	6	10	
08.11.2024	09.11.2024	255	174	40	14	10	CLEAR/MODERATE BREEZE
22.11.2024	23.11.2024	272	192	47	16	13	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

GHONSA VILLAGE | WNGOA3

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	2	6	10	
06.11.2024	07.11.2024	82	29	10	BDL	CLEAR/LIGHT BREEZE
07.11.2024	08.11.2024	71	25	8	BDL	CLEAR/LIGHT BREEZE
13.11.2024	14.11.2024	88	27	9	BDL	CLEAR/LIGHT BREEZE
14.11.2024	15.11.2024	67	19	7	BDL	CLEAR/LIGHT BREEZE
20.11.2024	21.11.2024	78	25	9	BDL	CLEAR/LIGHT BREEZE
21.11.2024	22.11.2024	69	20	8	BDL	CLEAR/CALM
27.11.2024	28.11.2024	86	29	10	BDL	CLEAR/MODERATE BREEZE
28.11.2024	29.11.2024	80	24	9	BDL	CLEAR/LIGHT BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

GUEST HOUSE/ COLONY | WNGOA4

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	2	6	10	
06.11.2024	07.11.2024	88	28	10	BDL	CLEAR/LIGHT BREEZE
07.11.2024	08.11.2024	76	22	9	BDL	CLEAR/LIGHT BREEZE
13.11.2024	14.11.2024	80	26	10	BDL	CLEAR/LIGHT BREEZE
14.11.2024	15.11.2024	79	20	10	BDL	CLEAR/LIGHT BREEZE
20.11.2024	21.11.2024	82	28	9	BDL	CLEAR/LIGHT BREEZE
21.11.2024	22.11.2024	70	23	8	BDL	CLEAR/CALM
27.11.2024	28.11.2024	86	27	8	BDL	CLEAR/MODERATE BREEZE
28.11.2024	29.11.2024	77	24	9	BDL	CLEAR/LIGHT BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	

SAMPLE DESCRIPTION	Water sample			
Test Required	pH: IS 3025 -Part 11:1983(RA 2017),TSS: IS 3025-Part 17:1984(RA 2017),COD: APHA (23rd Edition) 5220 C :2017,O &G: IS 3025-Part 39:1991(RA 2019) & BOD: IS 3025 (Part 44): 1993 (RA 2019)			
SAMPLING METHOD	LSOP 5	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-11-24 TO 15-12-24

MINE WATER DISCHARGE:	WNGOW1			
DATE OF SAMPLE COLLECTION	ANALYSIS RESULTS			
	pH	TSS (in mg/l)	COD(in mg/l)	O & G(in mg/l)
DETECTION LIMIT	2	10	4	2
12.11.2024	7.92	22	40	BDL
28.11.2024	7.90	26	36	BDL
STANDARDS FOR COAL MINE, GSR 742E, dt. 25/09/2000	**5.5 - 9.0**	**100**	**250**	**10**

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	

NOISE LEVEL MONITORING DATA

SAMPLE DESCRIPTION	NOISE SAMPLE
Test Required	CPCB PROTOCOL FOR AMBIENT NOISE MEASUREMENT, NOV-2015
SAMPLING METHOD	LSOP 6

MANAGER OFFICE:	WNGON1		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
NOV'24	10.11.2024	56.7	53.5
NOV'24	26.11.2024	54.6	52.2
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**75**	**70**

COLONY (GHONSA)	WNGON2		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
NOV'24	10.11.2024	44.4	42.2
NOV'24	26.11.2024	44.1	42.3
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**55**	**45**

Amol Kamble
Reviewed by

Deepanshu Sahu
Authorised by

1. This report cannot be reproduced in part or full without written of the management.
2. Laboratory activities are performed at the Laboratory permanent facility that is ground floor, Environment Lab, CMPDI RI-IV, Nagpur.
3. This report refers to the values related to the items tested.

********** End of report **********

STRICTLY RESTRICTED
FOR COMPANY USE ONLY
The information given in this report is not to be communicated either directly or indirectly to the press or to any person not holding an official position in the CIL / Government

ENVIRONMENTAL MONITORING REPORT

GHONSA OC

WANI NORTH AREA

WESTERN COALFIELDS LTD.

JOB NO. 4094423068

DECEMBER 2024

Environment Laboratory
NABL Accredited vide Cert. No. TC-7102
CMPDI
REGIONAL INSTITUTE-IV, KASTURBA NAGAR,
JARIPATKA, NAGPUR, PIN – 440 014

AN ISO 9001:2015 COMPANY

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

TEST REPORT NO.	RIN/TR/DEC-24/23	DATE OF ISSUE	28-01-2025
NAME OF CUSTOMER	GM(ENV.), WCL(HQ), NAGPUR		
TEST REQUIRED	SPM: IS 5182 Part-4:1999(RA 2019), PM-10: IS-5182 Part 23:2006(RA 2017), PM2.5: USEPA Quality Assurance guidance document volume-II (part-II)-2.12:2016, NO2: IS 5182 Part-06:2006(2017), SO2:IS 5182 Part-2:2001(RA 2017)		
SAMPLE DESCRIPTION	AIR SAMPLE	SAMPLING PLAN :	LQR 47
SAMPLING METHOD : LSOP 4	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-12-24 TO 15-01-25

PROJECT MANAGER OFFICE		WNGOA1					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	5	2	6	10	
07-12-2024	08-12-2024	281	192	48	16	13	CLEAR/MODERATE BREEZE
21-12-2024	22-12-2024	321	214	55	19	15	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

SAM OFFICE/ CANTEEN		WNKUA2					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	5	2	6	10	
07-12-2024	08-12-2024	263	187	41	13	10	CLEAR/MODERATE BREEZE
21-12-2024	22-12-2024	289	197	49	17	12	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

GHONSA VILLAGE		WNGOA3				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	2	6	10	
05-12-2024	06-12-2024	65	18	8	BDL	CLEAR/LIGHT BREEZE
06-12-2002	07-12-2002	78	22	9	BDL	CLEAR/CALM
12-12-2024	13-12-2024	81	27	8	BDL	CLEAR/MODERATE BREEZE
13-12-2024	14-12-2024	69	19	8	BDL	CLEAR/LIGHT BREEZE
19-12-2024	20-12-2024	85	28	9	BDL	CLEAR/LIGHT BREEZE
20-12-2024	21-12-2024	66	17	8	BDL	CLEAR/CALM
26-12-2024	27-12-2024	95	31	10	BDL	CLEAR/MODERATE BREEZE
27-12-2024	28-12-2024	81	25	10	BDL	CLEAR/LIGHT BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

GUEST HOUSE/ COLONY		WNGOA4				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	2	6	10	
05-12-2024	06-12-2024	75	24	9	BDL	CLEAR/LIGHT BREEZE
06-12-2002	07-12-2002	86	32	11	BDL	CLEAR/CALM
12-12-2024	13-12-2024	69	19	9	BDL	CLEAR/MODERATE BREEZE
13-12-2024	14-12-2024	80	27	10	BDL	CLEAR/LIGHT BREEZE
19-12-2024	20-12-2024	77	25	8	BDL	CLEAR/LIGHT BREEZE
20-12-2024	21-12-2024	62	20	7	BDL	CLEAR/CALM
26-12-2024	27-12-2024	89	29	10	BDL	CLEAR/MODERATE BREEZE
27-12-2024	28-12-2024	70	22	9	BDL	CLEAR/LIGHT BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

SAMPLE DESCRIPTION	Water sample			
Test Required	pH: IS 3025 -Part 11:1983(RA 2017),TSS: IS 3025-Part 17:1984(RA 2017),COD: APHA (23rd Edition) 5220 C :2017,O &G: IS 3025-Part 39:1991(RA 2019) & BOD: IS 3025 (Part 44): 1993 (RA 2019)			
SAMPLING METHOD	LSOP 5	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-12-24 TO 15-01-25

MINE WATER DISCHARGE:	WNGOW1			
DATE OF SAMPLE COLLECTION	**ANALYSIS RESULTS**			
	pH	TSS (in mg/l)	COD(in mg/l)	O & G(in mg/l)
DETECTION LIMIT	2	10	4	2
13-12-2024	7.59	20	40	BDL
26-12-2024	8.16	24	48	BDL
STANDARDS FOR COAL MINE, GSR 742E, dt. 25/09/2000	**5.5 - 9.0**	**100**	**250**	**10**

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

NOISE LEVEL MONITORING DATA

SAMPLE DESCRIPTION	NOISE SAMPLE
Test Required	CPCB PRDECOCOL FOR AMBIENT NOISE MEASUREMENT, DEC-2015
SAMPLING METHOD	LSOP 6

MANAGER OFFICE:	WNGON1		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
DEC'24	07-12-2024	56.2	52.7
DEC'24	26-12-2024	55.2	53.1
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**75**	**70**

COLONY (GHONSA)	WNGON2		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
DEC'24	07-12-2024	44.1	42.2
DEC'24	26-12-2024	44.2	41.6
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**55**	**45**



Amol Kamble
Reviewed by



M. Rabbani
Authorised by

1. This report cannot be reproduced in part or full without written of the management.
2. Laboratory activities are performed at the Laboratory permanent facility that is ground floor, Environment Lab, CMPDI RI-IV, Nagpur.
3. This report refers to the values related to the items tested.

********** End of report **********



STRICTLY RESTRICTED
FOR COMPANY USE ONLY
The information given in this report is not to be communicated either directly or indirectly to the press or to any person not holding an official position in the CIL / Government

ENVIRONMENTAL MONITORING REPORT

GHONSA OC

WANI NORTH AREA

WESTERN COALFIELDS LTD.

JOB NO. 4094423068

JANUARY 2025

Environment Laboratory
NABL Accredited vide Cert. No. TC-7102
CMPDI
REGIONAL INSTITUTE-IV, KASTURBA NAGAR,
JARIPATKA, NAGPUR, PIN – 440 014

AN ISO 9001:2015 COMPANY

Environment Laboratory CMPDI RI-IV, NAGPUR	**Test Report**	TC-7102

TEST REPORT NO.	RIN/TR/JAN-25/23	DATE OF ISSUE		25-02-2025
NAME OF CUSTOMER	GM(ENV.), WCL(HQ), NAGPUR			
TEST REQUIRED	SPM: IS 5182 Part-4:1999(RA 2019), PM-10: IS-5182 Part 23:2006(RA 2017), PM2.5: USEPA Quality Assurance guidance document volume-II (part-II)-2.12:2016, NO2: IS 5182 Part-06:2006(2017), SO2:IS 5182 Part-2:2001(RA 2017)			
SAMPLE DESCRIPTION	AIR SAMPLE		SAMPLING PLAN :	LQR 47
SAMPLING METHOD : LSOP 4	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:			16-01-25 TO 15-02-25

PROJECT MANAGER OFFICE		**WNGOA1**					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	**PM_{10}**	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	5	2	6	10	
06-01-2025	07-01-2025	312	234	52	18	15	CLEAR/MODERATE BREEZE
20-01-2025	21-01-2025	325	248	55	20	16	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

SAM OFFICE/ CANTEEN		**WNKUA2**					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	**PM_{10}**	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	5	2	6	10	
06-01-2025	07-01-2025	271	175	45	15	12	CLEAR/MODERATE BREEZE
20-01-2025	21-01-2025	296	202	52	18	14	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

GHONSA VILLAGE		**WNGOA3**				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	2	6	10	
03-01-2025	04-01-2025	71	21	9	BDL	CLEAR/LIGHT BREEZE
04-01-2025	05-01-2025	66	18	8	BDL	CLEAR/CALM
10-01-2025	11-01-2025	85	26	9	BDL	CLEAR/MODERATE BREEZE
11-01-2025	12-01-2025	70	24	10	BDL	CLOUDY/MODERATE BREEZE
17-01-2025	18-01-2025	76	29	10	BDL	CLEAR/LIGHT BREEZE
18-01-2025	19-01-2025	63	20	9	BDL	CLEAR/CALM
24-01-2025	25-01-2025	88	23	8	BDL	CLEAR/MODERATE BREEZE
25-01-2025	26-01-2025	72	21	9	BDL	CLOUDY/MODERATE BREEZE
29-01-2025	30-01-2025	81	27	10	BDL	CLEAR/MODERATE BREEZE
30-01-2025	31-01-2025	77	22	9	BDL	CLOUDY/MODERATE BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

GUEST HOUSE/ COLONY		**WNGOA4**				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	2	6	10	
03-01-2025	04-01-2025	84	28	10	BDL	CLEAR/LIGHT BREEZE
04-01-2025	05-01-2025	80	25	10	BDL	CLEAR/CALM
10-01-2025	11-01-2025	77	19	9	BDL	CLEAR/MODERATE BREEZE
11-01-2025	12-01-2025	86	23	10	BDL	CLOUDY/MODERATE BREEZE
17-01-2025	18-01-2025	72	24	9	BDL	CLEAR/LIGHT BREEZE
18-01-2025	19-01-2025	70	26	9	BDL	CLEAR/CALM
24-01-2025	25-01-2025	92	30	10	BDL	CLEAR/MODERATE BREEZE
25-01-2025	26-01-2025	88	27	9	BDL	CLOUDY/MODERATE BREEZE
29-01-2025	30-01-2025	79	24	8	BDL	CLEAR/MODERATE BREEZE
30-01-2025	31-01-2025	87	31	10	BDL	CLOUDY/MODERATE BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

SAMPLE DESCRIPTION	Water sample			
Test Required	pH: IS 3025 -Part 11:1983(RA 2017),TSS: IS 3025-Part 17:1984(RA 2017),COD: APHA (23rd Edition) 5220 C :2017,O &G: IS 3025-Part 39:1991(RA 2019) & BOD: IS 3025 (Part 44): 1993 (RA 2019)			
SAMPLING METHOD	LSOP 5	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-01-25 TO 15-02-25

MINE WATER DISCHARGE:	WNGOW1			
DATE OF SAMPLE COLLECTION	ANALYSIS RESULTS			
	pH	TSS (in mg/l)	COD(in mg/l)	O & G(in mg/l)
DETECTION LIMIT	2	10	4	2
12-01-2025	8.21	20	40	BDL
28-01-2025	8.16	26	44	BDL
STANDARDS FOR COAL MINE, GSR 742E, dt. 25/09/2000	**5.5 - 9.0**	**100**	**250**	**10**

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

NOISE LEVEL MONITORING DATA

SAMPLE DESCRIPTION	NOISE SAMPLE
Test Required	CPCB PROTOCOL FOR AMBIENT NOISE MEASUREMENT, DEC-2015
SAMPLING METHOD	LSOP 6

MANAGER OFFICE:	WNGON1		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
JAN'25	11-01-2025	55.4	53.1
JAN'25	28-01-2025	55.6	53.4
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**75**	**70**

COLONY (GHONSA)	WNGON2		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
JAN'25	11-01-2025	44.2	42.2
JAN'25	28-01-2025	43.7	41.5
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**55**	**45**



Amol Kamble
Reviewed by



M. Rabbani
Authorised by

1. This report cannot be reproduced in part or full without written of the management.
2. Laboratory activities are performed at the Laboratory permanent facility that is ground floor, Environment Lab, CMPDI RI-IV, Nagpur.
3. This report refers to the values related to the items tested.

********** End of report **********

STRICTLY RESTRICTED
FOR COMPANY USE ONLY
The information given in this report is not to be communicated either directly or indirectly to the press or to any person not holding an official position in the CIL / Government

ENVIRONMENTAL MONITORING REPORT

GHONSA OC

WANI NORTH AREA

WESTERN COALFIELDS LTD.

JOB NO. 4094423068

FEBRUARY 2025

Environment Laboratory
NABL Accredited vide Cert. No. TC-7102
CMPDI
REGIONAL INSTITUTE-IV, KASTURBA NAGAR,
JARIPATKA, NAGPUR, PIN – 440 014

AN ISO 9001:2015 COMPANY

Environment Laboratory CMPDI RI-IV, NAGPUR	**Test Report**	TC-7102

TEST REPORT NO.	RIN/TR/FEB-25/23		DATE OF ISSUE	25-03-2025
NAME OF CUSTOMER	GM(ENV.), WCL(HQ), NAGPUR			
TEST REQUIRED	SPM: IS 5182 Part-4:1999(RA 2019), PM-10: IS-5182 Part 23:2006(RA 2017), PM2.5: USEPA Quality Assurance guidance document volume-II (part-II)-2.12:2016, NO2: IS 5182 Part-06:2006(2017), SO2:IS 5182 Part-2:2001(RA 2017)			
SAMPLE DESCRIPTION	AIR SAMPLE		SAMPLING PLAN :	LQR 47
SAMPLING METHOD : LSOP 4	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:			16-02-25 TO 15-03-25

PROJECT MANAGER OFFICE		**WNGOA1**					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	**PM_{10}**	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	5	2	6	10	
08-02-2025	09-02-2025	281	192	48	16	13	CLEAR/MODERATE BREEZE
22-02-2025	23-02-2025	302	199	59	19	15	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

SAM OFFICE/ CANTEEN		**WNKUA2**					
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	**PM_{10}**	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	5	2	6	10	
08-02-2025	09-02-2025	263	187	41	13	10	CLEAR/MODERATE BREEZE
22-02-2025	23-02-2025	249	154	37	12	BDL	CLEAR/MODERATE BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

GHONSA VILLAGE		**WNGOA3**				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	2	6	10	
05-02-2025	06-02-2025	65	18	8	BDL	CLEAR/LIGHT BREEZE
06-02-2025	07-02-2025	78	22	9	BDL	CLEAR/CALM
12-02-2025	13-02-2025	81	27	8	BDL	CLEAR/MODERATE BREEZE
13-02-2025	14-02-2025	69	19	8	BDL	CLOUDY/MODERATE BREEZE
19-02-2025	20-02-2025	80	25	10	BDL	CLEAR/LIGHT BREEZE
20-02-2025	21-02-2025	71	21	9	BDL	CLEAR/CALM
26-02-2025	27-02-2025	90	34	10	BDL	CLEAR/MODERATE BREEZE
27-02-2025	28-02-2025	84	30	9	BDL	CLEAR/MODERATE BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

GUEST HOUSE/ COLONY		**WNGOA4**				
DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	**$PM_{2.5}$**	**NO_2**	**SO_2**	
FROM	TO	5	2	6	10	
05-02-2025	06-02-2025	75	24	9	BDL	CLEAR/LIGHT BREEZE
06-02-2025	07-02-2025	86	32	11	BDL	CLEAR/CALM
12-02-2025	13-02-2025	69	19	9	BDL	CLEAR/MODERATE BREEZE
13-02-2025	14-02-2025	80	27	10	BDL	CLOUDY/MODERATE BREEZE
19-02-2025	20-02-2025	82	26	9	BDL	CLEAR/LIGHT BREEZE
20-02-2025	21-02-2025	70	19	8	BDL	CLEAR/CALM
26-02-2025	27-02-2025	92	30	10	BDL	CLEAR/MODERATE BREEZE
27-02-2025	28-02-2025	81	25	9	BDL	CLEAR/MODERATE BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

SAMPLE DESCRIPTION	Water sample			
Test Required	pH: IS 3025 -Part 11:1983(RA 2017),TSS: IS 3025-Part 17:1984(RA 2017),COD: APHA (23rd Edition) 5220 C :2017,O &G: IS 3025-Part 39:1991(RA 2019) & BOD: IS 3025 (Part 44): 1993 (RA 2019)			
SAMPLING METHOD	LSOP 5	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-02-25 TO 15-03-25

MINE WATER DISCHARGE:	WNGOW1			
DATE OF SAMPLE COLLECTION	**ANALYSIS RESULTS**			
	pH	TSS (in mg/l)	COD(in mg/l)	O & G(in mg/l)
DETECTION LIMIT	2	10	4	2
13-02-2025	8.23	22	40	BDL
27-02-2025	8.14	28	48	BDL
STANDARDS FOR COAL MINE, GSR 742E, dt. 25/09/2000	**5.5 - 9.0**	**100**	**250**	**10**

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

NOISE LEVEL MONITORING DATA

SAMPLE DESCRIPTION	NOISE SAMPLE
Test Required	CPCB PRDECOCOL FOR AMBIENT NOISE MEASUREMENT, DEC-2015
SAMPLING METHOD	LSOP 6

MANAGER OFFICE:	WNGON1		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
FEB'25	12-02-2025	59.8	58.6
FEB'25	25-02-2025	55.4	53.2
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**75**	**70**

COLONY (GHONSA)	WNGON2		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
FEB'25	12-02-2025	44.8	43.2
FEB'25	25-02-2025	43.5	41.2
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**55**	**45**

Amol Kamble
Reviewed by

M. Rabbani
Authorised by

1. This report cannot be reproduced in part or full without written of the management.
2. Laboratory activities are performed at the Laboratory permanent facility that is ground floor, Environment Lab, CMPDI RI-IV, Nagpur.
3. This report refers to the values related to the items tested.

********** End of report **********

STRICTLY RESTRICTED
FOR COMPANY USE ONLY
The information given in this report is not to be communicated either directly or indirectly to the press or to any person not holding an official position in the CIL / Government

ENVIRONMENTAL MONITORING REPORT

GHONSA OC

WANI NORTH AREA

WESTERN COALFIELDS LTD.

JOB NO. 4094423068

MARCH 2025

Environment Laboratory
NABL Accredited vide Cert. No. TC-7102
CMPDI
REGIONAL INSTITUTE-IV, KASTURBA NAGAR,
JARIPATKA, NAGPUR, PIN – 440 014

AN ISO 9001:2015 COMPANY

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

TEST REPORT NO.	RIN/TR/MAR-25/23	DATE OF ISSUE	15-04-2025
NAME OF CUSTOMER	GM(ENV.), WCL(HQ), NAGPUR		
TEST REQUIRED	SPM: IS 5182 Part-4:1999(RA 2019), PM-10: IS-5182 Part 23:2006(RA 2017), PM2.5: USEPA Quality Assurance guidance document volume-II (part-II)-2.12:2016, NO2: IS 5182 Part-06:2006(2017), SO2:IS 5182 Part-2:2001(RA 2017)		
SAMPLE DESCRIPTION	AIR SAMPLE	SAMPLING PLAN :	LQR 47
SAMPLING METHOD : LSOP 4	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-03-25 TO 15-04-25

PROJECT MANAGER OFFICE | WNGOA1

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	5	2	6	10	
08-03-2025	09-03-2025	266	174	41	14	10	CLEAR/MODERATE BREEZE
22-03-2025	23-03-2025	241	156	34	12	9	CLEAR/LIGHT BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

SAM OFFICE/ CANTEEN | WNKUA2

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)					ENVIRONMENT CONDITIONS (Sky/Wind)
		SPM	PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	5	2	6	10	
08-03-2025	09-03-2025	264	182	42	14	11	CLEAR/MODERATE BREEZE
22-03-2025	23-03-2025	243	162	37	12	9	CLEAR/LIGHT BREEZE
STANDARDS FOR COAL MINE, GSR 742(E), dt. 25TH DECember 2000		**600**	**300**	**-**	**120**	**120**	

GHONSA VILLAGE | WNGOA3

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	2	6	10	
04-03-2025	05-03-2025	62	28	9	6	CLEAR/LIGHT BREEZE
05-03-2025	06-03-2025	79	21	7	4	CLEAR/CALM
11-03-2025	12-03-2025	84	34	10	7	CLEAR/MODERATE BREEZE
12-03-2025	13-03-2025	75	25	8	5	CLEAR/MODERATE BREEZE
18-03-2025	19-03-2025	80	25	10	6	CLEAR/LIGHT BREEZE
19-03-2025	20-03-2025	71	21	9	5	CLEAR/CALM
25-03-2025	26-03-2025	86	34	10	6	CLEAR/LIGHT BREEZE
26-03-2025	27-03-2025	70	20	8	5	CLEAR/LIGHT BREEZE
28-03-2025	29-03-2025	69	17	7	4	CLEAR/LIGHT BREEZE
29-03-2025	30-03-2025	85	28	10	7	CLEAR/MODERATE BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

GUEST HOUSE/ COLONY | WNGOA4

DATE(dd:mm:yy) OF SAMPLING		PARAMETERS (24 hourly values in µg/m^3)				ENVIRONMENT CONDITIONS (Sky/Wind)
		PM_{10}	$PM_{2.5}$	NO_2	SO_2	
FROM	TO	5	2	6	10	
04-03-2025	05-03-2025	84	27	8	5	CLEAR/LIGHT BREEZE
05-03-2025	06-03-2025	77	24	7	3	CLEAR/CALM
11-03-2025	12-03-2025	86	34	9	6	CLEAR/MODERATE BREEZE
12-03-2025	13-03-2025	64	19	7	5	CLEAR/MODERATE BREEZE
18-03-2025	19-03-2025	81	30	9	5	CLEAR/LIGHT BREEZE
19-03-2025	20-03-2025	62	20	8	4	CLEAR/CALM
25-03-2025	26-03-2025	83	27	10	7	CLEAR/LIGHT BREEZE
26-03-2025	27-03-2025	76	24	9	5	CLEAR/LIGHT BREEZE
28-03-2025	29-03-2025	88	31	9	6	CLEAR/LIGHT BREEZE
29-03-2025	30-03-2025	81	27	10	7	CLEAR/MODERATE BREEZE
NAAQS, 2009		**100**	**60**	**80**	**80**	

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

SAMPLE DESCRIPTION	Water sample			
Test Required	pH: IS 3025 -Part 11:1983(RA 2017),TSS: IS 3025-Part 17:1984(RA 2017),COD: APHA (23rd Edition) 5220 C :2017,O &G: IS 3025-Part 39:1991(RA 2019) & BOD: IS 3025 (Part 44): 1993 (RA 2019)			
SAMPLING METHOD	LSOP 5	PERIOD OF PERFORMANCE OF LAB ACTIVITIES:		16-03-25 TO 15-04-25

MINE WATER DISCHARGE:	WNGOW1			
DATE OF SAMPLE COLLECTION	**ANALYSIS RESULTS**			
	pH	TSS (in mg/l)	COD(in mg/l)	O & G(in mg/l)
DETECTION LIMIT	2	10	4	2
09-03-2025	8.32	26	40	BDL
29-03-2025	8.23	20	36	BDL
STANDARDS FOR COAL MINE, GSR 742E, dt. 25/09/2000	**5.5 - 9.0**	**100**	**250**	**10**

Analysed by

Environment Laboratory CMPDI RI-IV, NAGPUR	Test Report	TC-7102

NOISE LEVEL MONITORING DATA

SAMPLE DESCRIPTION	NOISE SAMPLE
Test Required	CPCB PROTOCOL FOR AMBIENT NOISE MEASUREMENT, DEC-2015
SAMPLING METHOD	LSOP 6

MANAGER OFFICE:	WNGON1		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
MAR'25	06-03-2025	55.6	53.2
MAR'25	25-03-2025	55.1	53.3
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**75**	**70**

COLONY (GHONSA)	WNGON2		
MONTH	DATE OF SAMPLE COLLECTION	NOISE LEVEL IN dB(A)	
		DAY TIME	NIGHT TIME
	DETECTION LIMIT	20	20
MAR'25	06-03-2025	44.2	42.1
MAR'25	25-03-2025	42.7	40.4
NOISE POLLUTION (REGULATION AND CONTROL) RULES		**55**	**45**

Amol Kamble
Reviewed by

M. Rabbani
Authorised by

1. This report cannot be reproduced in part or full without written of the management.
2. Laboratory activities are performed at the Laboratory permanent facility that is ground floor, Environment Lab, CMPDI RI-IV, Nagpur.
3. This report refers to the values related to the items tested.

********** End of report **********

STRICTLY RESTRICTED
FOR COMPANY USE ONLY
The information given in this report is not to be communicated either directly or indirectly to the press or to any person not holding an official position in the CIL / Government

ENVIRONMENTAL MONITORING REPORT
w.r.t. HEAVY METALS IN AMBIENT AIR

WANI NORTH AREA

WESTERN COALFIELDS LTD.

HALF YEARLY (OCT 24 - MAR 25)

Environment Laboratory
NABL Accredited vide Cert. No. TC-7102

CMPDI

REGIONAL INSTITUTE-IV, KASTURBA NAGAR,
JARIPATKA, NAGPUR, PIN – 440 014

AN ISO 9001:2015 COMPANY

INDEX

Sl. No.	PARTICULARS	PAGE NO.
1	HEAVY METAL ANALYSIS REPORT	1 TO 15

Environment Laboratory CMPDI RI-IV, NAGPUR	**Test Report** **Ambient Air Quality Monitoring Data For Heavy Metals**	

TEST REPORT NO.	RIN/TR/DEC /HM87	DATE OF ISSUE	28-01-2025
NAME OF CUSTOMER	GM(ENV.),WCL(HQ), NAGPUR	SAMPLE DESCRIPTION	AIR SAMPLE
CUSTOMER LETTER REFERENCE NO.	WCL/HQ/ENV/14-I/443-455 DATED 03.04.2024		
TEST REQUIRED	Heavy metals (As, Pb, Ni, Cr & Cd) in air samples (ASTM D 4185)		
NAME OF AREA	WANI NORTH	SAMPLING METHOD : LSOP 4	
NAME OF PROJECT	GHONSA OC EXPN	SAMPLING PLAN : LQR 47	
No. of Pages	1		

Sl No.	Name of location	Location Code	Date of sampling
1	PROJECT MANAGER OFFICE	WNKUA-1	07-10-2024
2	SAM OFFICE /CANTEEN	WNKUA-2	07-10-2024
3	GUEST HOUSE /COLONY	WNKUA-3	05-10-2024
4	GHONSA VILLAGE	WNGOA-4	05-10-2024

Sl. No.	Parameter	Method of analysis	Detection limit	Observed Value				National Ambient Air Quality Standard NAAQS, 2009
				WNKUA-1	WNKUA-2	WNKUA-3	WNGOA-4	
1	Arsenic, µg/m^3	ASTM D 4185	0.0007 µg/m^3	BDL	BDL	BDL	BDL	0.006 µg/m^3 (Annual average)
2	Lead, µg/m3	IS 5182 PART 22	7.0 µg/m^3	BDL	BDL	BDL	BDL	1.0 µg/m^3 (24 Hourly average)
3	Nickle, µg/m^3	ASTM D 4185	0.007 µg/m^3	0.0074	BDL	BDL	BDL	0.02 µg/m3 (Annual average)
4	Total Chromium, µg/m^3	ASTM D 4185	0.0045 µg/m^3	0.0045	BDL	BDL	BDL	**
5	Cadmium, µg/m^3	ASTM D 4185	0.0015 µg/m^3	BDL	BDL	BDL	BDL	**
6	Mercury, µg/m3	ASTM D 4185	0.0007 µg/m^3	BDL	BDL	BDL	BDL	**

BDL: BELOW DETECTION LIMIT

SCIENTIFIC ASSISTANT

M. RABBANI
AUTHORIZED SIGNATORY

1 This Report refers to the values related to the items tested.
2 This Report cannot be reproduced in part or full without written permission of the management.
3 ** This parameter not regulated as per NAAQS

REPORT ON

MONITORING OF GROUND WATER LEVEL

OF

GHONSA OC EXPN. MINE,

WANI NORTH AREA

WESTERN COALFIELDS LTD.

PERIOD- DEC 2022 (POST-MONSOON), JAN-FEB -2023 (WINTER) , MAY-2023 (PRE-MONSOON) AUG-23 (MONSOON) NOV 2023 (POST-MONSOON) ,JAN 2024 (WINTER) ,MAY 2024(PRE MONSOON), AUG 2024 (MONSOON), NOV (POST-MONSOON) 2024 & JAN 2025 (WINTER)

M/s Anacon Laboratories Pvt. Ltd., Nagpur

MoEF&CC (GOI) Recognized Laboratory
ISO 9001:2015, ISO 14001:2015, ISO 45001:2018
Lab. & Consultancy: FP-34, 35, Food Park,
MIDC, Butibori, Nagpur – 441122
Mob: +91-9372960077
Email: ***ngp@anacon.in***
Website: ***www.anaconlaboratories.com***

Report No. ANqr /PD/20A/2023/199

2023-24 & 2024-25

Certificate

Groundwater level monitoring has been conducted with due diligence, and a comprehensive report on the monitoring of groundwater levels in all observation wells has been prepared as per the scope of work outlined in work order no. वेकोलि/मुख्यालय/पर्यावरण/14-L/77, dated 08.12.2022 & second extension of work vide reference no. वेकोलि/मुख्यालय/पर्यावरण /14-L/48-60 Dated-01.01.2025 for the Jan 2025 (winter) Period.

The report includes the monitoring of groundwater levels and water quality analysis of observation wells pertaining to the GHONSA OC EXPN. MINE, Wani North area of Yeotmal District, M.S.

The groundwater level monitoring was meticulously carried out by Anacon Laboratories Pvt. Ltd., and the analysis of the samples was performed by Skylab Analytical Laboratory, Bhiwandi, Kalyan a NABL Accredited Laboratory. (NABL Certificate no. TC-5150)

Anacon Laboratories Pvt. Ltd. gratefully acknowledges the full cooperation rendered by the concerned WCL officials, which facilitated the timely completion of the project.

Atharva Nayab
(Geologist)

Gyanchand Bohra
NABET Accredited EIA Expert
for Hydrogeology & Geology

ANACON LABORATORIES PVT. LTD. NAGPUR

Nagpur
Jan-2025

(Dr. D. G. Garway)
Head of Organization
Anacon Laboratories Pvt. Ltd., Nagpur

CONTENTS			
TABLE/FIGURE	**NAME OF SUB MINE PROJECT**	**GROUND WATER MONITORING DETAILS OF WELL**	**Page No.**
I-FIGURE	GHONSA OC EXPN. MINE,	GROUND WATER MONITORING STATION (OBSERVATION WELLS IN AND AROUND OF GHONSA OC EXPN. MINE,	7
I-TABLE	GHONSA OC EXPN. MINE,	**PERIOD- DEC 2022 (POST-MONSOON), JAN-FEB -2023 (WINTER) , MAY-2023 (PRE-MONSOON) AUG-23 (MONSOON) NOV 2023 (POST-MONSOON) ,JAN 2024 (WINTER) ,MAY 2024(PRE MONSOON), AUG 2024 (MONSOON), NOV (POST-MONSOON) 2024 & JAN 2025 (WINTER)**	8
FIGURE-II	GHONSA OC EXPN. MINE,	**HYDROGRAPHS OF THE WATER LEVEL (OBSERVATION WELLS IN AND AROUND GHONSA OC EXPN. MINE)**	11

ANACON LABORATORIES PVT LTD. NAGPUR

INTRODUCTION

Western Coalfields Limited (WCL) is one of the eight Subsidiary Companies of Coal India Limited (CIL) which is under administrative control of Ministry of Coal. The Company incorporated under the Companies Act, 1956 has its registered office at Coal Estate, Civil Lines, Nagpur–440001. WCL has been conferred "Mini-ratna" status on 15 March 2008. It has mining operation spread over the states of Maharashtra (in Nagpur, Chandrapur & Yeotmal Districts) and Madhya Pradesh (in Betul and Chhindwara Districts). It has been divided into 10 administrative areas. The Company is a major source of supplies of coal to the industries located in Western India in the States of Maharashtra, Madhya Pradesh, Gujarat and also in Southern India in the States of Andhra Pradesh, Tamil Nadu, Karnataka and Kerala. A large numbers of Power Houses under Maharashtra, Madhya Pradesh, Gujarat, Karnataka, Punjab and Uttar Pradesh - Electricity Boards are major consumers of its coal along with cement, steel, chemical, fertilizer, paper and brick Industries in these states.

M/s Anacon Laboratories Pvt. Ltd. has been awarded the Work of "Groundwater level Monitoring (i.e. bore well / piezometer Water levels) and Water quality analysis (as per IS10500) for 76 projects / mines of WCL (situated in the state of Madhya Pradesh – Chhindwara & Betul districts and Maharashtra – Nagpur, Chandrapur & Yeotmal districts) for one year as per condition stipulated in Environmental Clearance letters issued by MoEF & CC & NOC issued by CGWA" vide work order वेकोलि/मुख्यालय/पर्यावरण/14-L/77 on date: 08.12.2022 & second extension of work vide reference no. वेकोलि/मुख्यालय/पर्यावरण /14-L/48-60 Dated- 01.01.2025 for the Jan 2025 (winter) Period.

This Ground Water Level Monitoring report is prepared GHONSA OC EXPN. MINE,,of Wani North area of WCL for 10 seasons i.e. **PERIOD- DEC 2022 (POST-MONSOON), JAN-FEB -2023 (WINTER) , MAY-2023 (PRE-MONSOON) AUG-23 (MONSOON) NOV 2023 (POST-MONSOON) ,JAN 2024 (WINTER) ,MAY 2024(PRE MONSOON), AUG 2024 (MONSOON), NOV (POST-MONSOON) 2024 & JAN 2025 (WINTER).**These mines are located in Wani North Area of Yeotmal District, Maharashtra.

GENERAL HYDROGEOLOGICAL CONDITION

Deccan Trap Basalt is the predominant water bearing formation, followed by Gondwana formation having Sandstone and Shale sequence. Penganga and Quaternary Alluvium aquifers are spread in limited areas. Archean aquifers are limited and have less significance in the area.

ARCHEAN

Achaeans, which comprise granites, granitic gneisses and schists, occur in Umarkhed taluka. These rocks as such have limited ground water potential. In these rocks only weathered portions and jointed zones possess water-bearing capacity and ground water occurs under unconfined condition in the area.

VINDHYAN

In Vindhyans, Limestones are water bearing formation while Sandstone, due to their hard and compact nature, have poor ground water potential and occur in southeastern peripheral parts of Wani taluka. The Limestones as such are massive but wherever they are cavernous they are capable of holding water. The ground water occurs under unconfined condition in the area.

GONDWANA

The Gondwana consists of Kamthi and Barakar Sandstone and Shale and occupy north-south extending elongated stretch in parts of Maregaon and Wani talukas. Sandstone is usually friable and possesses primary porosity due to its granular nature. They are most productive water bearing formations in the district. The ground water occurs under semi confined to confined conditions in the area and water bearing zones have been encountered down to depth of 470 m.

DECCAN TRAP BASALT

Deccan Trap Basalt is widely spread and forms important water bearing formation, which occupies almost entire district except south eastern part. On the whole, Deccan Trap Basalt exhibits a multi aquifer system. Based on the Litholog of 51 exploratory wells and Piezometers, it is observed that weathered Vesicular Basalt mainly forms the predominant shallow aquifer down to the depth of 20 m bgl. Massive Basalt is also encountered at the top thereby forming poor yielding aquifer and also restricting the ground water recharge to the underlying porous Vesicular Basalt. Fractured Basalt is also observed in certain places with limited to significant thickness. In Deccan Trap Basalt phreatic aquifer generally occurs down to 25 m, however, fracture zones have occurred within 80 m range except at few places where it occurs down to 158 m also.

ALLUVIUM

Alluvium occurs in patches along the banks of Wardha and Penganga rivers and their major tributaries and consists of clay and silt with lenticular bodies of sand and gravel. In Ralegaon area, it is observed that sand zones are found in the depth range of 20-25 m bgl, while the top 15-16 m is full of clay and silt. Ground water in Alluvium occurs both under unconfined and 8 semi-confined conditions.



GHONSA OC EXPN. MINE,

WANI NORTH AREA

WESTERN COALFIELDS LTD.

PERIOD- DEC 2022 (POST-MONSOON), JAN-FEB -2023 (WINTER) , MAY-2023 (PRE-MONSOON) AUG-23 (MONSOON) NOV 2023 (POST-MONSOON) ,JAN 2024 (WINTER) ,MAY 2024(PRE MONSOON), AUG 2024 (MONSOON), NOV (POST-MONSOON) 2024 & JAN 2025 (WINTER)



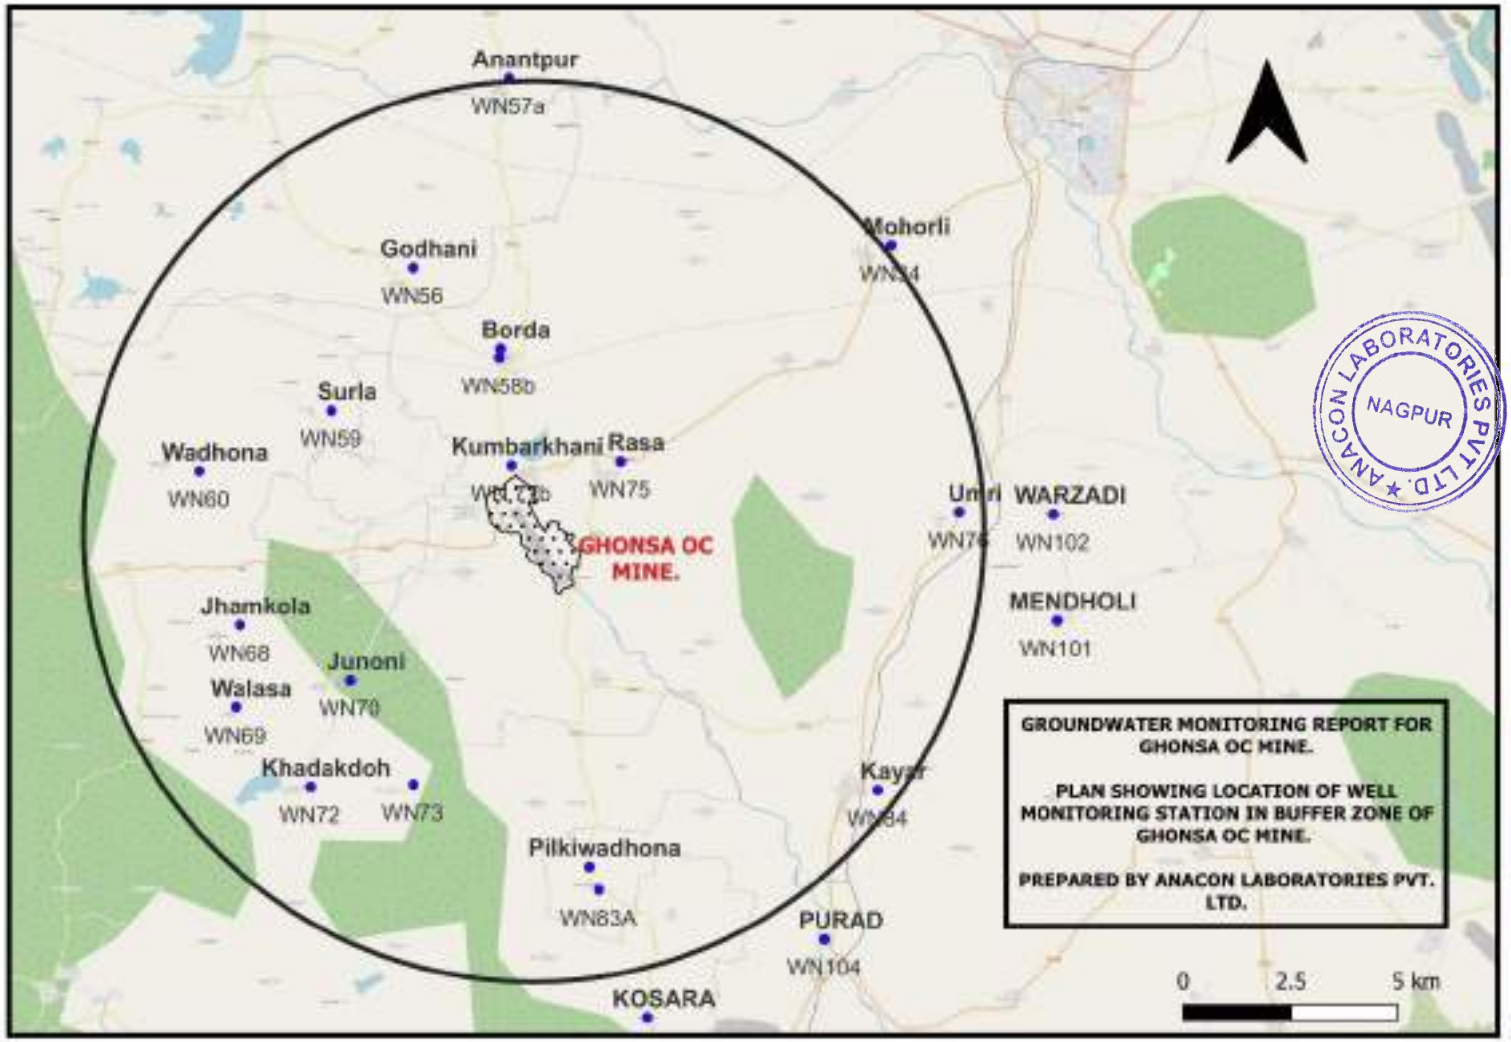


FIGURE-I: GROUND WATER MONITORING STATION (OBSERVATION WELLS IN AND AROUND OF GHONSA OC EXPN. MINE)

Table-IIA: Groundwater level monitoring data of dugwells in buffer zone of Expn. of Ghonsa OC, Wani North Area, WCL

Sr. No	Well No.	Name of village	Well location	Latitude	Longitude	R.L. in m	Well dia (m)	Well depth (m bmp)	Height of measuring point (m agl)	Depth to Water Level (m bgl)									
										Dec-22	JAN-FEB-23	May-23	Aug-23	Nov-23	Jan-24	May-24	Aug-24	Nov-24	Jan-25
1	WN 23	Wehegaon	Back side of Vittal Mandir	20°3'51.5967154742725''	78°49'44.0181968167315''	197	4.57	16	0.6	1.90	3.60	6.0	2.80	3.40	3.70	5.90	3.00	3.15	3.80
2	WN 34	Mohorli	Near Hanuman temple and 60m E of Wani Rd.	20°1'37.7528239480725''	78°54'49.4794349217079''	199	2.68	6.69	0.42	2	4.7	5.8	3.00	3.60	4.80	5.60	2.75	3.80	4.50
3	WN 56	Godhani	About 400 m NW o village, adjacent to nala	20°1'19.8599825450415''	78°48'27.2972958728768''	195	7.4	5.61	0.3	2.1	2.4	4.1	2.10	2.70	2.50	3.80	2.25	2.40	2.70
4	WN 57a	Anantpur	About 70 m N of village, adjacent to nala	20°3'51.5967154742725''	78°49'44.0181968167315''	195	3.17	5.37	0.42	1.5	2.65	4.0	1.80	3.75	4.00	4.10	1.85	3.70	4.50
5	WN 58a	Borda	About 150 m W of village, 25 m N of Godhani road	20°0'15.1446979078372''	78°49'36.8423795429954''	212	3.17	7.68	0.7	3.45	4.35	6.2	2.70	4.00	4.30	6.80	2.40	3.60	4.50
6	WN 58b	Borda	About 450 m S of village, adjacent to Godhani road(Well of Tulsiram Lole)	20°0'8''	78°49'36''	215	2.78	6.4	0.76	2.6	4.5	6.3	1.90	2.80	4.10	6.60	2.05	2.50	3.60
7	WN 59	Surla	C of village	19°59'25.6751442248344''	78°47'21.9261318028248''	221	3.29	7.84	0.82	3	3.3	5.2	1.75	2.40	3.20	5.10	1.80	2.45	3.00
8	WN 60	Wadhona	E of village, about 70 m N of road	19°58'37.3556918002976''	78°45'36.3902026899154''	196	6.13	7.56	0.58	3. 4	5	6.8	2.50	3.10	4.80	6.50	2.90	3.15	4.30

Sr. No	Well No.	Name of village	Utility / Owner	Formation Tapped
1	WN 23	Wehegaon	IRRIGATION	SHELLY LIMESTONE
2	WN 34	Mohorli	IRRIGATION	BASALT
3	WN 56	Godhani	IRRIGATION	BASALT
4	WN 57a	Anantpur	IRRIGATION	SHELLY LIMESTONE
5	WN 58a	Borda	DOMESTIC	BASALT
6	WN 58b	Borda	DOMESTIC	LIMESTONE
7	WN 59	Surla	IRRIGATION	SHELLY LIMESTONE
8	WN 60	Wadhona	IRRIGATION	BASALT

Sr. No	Well No.	Name of village	Well location	Latitude	Longitude	R.L. in m	Well dia (m)	Well depth (m bmp)	Height of measuring point (m agl)	Depth to Water Level (m bgl)										Utility / Owner	Formation Tapped
										Dec-22	JAN-FEB-23	May-23	Aug-23	Nov-23	Jan-24	May-24	Aug-24	Nov-24	Jan-25		
9	WN 68	Jhamkola	200m SE of village near nalla	19°56'34.3338805208361''	78°46'8.77943275894704''	202	8.53	6.68	0.39	2.7	3.9	4.9	3.00	4.60	4.90	4.50	2.50	4.40	5.00	IRRIGATION	BASALT
10	WN 69	Walasa	About 800 m N of village in low lying area, 25 m N of Jhamkola road	19°55'28.600091765621''	78°46'5.56862034878445''	205	2.44	6.04	0.67	2.1	2.85	4.2	2.80	4.25	4.00	3.90	2.55	4.35	4.55	IRRIGATION	SHELLY LIMESTONE
11	WN 70	Junoni	About 100 m W of village in the field, about 30 m N of Walasa road	19°55'50.1201565183621''	78°47'37.0672438566931''	209	3.51	5.27	0.64	2.6	4.75	5.0	3.10	3.60	4.80	4.60	3.40	4.70	5.00	DOMESTIC	BASALT
12	WN 72	Khadakdoh	300 m SE of village, 15 m W of Jhari road	19°54'24.9923786805596''	78°47'5.10921171036673''	211	7.22	5.64	0.61	2.8	3.6	5.2	3.60	4.30	4.20	5.40	3.50	4.10	4.40	DOMESTIC	BASALT
13	WN 73	Chinchghat	C of village one well only	19°54'26.873392867364''	78°48'27.4712307620244''	218	4.27	6.98	0.18	3.1	4.7	5.9	4.10	4.80	5.00	5.50	4.20	4.90	5.20	IRRIGATION	SHELLY LIMESTONE
14	WN 75	Rasa	S edge of village, adjacent to Sakra road	19°58'45.1282324667417''	78°51'13.1054994562215''	218	4.27	6.98	0.18	2.2	3.6	4.2	2.90	3.00	3.70	5.00	2.65	3.20	3.50	IRRIGATION	SHELLY LIMESTONE
15	WN 76	Umri	About 150m NW of village near school, adjacent to nala	19°58'4.58213032590891''	78°55'44.1082006743899''	212	4.36	8.85	0.6	4.4	6.2	7.2	2.60	3.85	4.90	7.70	2.20	3.90	4.60	IRRIGATION	BASALT
16	WN 77b	Kumbarkhani	near Vidarbh River, near road from Kumbarkhani to Sakra	19°58'42''	78°49'46''	213	5.18	7.87	0.33	2.8	5.3	6.2	3.80	3.50	4.80	6.10	4.00	3.60	4.50	IRRIGATION	SHELLY LIMESTONE

Sr. No	Well No.	Name of village	Well location	Latitude	Longitude	R.L. in m	Well dia (m)	Well depth (m bmp)	Height of measuring point (m agl)	Depth to Water Level (m bgl)										Utility / Owner	Formation Tapped
										Dec-22	JAN-FEB-23	May-23	Aug-23	Nov-23	Jan-24	May-24	Aug-24	Nov-24	Jan-25		
17	WN 103	KOSARA	SOUTH 150 FROM MANDIR NEAR ROAD JUNCTION .	19°51'20.42''	78°51'34.72''	215	6	13	0.5	4.65	6.80	7.1	4.00	4.80	5.00	7.00	3.50	4.70	5.30	—	—
18	WN 104	PURAD	NORTH-WEST 200M FROM MEGRAJ PANDHARI LEDANGE HOUSE	19°52'23.14''	78°53'56.47''	205	4.2	9.5	0.3	4.1	5.4	8.2	3.80	4.50	5.20	7.85	4.00	4.35	5.00	—	—
19	WN 83A	Pilkiwadhona	20 m S of road, C of village Near Hanuman Mandir	19°53'2.66869877438864''	78°50'55.7634485273353''	207	3.01	8.29	0.55	3.3	4	6.8	3.00	3.80	4.20	6.65	3.50	4.00	4.10	DOMESTIC	BASALT
20	WN 83B	Pilkiwadhona	About 700m N of village adjacent to nalla on W side	19°53'21''	78°50'48''	208	4.88	7.47	0.76	3.05	4.8	6.1	2.90	3.30	4.70	6.00	3.00	3.20	4.30	IRRIGATION	SHELLY LIMESTONE
21	WN 84	Kayar	About 10 m E of main road in Railway Colony	19°54'22.374535689346''	78°54'38.8706174765252''	222	5.02	4.56	0.46	2.1	3.3	4.2	1.60	2.40	3.20	4.40	1.40	2.00	2.90	DOMESTIC	BASALT
22	WN 101	MENDHOLI	ABOUT 150m ADJACENT TO ROAD NEAR ZP SCHOOL	19°56'37.89''	78°57'2.35"	200	3.6	8.4	0.6	3.5	3.1	5.8	3.70	4.00	3.85	6.00	3.95	4.15	4.10	—	—
23	WN 102	WARZADI	IN THE FIELD OF AGRICULTURE	19°58'2.88"	78°56'59.33"	222	4.6	9.2	0.2	3.8	5.3	8.5	4.30	5.20	5.65	8.10	4.55	5.20	5.50	—	—

ANACON LABORATORIES PVT. LTD. NAGPUR

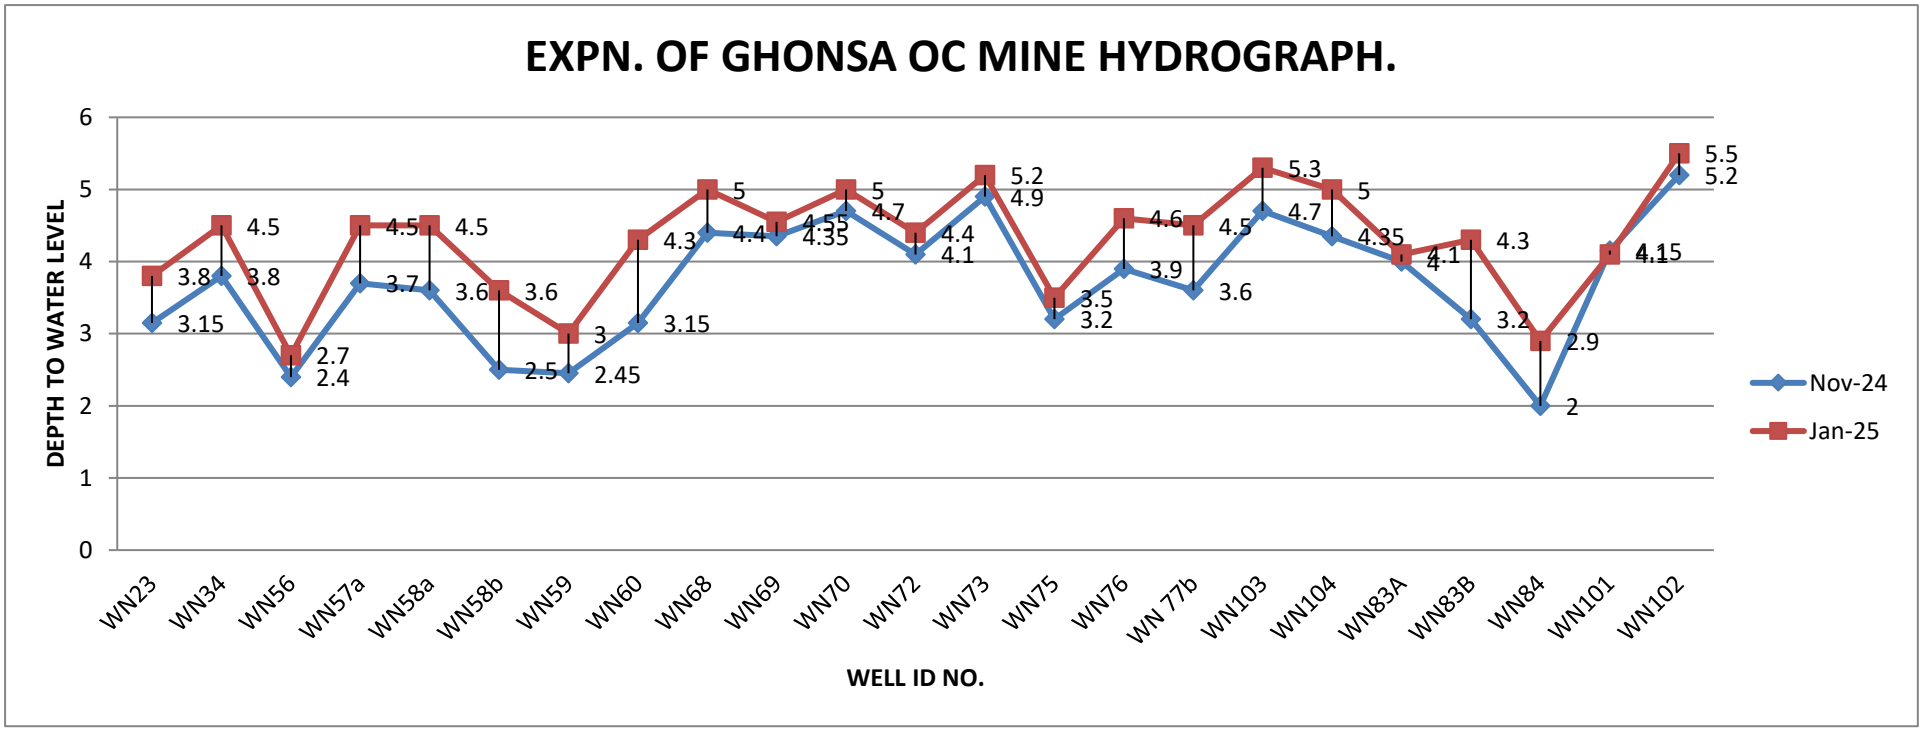


FIGURE-II: HYDROGRAPHS OF THE WATER LEVEL (OBSERVATION WELLS IN AND AROUND GHONSA OC EXPN. MINE)

ANACON LABORATORIES PVT. LTD. NAGPUR

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
SKY LAB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000005F

SKY LAB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-005)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-005)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Wehegaon - (Wani North Area) Well No.: WN23
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**256.09**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	158.06	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**115.9**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.38	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	**48.59**	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	BDL(DL- 2)	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.18	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	17.00	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**924**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**498**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.05	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.42	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	0.06	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity ,Calcium , Magnesium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEF,CC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000006F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-006)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-006)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Mohorli - (Wani North Area) Well No.: WN34
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**216.02**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	138.02	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**148.06**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.51	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	26.73	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	2.13	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.83	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	18.33	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**849**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**414**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.05	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.44	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	0.06	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.18	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity ,Calcium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory 3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water 5 'mg/l' is equivalent to 'ppm' 6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC24230915965

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

SKYLAB is always subject to improvement. For better customer satisfaction, we welcome your feedback on : feedback@skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000007F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-007)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-007)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Godhani - (Wani North Area) Well No.: WN56
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	148	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	168	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**85.6**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.71	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	16.64	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	4.74	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.91	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	21.37	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**834**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**376**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.03	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Calcium , TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory 3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000008F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-008)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-008)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Anantpur - (Wani North Area) Well No.: WN57A
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**242.35**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	180.06	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**164**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.67	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	12.02	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	4.39	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.03	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	19.18	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**924**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**432**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.37	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity ,Calcium , TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by alteration, falsification etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 mg/l is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist.. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com
SKYLAB is always subject to improvement. For better customer satisfaction, we welcome your feedback on : feedback@skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
TC 5150
• ENVIRONMENT • FOOD • TEXTILE

ULR:TC5150240000000009F

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-009)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-009)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Borda - (Wani North Area) Well No.: WN58A
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**214.02**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	179.87	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**89.6**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	**1.03**	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	20.06	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	5.38	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.68	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	25.83	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**749**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**342**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.39	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity ,Calcium , Fluoride, TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory. 3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 mg/L is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. Email : mails@skylabenviro.com, Website : www.skylabenviro.com
SKYLAB is always subject to improvement. For better customer satisfaction, we welcome your feedback on : feedback@skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000010F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
TC 5150
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-010)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-010)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Borda - (Wani North Area) Well No.: WNSBB
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit *	Permissible Limit *	Reference Method
1	Alkalinity	mg/L	154	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	117.12	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	56.8	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.24	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	**33.04**	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	3.04	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.84	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	18.71	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**721**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**278**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.27	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.07	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Magnesium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 mg/l is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000011F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-011)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-011)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Surla - (Wani North Area) Well No.: WN59
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	186.02	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	162.06	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	67.2	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.38	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	29.16	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	3.59	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.16	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	19.75	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**768**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**288**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.05	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.03	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	0.06	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com
SKYLAB is always subject to improvement. For better customer satisfaction, we welcome your feedback on : feedback@skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000012F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
TC 5150
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-012)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-012)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Wadhona - (Wani North Area) Well No.: WN60
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit *	Permissible Limit *	Reference Method
1	Alkalinity	mg/L	**210.06**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	150.59	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**132**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.64	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	24.78	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	3.72	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.04	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	20.42	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**836**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**402**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.04	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.07	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	0.06	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.09	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium, TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is not to be reproduced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000013F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
TC 5150
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-013)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-013)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Jhamkola - (Wani North Area) Well No.: WN68
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**240.42**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	154	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**144.2**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.51	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	21.87	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	2.46	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.14	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	16.62	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**840**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**356**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.05	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.15	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium, TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC24230915972

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000014F

Sky LaB
ANALYTICAL LABORATORY

Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-014)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:
SAMPLE REGISTRATION NO. : 05/GW(24-25-014)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS
LOCATION : Walasa - (Wani North Area) Well No.: WN69
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**240.02**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	129.67	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**132**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.69	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	**32.56**	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	5.05	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.26	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	19.18	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**989**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**498**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.22	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium, Magnesium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will ttract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

SALAC24230915973

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000015F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-015)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-015)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Junoni - (Wani North Area) Well No.: WN70
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit *	Permissible Limit *	Reference Method
1	Alkalinity	mg/L	**248.02**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	184	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	40.8	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.16	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	21.87	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	2.85	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.17	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	15.48	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**856**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**356**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.38	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.05	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will ttract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 mg/l is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

SALAC24230915974

ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000016F

Sky LaB
ANALYTICAL LABORATORY

Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
TC 5150
▪ ENVIRONMENT ▪ FOOD ▪ TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-016)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-016)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Khadakdoh - (Wani North Area) Well No.: WN72
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**233.66**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	96.21	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**140.2**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.16	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	21.87	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	2.85	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.17	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	15.48	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**886**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**442**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.05	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.58	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.16	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL Indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC24230915975

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
SKY LAB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000017F

SKY LAB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-017)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-017)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Chinchghat - (Wani North Area) Well No.: WN73
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit *	Permissible Limit *	Reference Method
1	Alkalinity	mg/L	**244.45**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	184	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**120.6**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.56	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	23.81	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	5.05	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.08	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	28.30	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**972**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**524**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.06	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.13	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/firm/company/ etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. *Permissible limit in absence of an alternate source for drinking water. 5. mg/L equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC24230915976

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000018F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-018)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-018)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Rasa - (Wani North Area) Well No.: WN75
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**212**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	138	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**112.4**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.43	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	**33.53**	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	4.89	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.02	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	21.94	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**812**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**408**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	**1.44**	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium , Magnesium ,TDS, Hardness(total), Iron are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. The report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC2423091597

ENVIRONMENTAL LABORATORY
SKY LAB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000019F

SKY LAB
ANALYTICAL LABORATORY

Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-019)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-019)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Umri - (Wani North Area) Well No.: WN76
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**256.99**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	164	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**110**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	1.02	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	**35.47**	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	4.91	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.37	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	29.54	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**956**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**413**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.08	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.07	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium , Magnesium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be reproduced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

SALAC24230915978

ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000020F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-020)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-020)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION :Kumbarkhani (Wani North Area) Well No.: WN77b
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit *	Permissible Limit *	Reference Method
1	Alkalinity	mg/L	**212**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	142.22	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	**132**	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.61	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	**31.10**	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	3.21	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.10	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	22.70	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**832**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**398**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.07	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.16	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.09	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity, Calcium , Magnesium ,TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by advertisement, organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5. mg/l is equivalent to 'ppm' .6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000021F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-021)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-021)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION :Pilkiwadhona - (Wani North Area) Well No: WN83A
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	150	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	129.67	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	61.6	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.73	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	22.84	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	7.18	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.53	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	22.89	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**662**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**248**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.06	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.27	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 TDS, Hardness(total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be reproduced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC24230915980

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000022F

Sky LaB
ANALYTICAL LABORATORY

Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-022)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:
SAMPLE REGISTRATION NO. : 05/GW(24-25-022)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS
LOCATION :Pilkiwadhona - (Wani North Area) Well No: WN83B
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit *	Permissible Limit *	Reference Method
1	Alkalinity	mg/L	**214**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	112.94	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	74.4	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.61	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	**40.33**	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	4.26	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.94	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	18.71	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**582**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**352**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.06	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	**1.03**	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.08	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity , Magnesium ,TDS, Hardness(total) ,Iron are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. The report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm' & BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC24230915981

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000023F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
TC 5150
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-023)
REPORT DATE : 06/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-023)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :01/05/2024
SAMPLE RECEIPT DATE :02/05/2024
ANALYSIS START DATE :02/05/2024
ANALYSIS COMPLETE DATE :06/05/2024

GROUND WATER ANALYSIS

LOCATION : Kayar - (Wani North Area) Well No: WN84
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	**284.06**	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	**174**	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	42.4	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.42	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	17.49	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	BDL(DL-2)	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.28	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	15.10	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	**732**	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	178	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.06	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	**1.02**	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.08	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Alkalinity , TDS, Iron are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. The report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm' .6 BDL- Below detection limit. 7 DL- DL Indicates detection limit of instrument /method and shall be considered as 'absent.

SALAC24230915982

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
SKY LAB
OUR GOAL POLLUTION CONTROL

ULR:TC515024000000048F

SKY LAB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-048)
REPORT DATE : 07/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-048)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :02/05/2024
SAMPLE RECEIPT DATE :03/05/2024
ANALYSIS START DATE :03/05/2024
ANALYSIS COMPLETE DATE :07/05/2024

GROUND WATER ANALYSIS

LOCATION : Mendholi - (Wani North Area) Well No: WN101
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	87.5	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	28.02	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	22.4	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	BDL(DL- 0.1)	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	20.89	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	2.56	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	7.83	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	11.49	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	310	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	BDL(DL- 0.1)	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	142	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.06	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.49	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: *Analyzed parameters in above tested sample* As per IS 10500: 2012 *are within limit* acceptable limit & permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5. mg/L is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com

RECOG. BY GOVT. OF INDIA (MoEFCC)
ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL

ULR:TC5150240000000049F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE
TC 5150

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-049)
REPORT DATE : 07/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-049)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :02/05/2024
SAMPLE RECEIPT DATE :03/05/2024
ANALYSIS START DATE :03/05/2024
ANALYSIS COMPLETE DATE :07/05/2024

GROUND WATER ANALYSIS

LOCATION : Warzadi - (Wani North Area) Well No: WN102
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit *	Permissible Limit *	Reference Method
1	Alkalinity	mg/L	118.75	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL-1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	129.67	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	51.2	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.37	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	28.61	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	4.33	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.02	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	16.90	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	463	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**254**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.08	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	**1.32**	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012, Hardness (total) ,Iron are Exceeds acceptable limit, however, the result is within permissible limit..

Verified by
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 mg/l is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. **Email** : mails@skylabenviro.com, **Website** : www.skylabenviro.com
SKYLAB is always subject to improvement. For better customer satisfaction, we welcome your feedback on : feedback@skylabenviro.com

ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000050F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
TC 5150
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-050)
REPORT DATE : 07/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-050)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :02/05/2024
SAMPLE RECEIPT DATE :03/05/2024
ANALYSIS START DATE :03/05/2024
ANALYSIS COMPLETE DATE :07/05/2024

GROUND WATER ANALYSIS

LOCATION : Kosara - (Wani North Area) Well No: WN103
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	118.75	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	138.04	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	60	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.52	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	29.64	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	4.14	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.04	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	22.03	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	488	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**272**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.06	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.09	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	BDL(DL- 0.05)	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Hardness (total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by:
Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY
Authorized Signatory

END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5. mg/l is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl.Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA, Pincode-421311.
Mob. : 9867577309-312 / 8422929165. Email : mails@skylabenviro.com, Website : www.skylabenviro.com
SKYLAB is always subject to improvement. For better customer satisfaction, we welcome your feedback on : feedback@skylabenviro.com

SALAC24230916013

ENVIRONMENTAL LABORATORY
Sky LaB
OUR GOAL POLLUTION CONTROL
ULR:TC5150240000000051F

Sky LaB
ANALYTICAL LABORATORY
Accredited by NABL as per ISO/IEC 17025:2017
Certified by ISO 9001:2015, ISO 14001:2015 & ISO 45001:2018
TC 5150
Recognized by Ministry of Environment, Forest & Climate Change (MoEFCC), Govt. of India, New Delhi
• ENVIRONMENT • FOOD • TEXTILE

TEST REPORT

NAME & ADDRESS OF CUSTOMER:
M/s Western Coalfields Limited (WCL)(Wani North Area)
Futala Road, Coal Estate, Civil Lines, Nagpur, WCL HQ (M.S), 44000.

REPORT NO :SAL/MSP19/FMD/05/GW(24-25-051)
REPORT DATE : 07/05/2024
CUSTOMER REF : Verbal
REF DATE : NA

SAMPLE TYPE:

SAMPLE REGISTRATION NO. : 05/GW(24-25-051)
SAMPLING PLAN& METHOD NO.: IS 3025 Part 1
SAMPLING DATE :02/05/2024
SAMPLE RECEIPT DATE :03/05/2024
ANALYSIS START DATE :03/05/2024
ANALYSIS COMPLETE DATE :07/05/2024

GROUND WATER ANALYSIS

LOCATION : Purad - (Wani North Area) Well No: WN104
SAMPLE SPECIFICATION : Ground Water

SAMPLE COLLECTED BY : Mr.Kartik Shrivas-Anacon Laboratory
SAMPLE QUANTITY : 1 Ltrs

Sr. No.	Test Parameter	Unit	Result	Acceptable Limit #	Permissible Limit #	Reference Method
1	Alkalinity	mg/L	131.25	200	600	IS 3025 (Part 23)
2	Colour	Hazen Unit	BDL(DL- 1)	5	15	IS 3025 (Part 4)
3	Chloride	mg/L	125.49	250	1000	IS 3025 (Part 32)
4	Calcium	mg/L	49.6	75	200	IS 3025 (Part 40)
5	Residual free chlorine (RFC)	mg/L	BDL(DL- 0.1)	>0.2	1	IS 3025 (Part 26)
6	Fluoride	mg/L	0.44	1.0	1.5	IS 3025 (Part 60)
7	Metal-Magnesium	mg/L	28.67	30	100	IS 3025 (Part 46)
8	Nitrate	mg/L	2.23	45	No Relaxation	IS 3025 (Part 34)
9	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Part 5)
10	pH	-	8.52	6.5 - 8.5	No Relaxation	IS 3025 (Part 11)
11	Sulphate, SO4	mg/L	19.09	200	400	IS 3025 (Part 24)
12	Total dissolved solids	mg/L	477	500	2000	IS 3025 (Part 16)
13	Turbidity	NTU	0.1	1	5	IS 3025 (Part 10)
14	Hardness (total)	mg/L	**242**	200	600	IS 3025 (Part 21)
15	Metal-Arsenic	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
16	Metal-Aluminium	mg/L	BDL(DL- 0.02)	0.03	0.2	IS 3025 (Part 2)
17	Boron as B	mg/L	0.04	0.5	2.4	IS 3025 (Part 2)
18	Metal-Copper	mg/L	BDL(DL- 0.05)	0.05	1.5	IS 3025 (Part 2)
19	Metal-Cadmium	mg/L	BDL(DL- 0.003)	0.003	No Relaxation	IS 3025 (Part 2)
20	Metal-Iron	mg/L	0.06	1.0	No Relaxation	IS 3025 (Part 2)
21	Metal-Lead	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
22	Metal-Manganese	mg/L	BDL(DL- 0.05)	0.1	0.3	IS 3025 (Part 2)
23	Metal-Nickel	mg/L	BDL(DL- 0.02)	0.02	No Relaxation	IS 3025 (Part 2)
24	Metal-Selenium	mg/L	BDL (DL-0.01)	0.01	No Relaxation	IS 3025 (Part 2)
25	Chromium	mg/L	BDL(DL- 0.05)	0.05	No Relaxation	IS 3025 (Part 2)
26	Zinc	mg/L	0.08	5	15	IS 3025 (Part 2)

Opinion/Observation: Analyzed parameters in above tested sample As per IS 10500: 2012 Hardness (total) are Exceeds acceptable limit, however, the result is within permissible limit.

Verified by

Sr. Analyst

For SKYLAB ANALYTICAL LABORATORY

Authorized Signatory


END OF REPORT

1. This report reflects findings only for the above sample tested/monitored and only for time and place of monitoring/testing. 2. This report is confidential & cannot be re-produced in part or full without permission of SKYLAB Analytical Laboratory.3. Any attempt of forgery or misleading use of this report by any person/organization etc will attract suitable legal action against them by Skylab Analytical Laboratory. 4. #Permissible limit in absence of an alternate source for drinking water. 5 'mg/l' is equivalent to 'ppm'.6 BDL- Below detection limit. 7 DL- DL indicates detection limit of instrument /method and shall be considered as 'absent.

202, CFC-3, Asmeeta Texpa, Addl Kalyan-Bhiwandi Industrial Area, MIDC, Village Kon, Tal. Bhiwandi, Dist,. Thane, Maharashtra, INDIA. Pincode-421311.
Mob. : 9867577309-312 / 8422929165. Email : mails@skylabenviro.com, Website : www.skylabenviro.com

वेस्टर्न कोल्फील्ड्स लिमिटेड के ५ मिलियन घन मीटर (कोल + अधिभार) से कम उत्पादन क्षमतावाले ५ खुली खदानों का भूमि पुनरुद्धार हेतु २०२४ के उपग्रह डाटा के आधार पर निगरानी का प्रतिवेदन

Land Restoration / Reclamation Monitoring of 5 opencast projects of Western Coalfield Limited producing less than 5 million Cu. M. (Coal+OB) per annum based on Satellite Data of the Year 2024

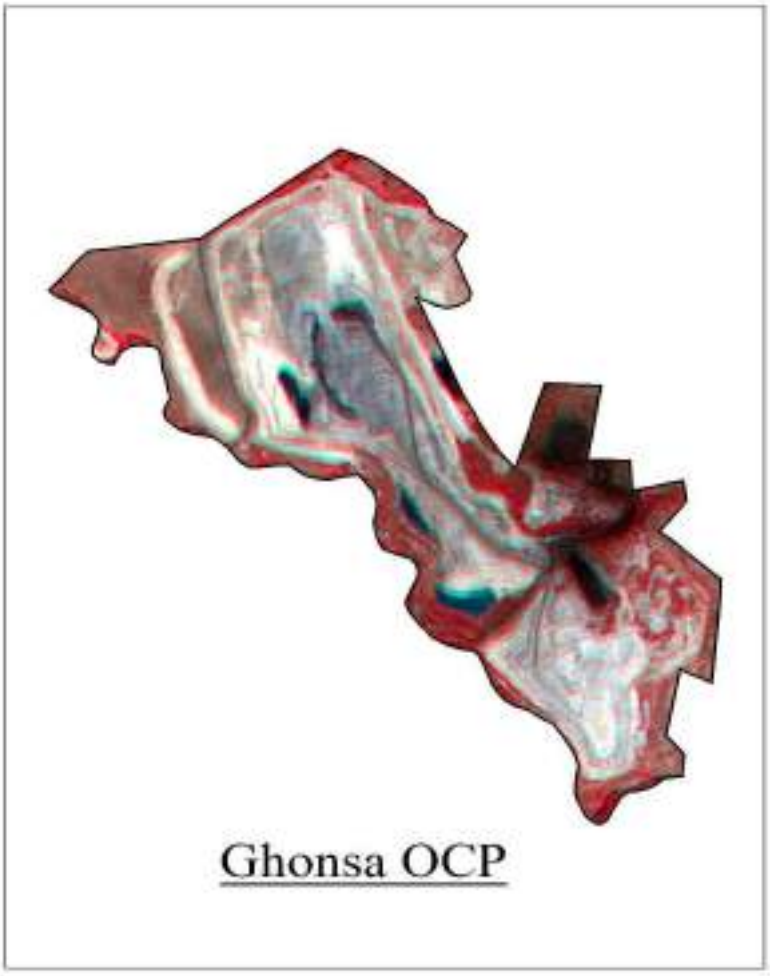

Submitted to

WESTERN COALFIELDS LIMITED

वेस्टर्न कोल्फील्ड्स लिमिटेड के ५ मिलियन घन मीटर (कोल + अधिभार) से कम उत्पादन क्षमतावाले ५ खुली खदानों का भूमि पुनरुद्धार हेतु २०२४ के उपग्रह डाटा के आधार पर निगरानी का प्रतिवेदन

Land Restoration / Reclamation Monitoring of 5 opencast projects of Western Coalfield Limited producing less than 5 million Cu. M. (Coal+OB) per annum based on Satellite Data of the Year 2024

March-2025

Remote Sensing Cell
Geomatics Division
CMPDI, Ranchi

Document Control Sheet

(1) Job No.	564924124
(2) Publication Date	March 2025
(3) Number of Pages	38
(4) Number of Figures	08
(5) Number of Tables	03
(6) Number of Plates	5
(7) Title of Report	Land Restoration / Reclamation Monitoring of Open Cast of Western Coalfields Ltd producing Less than 5 million Cu.m. (Coal+OB) Based on Satellite Data for the Year 2024
(8) Aim of the Report	To prepare land use/cover map of leasehold area of 05 opencast projects based on high resolution satellite data (IRSR2-L4FX) of the year 2024 using digital image processing technique.
(9) Executing Unit	Remote Sensing Cell, Geomatics Division, Central Mine Planning & Design Institute Limited, Gondwana Place, Kanke Road, Ranchi 834008
(10) User Agency	Western Coalfields Ltd., Nagpur, Maharashtra.
(11) Author	1) Swabhiman Dehariya, Asst. Manager (Mining/Geomatics) 2) Tilak Mondal, Chief Manager (E&M /Geomatics)
(12) Security Restriction	Restricted Circulation
(13) No. of Copies	5
(14) Distribution Statement	Official

CONTENTS

कार्यकारी सारांश *v-vi*

Executive Summary *vii-viii*

1.0 Background 1

2.0 Objective 2

3.0 Methodology 2

4.0 Land Reclamation in WCL 6

List of Tables

Table-1 Project wise Land Reclamation Status *ix*

Table-1.1 Composite land reclamation status *x*

Table-2 Area Statistics of Land Use Classes in OC Mines 8

List of Plates

Plate-1 Land Use Map of Gauri Deep OCP 9

Plate-2 Land Use Map of Ghonsa OCP 10

Plate-3 Land Use Map of Kolegaon OCP 11

Plate-4 Land Use Map of Urdhan OCP 12

Plate-5 Land Use Map of Chhinda OCP 13

List of Figures

Figure-1 Bar-Chart of Project wise Status *xi*

Figure-2 Pie Chart of total Excavated area in WCL OCP Mines xii

Figure-3 Methodology of Land Reclamation Monitoring 03

Figure-4 Bar-Chart of Land Reclamation Status of Gauri Deep OCP 14

Figure-5 Bar-Chart of Land Reclamation Status of Ghonsa OCP 14

Figure-6 Bar-Chart of Land Reclamation Status of Kolegaon OCP 15

Figure-7 Bar-Chart of Land Reclamation Status of Urdhan OCP 15

Figure-8 Bar-Chart of Land Reclamation Status of Chhinda OCP 16

List of Photographs

Photograph-1	Social Forestry Plantation in Gauri Deep OCP	17
Photograph-2	Plantation on Barren OB Dump in Chhinda OCP	17
Photograph-3	Social Forestry Plantation in Kolegaon OC	18
Photograph-4	Plantation on OB dump in Urdhan OCP	18
Photograph-5	Plantation on OB in Chhinda OCP	19

शब्द-कोष 20

Abbreviations 22

Glossary 23

कार्यकारी सारांश

१.० परियोजना वेस्टर्न कोल्फील्ड्स लिमिटेड के ५ मिलियन घन मीटर (कोल+ अधिभार) से कम उत्पादन क्षमतावाले ५ खुली खदानों के पुनरुद्धार हेतु वर्ष २०२४ के उपग्रह डाटा पर आधारित तीन साल के अन्तराल पर सलाना नियमित निगरानी।

२.० उद्देश्य भूमि पुनरुद्धार (लैंड रिक्लेमेशन) का उद्देश्य कुल पट्टाक्षेत्र में बैकफील, वृक्षारोपण, सामाजिक वानिकी, सक्रिय खनन क्षेत्र, जल निकाय (वाटर ड्रेनेज), बंजर भूमि, कृषि भूमि और जंगल के विभिन्न प्रकार के वितरण प्रणाली के क्षेत्र का आकलन करने के लिए है। यह अध्ययन उपरोक्त सभी खुली खदानों के भूमि पुनरुद्धार (लैंड रिक्लेमेशन) का निगरानी के प्रगति का आकलन करने में मदद करेगा तथा इसके अतिरिक्त पर्यावरण संरक्षण के लिए आवश्यक उपचारात्मक उपायों को क्रियान्वित करने में भी सहायता करेगा।

३.० मुख्य निष्कर्ष

- वर्ष २०२४-२५ में कुल ०५ खुली खदान परियोजनाओं में भूमि सुधार की स्थिति की निगरानी पर विचार किया गया है। (<5 एमसीएम कोयला+ओबी)

- वर्ष २०२४-२५ में भूमि पुनरुद्धार (लैंड रिक्लेमेशन) हेतु चयन किये गए कुल ०५ खुली खदान परियोजनाओं यथा: कोलेगांव, घोंसा, उर्धन, गौरी डीप छिंदा का कुल पट्टाक्षेत्र अथवा माइन लीज होल्ड एरिया १४३६.९८ हेक्टेयर है जिसमें ३७४.९८ हेक्टेयर उत्खनन क्षेत्र के अंतर्गत है तथा २५.६७ हेक्टेयर (६.८५%) क्षेत्र में तकनीकी पुनरुद्धार (बैकफीलिंग) का कार्य प्रगति पर है और शेष ३४९.३१ हेक्टेयर (९३.१५%) क्षेत्र सक्रिय खनन के अन्तर्गत है। विश्लेषण से यह स्पष्ट है कि वर्ष २०२४-२५ के लिए कोई जैविक पुनरुद्धार यानी बैकफिल पर वृक्षारोपण नहीं किया गया है। परियोजनावार भूमि पुनरुद्धार (लैंड रिक्लेमेशन) के निगरानी का वर्णन विस्तार रूप से तालिका संख्या ०१, बार चार्ट चित्र संख्या ०१ में दर्शाया गया है ।

- डब्ल्यूसीएल में पिछले चक्र अध्ययन के संबंध में वर्ष २०२४-२५ में ५ ओसी परियोजनाओं के लिए किए गए भूमि सुधार की स्थिति की तुलना करने पर यह स्पष्ट है कि भूमि पुनरुद्धार (लैंड रिक्लेमेशन) के तहत आनेवाले क्षेत्र का क्षेत्रफल वर्ष २०२३-२४ के १६.५१ हेक्टेयर की तुलना में वर्ष २०२४-२५ में बढ़कर २५.९३ हेक्टेयर हो गया है जिसमें (बैकफ़िल पर वृक्षारोपण) जैविक पुनरुद्धार और (बैकफ़िलिंग के तहत क्षेत्र) तकनीकी पुनरुद्धार दोनों शामिल हैं। तीन वर्षों की अवधि में भूमि पुनरुद्धार क्षेत्र में ९.४२ हेक्टेयर की यह वृद्धि डब्ल्यूसीएल द्वारा भूमि पुनरुद्धार की दिशा में किए गए प्रयासों का परिणाम है। विभिन्न ओसी परियोजनाओं में भूमि सुधार की वर्षवार तुलना तालिका-१ में दी गई है।

- तालिका 1.1 में डब्ल्यूसीएल (<5 एमसीएम कोयला+ओबी) की शेष खानों में भूमि पुनरुद्धार (लैंड रिक्लेमेशन) सामूहिक रूप से दर्शाया गया हे।

- कुल वृक्षारोपण (हरित आवरण), बैकफ़िल पर किए गए वृक्षारोपण, बंजर अधिभार डंप पर किए गए वृक्षारोपण, सामाजिक वानिकी के तहत किए वृक्षारोपण के तहत आने वाले क्षेत्र का क्षेत्रफल वर्ष २०२३-२४ में १७१.८२ हेक्टेयर से बढ़कर वर्ष २०२४-२५ में २२३.४३ हेक्टेयर हो गया है।

Executive Summary

1.0 Project

Land restoration / reclamation monitoring of 5 opencast coal mines of Western Coalfields Ltd. (WCL) producing less than 5 million cu.m. (Coal+OB) per year based on satellite data, at an interval of three years.

2.0 Objective

Objective of land restoration / reclamation monitoring is to assess the area of backfilled, plantation, social forestry, active mining area, water bodies, distribution of wasteland, agricultural land and forest in the leasehold area of the projects. This will help in assessing the progressive status of mined land reclamation and to take up remedial measures, if any, required for environmental protection.

3.0 Salient Findings

- Total 5 no. of OC projects have been considered for monitoring the status of land reclamation in the year 2024-25

- Out of the total mine leasehold area of 1436.98 Hectare of the 5 OC projects Viz. Gauri Deep, Ghonsa, Kolegaon, Urdhan, and Chhinda considered for monitoring during the year 2024-25; total excavated area is only 374.98 Ha out of which 25.67 Ha area (6.85%) is under backfilling (Technically Reclaimed) and 349.31 Ha (93.15%) area is under active mining. It is evident from the analysis that there is no biological reclamation i.e. plantation on backfill for the year 2024-25. Project wise details are given in Table-1 & bar chart Fig1.

- On comparing the status of land reclamation carried out for 5 nos of OC projects in year 2024-25 with respect to previous cycle study

in WCL, it is evident from analysis that area under land reclamation has increased from 16.51 Hectares (Yr 2023-24) to 25.93 Hectares (Yr 2024-25) which includes both planation on backfill (Biological Reclamation) and area under backfilling (Technical Reclamation). This increase of 9.42 Hectares area of land reclamation in a period of three years is the result of the efforts made by WCL towards land reclamation. Year wise comparison in land reclamation in different OC projects is given in Table-1.

- Table 1.1 Show the Composite land reclamation status in remaining mines of WCL (<5 MCM Coal+OB) as per clause 2.(ii) of the received work order from CIL.

- Overall, total area under plantation (green cover) carried out on backfill, barren OB dump and plantation under social forestry has gone up from 171.82 Hectares in the year 2023-24 to 223.43 Hectares in the year 2024-25.

Table-1

Project wise Land Reclamation Status in Opencast Projects of WCL (<5 MCM Coal+OB) based on Satellite Data of the year 2024-25

(Area in Hectare)

Sl.No.	Project	Total Leasehold Area		Technical Reclamation		Plantation						Area under Active Mining		Total Excavated Area		Total Area under Plantation (% Green Cover Generated in Leasehold)		Total Area under Reclamation	
						Biological Reclamation		Other Plantations											
				Area under Backfilling		Plantation on Excavated / Backfilled Area		Plantation on External Over Burden Dumps		Social Forestry, Avenue Plantation Etc.									
1	2	3		4		5		6		7		8		9 (=4+5+8)		10 (=5+6+7)		11(=4+5)	
		2023	2024	2023	2024	2023	2024	2023	2024	2023	2024	2023	2024	2023	2024	2023	2024	2023	2024
1	Gaun Deep	339.10	339.10	0.00	0.00	0.00	0.00	0.00	14.46	8.00	10.42	62.77	70.94	62.77	70.94	8.00	24.88	0.00	0.00
				0.00%	0.00%	0.00%	0.00%					100.00%	100.00%			2.36%	7.34%	0.00%	0.00%
2	Ghonsa	278.68	278.68	11.59	18.29	0.00	0.00	5.51	8.61	6.54	10.80	98.39	118.12	109.98	136.41	12.05	19.41	11.59	18.29
				10.54%	13.41%	0.00%	0.00%					89.46%	86.59%			4.32%	6.04%	10.54%	13.41%
3	Kolegaon	397.52	397.52	0.00	0.00	0.00	0.00	83.45	96.67	24.11	29.70	67.64	82.78	67.64	82.78	107.56	126.37	0.00	0.00
				0.00%	0.00%	0.00%	0.00%					100.00%	100.00%			27.06%	31.79%	0.00%	0.00%
4	Urdhan	315.00	315.00	4.70	7.38	0.00	0.00	10.15	15.44	9.02	11.13	38.06	50.96	42.76	58.34	19.17	26.57	4.70	7.38
				10.99%	12.65%	0.00%	0.00%					89.01%	87.35%			6.09%	8.43%	10.99%	12.65%
5	Chanda	106.68	106.68	0.00	0.00	0.00	0.00	20.11	20.74	4.30	4.68	23.81	26.51	23.81	26.51	24.41	25.42	0.00	0.00
				0.00%	0.00%	0.00%	0.00%					100.00%	100.00%			22.88%	23.83%	0.00%	0.00%
	Total (A)	**1436.98**	**1436.98**	**16.29**	**25.67**	**0.00**	**0.00**	**119.22**	**155.92**	**51.97**	**66.73**	**290.67**	**349.31**	**306.96**	**374.98**	**171.82**	**223.43**	**16.51**	**25.93**
		A		5.31%	6.85%	0.00%	0.00%					94.69%	93.15%			11.96%	15.55%	5.38%	6.92%

(%) calculated is in respect to Total Excavated Area as applicable

Note: In reference of the above Table, different parameters are classified as follows:

1. Area under Biological Reclamation includes Areas under Plantation done on Backfilled Area Only.
2. Area under Technical Reclamation includes Area under Barren Backfilling only.
3. Area under Active Mining Includes Coal Quarry, Advance Quarry Site and Quarry filled with water etc., if any.
4. Social Forestry and Plantation on External OB Dumps are not included in Biological Reclamation and are put under separate categories as shown in the above Table.
5. (%) calculated in the above Table is in respect to Total Excavated Area except for “Total Area under Plantation” where % is in terms of “Leasehold Area”.

Table-1.1

Composite land reclamation status in remaining mines of WCL (<5 MCM Coal+OB) as per clause 2.(ii) of the received work order from CIL


(Area in Hectare)

Sl.No.	Cluster No.	Total Leasehold Area		Technical Reclamation		Plantation				Area under Active Mining		Total Excavated Area		Total Area under Plantation (% Green Cover Generated in Leasehold)		Total Area under Reclamation	
						Biological		Other Plantations									
				Area under Backfilling		Plantation on Excavated / Backfilled Area		Plantation on External OB Dumps	Social Forestry, Avenue Plantation Etc.								
1	2	3		4		5		6	7	8		9 (=4+5+8)		10 (=5+6+7)		11(=4+5)	
		2022	2023	2022	2023	2022	2023	2022	2023	2022	2023	2022	2023	2022	2023	2022	2023
6	Padmapur OC **	829.00	829.00	59.00	65.00	28.00	28.00	214.00	221.00	83.00	83.00	118.00	112.00	205.00	205.00	325.00	332.00	87.00	93.00
				28.78%	31.71%	13.66%	13.66%					57.56%	54.63%			39.20%	40.05%	42.44%	45.37%
	TOTAL (B)	829.00	829.00	59.00	65.00	28.00	28.00	214.00	221.00	83.00	83.00	118.00	112.00	205.00	205.00	325.00	332.00	87.00	93.00
				28.78%	31.71%	13.66%	13.66%					57.56%	54.63%			39.20%	40.05%	42.44%	45.37%
		2019	2022	2019	2022	2019	2022	2019	2022	2019	2022	2019	2022	2019	2022	2019	2022	2019	2022
7	Singhori OC	425.04	425.04	0.00	0.00	0.00	0.00	0.00	0.00	4.59	7.63	26.82	50.56	26.82	50.56	4.59	7.63	0.00	0.00
				0.00%	0.00%	0.00%	0.00%					100.00%	100.00%			1.08%	1.80%	0.00%	0.00%
8	Makardhokra -II OC	258.23	258.23	44.61	57.75	2.90	0.60	58.76	47.14	2.57	2.57	6.91	0.00	54.42	57.35	64.23	49.71	47.51	57.75
				81.97%	100.00%	5.33%	0.00%					12.70%	0.00%			24.87%	19.25%	87.30%	100.00%
9	New Sethia OC	144.45	144.45	25.99	30.63	23.58	18.92	6.80	7.01	9.53	10.15	40.81	41.65	90.38	91.22	59.91	36.08	49.57	49.57
				28.76%	33.60%	26.09%	20.74%					45.15%	45.66%			27.63%	24.98%	54.85%	54.24%
10	Ghugus OC	1020.00	1020.00	267.70	258.74	53.38	73.22	135.00	136.64	14.91	125.20	35.77	26.89	358.85	358.85	275.29	335.06	323.08	331.96
				0.00%	72.10%	0.00%	20.40%					0.00%	7.49%			26.99%	32.85%	0.00%	92.51%
11	Pimpalgaon OC	451.87	451.87	13.33	13.34	0.00	0.00	136.11	149.76	10.32	79.62	46.25	54.23	59.58	67.57	216.42	229.38	13.33	13.34
				0.00%	19.74%	0.00%	0.00%					0.00%	80.26%			47.90%	50.76%	0.00%	19.74%
	TOTAL (C)	2299.59	2299.59	351.63	360.48	81.86	92.14	336.67	340.55	181.92	225.17	156.56	173.33	590.05	625.95	600.45	657.86	433.49	452.62
				59.59%	57.59%	13.87%	14.72%					26.53%	27.69%			26.11%	28.61%	72.47%	71.31%
		2018	2021	2018	2021	2018	2021	2018	2021	2018	2021	2018	2021	2018	2021	2018	2021	2018	2021
12	Shivpuri OC	336.29	336.29	17.98	44.97	6.06	10.15	20.41	20.93	16.55	23.91	47.31	35.14	71.35	90.26	45.00	54.99	24.04	55.12
				25.20%	49.83%	8.49%	11.25%					66.31%	38.93%			12.79%	16.35%	33.69%	61.07%
13	Ghorawar OC	1296.01	1296.01	32.06	42.76	8.92	16.24	27.60	27.61	14.42	14.84	23.07	38.10	64.03	97.10	50.95	58.76	40.98	59.00
				50.05%	44.04%	13.93%	16.73%					36.02%	39.24%			3.93%	4.53%	63.98%	60.76%
14	Barkuhi OC	237.51	237.51	13.84	15.64	0.00	0.00	0.00	0.00	8.73	8.81	18.69	18.01	32.53	33.65	8.73	8.81	13.84	15.64
				42.55%	46.48%	0.00%	0.00%					57.45%	53.52%			3.68%	3.71%	42.52%	46.48%
15	Ambara OC	162.15	162.15	45.34	45.67	13.51	13.84	0.00	0.00	10.55	10.91	21.50	26.55	80.35	86.06	24.06	24.75	58.85	59.51
				56.43%	53.07%	16.81%	16.08%					26.76%	30.82%			14.84%	15.26%	73.24%	69.15%
	TOTAL (D)	2031.96	2031.96	109.22	149.04	28.49	40.23	48.01	48.61	50.24	58.47	130.57	117.80	248.28	307.07	126.74	147.31	137.71	189.27
				43.99%	48.54%	11.47%	13.10%					41.63%	38.36%			6.24%	7.25%	55.47%	61.64%
	*GRAND TOTAL (A+B+C+D)	6597.53	6597.53	536.14	600.19	138.35	160.37	717.90	766.08	367.13	433.37	675.80	752.44	1350.29	1513.00	1224.01	1360.60	674.71	760.82
				39.71%	39.67%	10.25%	10.60%					50.05%	49.73%			18.55%	20.62%	49.97%	50.29%


*Grand Total (A+B+C+D) is the composite value of all 15 mines of WCL covered in 3 years cycle of Land Reclamation Monitoring

(% is calculated with respect to Excavated Area as applicable)

** The Land Reclamation Monitoring for this mine was previously conducted under the category of more than 5 MTY capacity. For normalized calculations, the data from this mines has been converted from Sq.Kms to Ha.

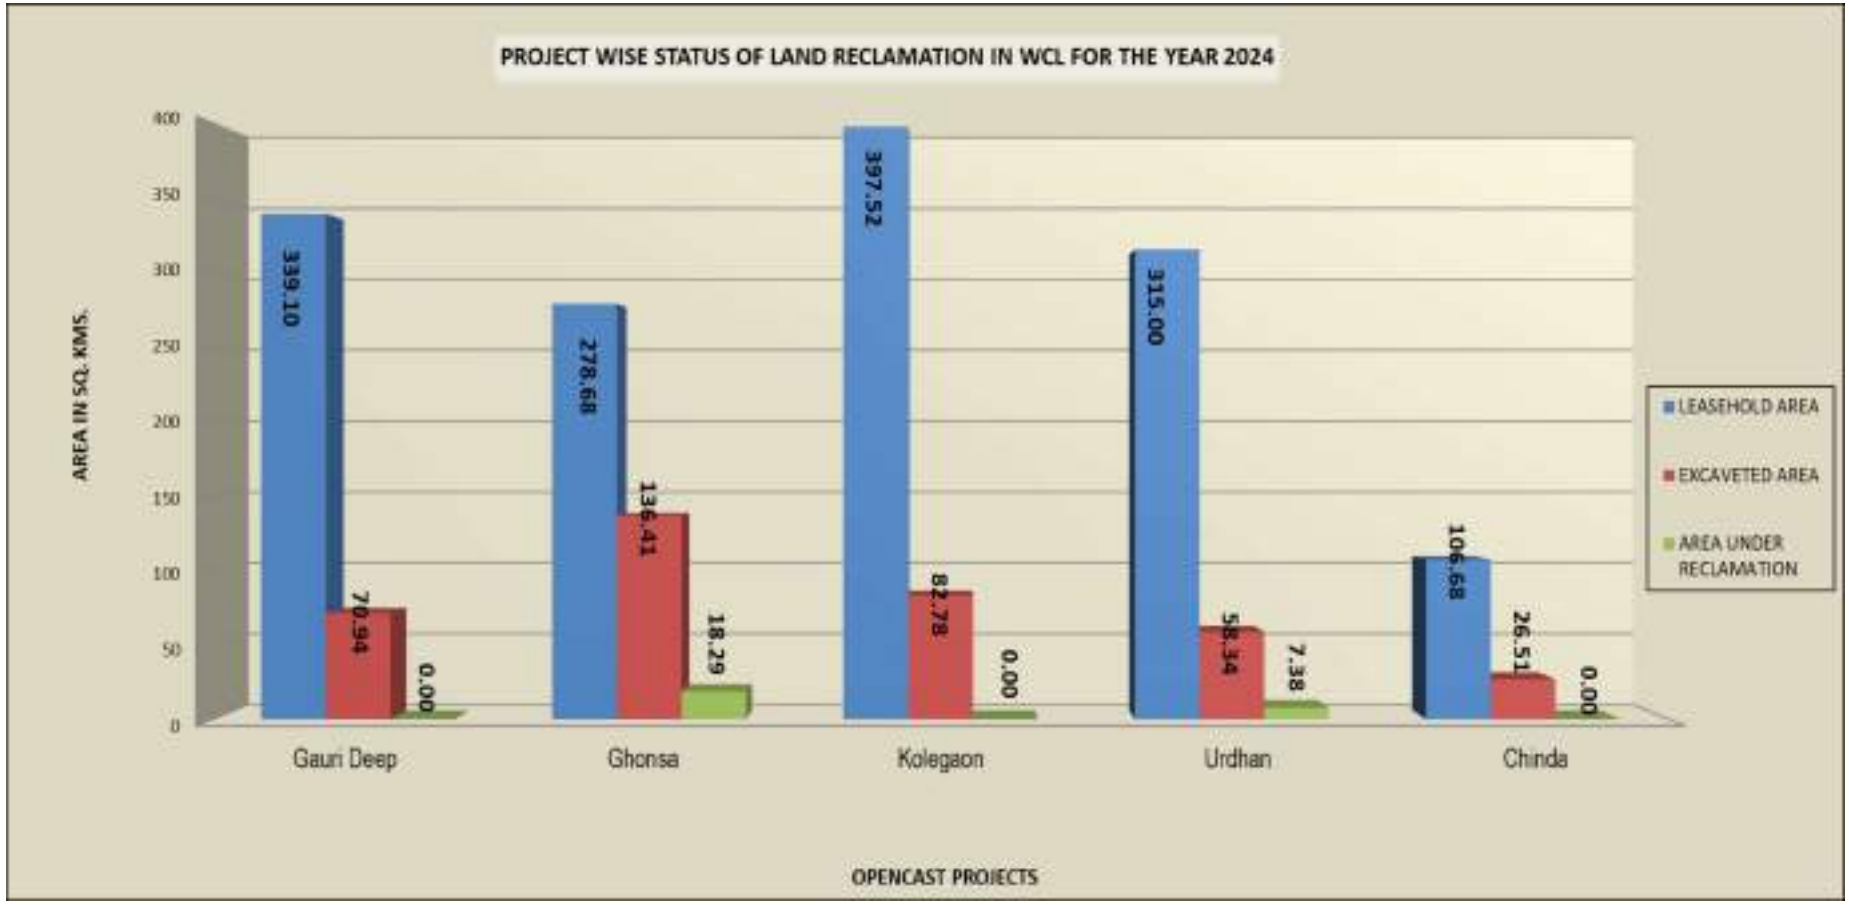

Flg.1: Land Reclamation Status in OC projects producing less than 5mcm (Coal +OB) of WCL in the Year 2024

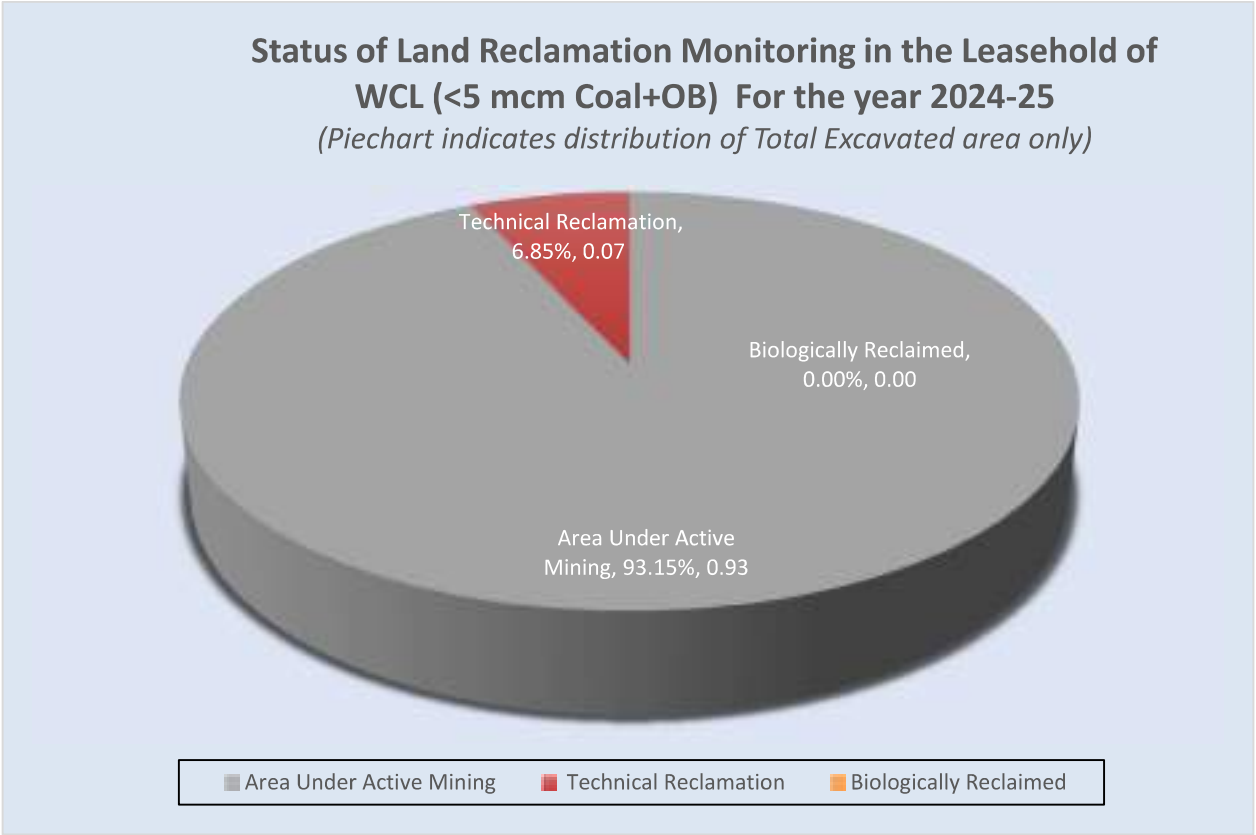

Flg.2: Land Reclamation Status of Total Excavated area in OC projects of WCL (<5 MCM Coal+OB) in the Year 2024

1.0 Background

1.1 Land is the most important natural resource which embodies soil, water, flora fauna and total ecosystem. All human activities are based on the land which is the most scarce natural resource in our country. Mining is a site specific industry and it could not be shifted anywhere else from the location where mineral occurs. It is a fact that surface mining activities do effect the land environment due to ground breaking. Therefore, there is an urgent need to reclaim and restore the mined out land for its productive use for sustainable development of mining. This will not only mitigate environmental degradation, but would also help in creating a more congenial environment for land acquisition by coal companies in future.

1.2 Keeping above in view, Coal India Ltd. (CIL) issued a work order vide letter no. CIL/WBP/Env/2009/2478 dated 29.12.2009 to Central Mine Planning & Design Institute (CMPDI), Ranchi, for monitoring land reclamation status of all the opencast coal mines having production of less than 5 million m^3 per annum (coal + OB taken together per annum) based on remote sensing satellite data regularly on annual basis and less than 5 million m^3 per annum (coal + OB taken together per annum) at interval of three years based on remote sensing satellite data, for sustainable development of mining. A revised work order was issued vide letter no.CIL /WBP/Env/2011/4706 dated 12.10.2012 from Coal India Ltd for the period 2012-13 to 2016-2017.which was subsequently followed by another work order vide letter no: CIL/WBP/Env/2017/DP/8477 dated 21.09.2017 from coal India ltd for period 2017-18 to 2021-22. Further, a revised work order was issued vide letter no. CIL/ENVT/2022-23/W.O/10899 dated 06.07.2022 from Coal India Limited for the period 2022-23 to 2023-24. Again the above work order has been renewed vide letter no. CIL/ ENV/11463 dated 03.07.2024 for a period of 3 more years for 2024-25, 2025-26 and 2026-27. The result of land reclamation status of all such mines to be put on the website of CIL, (www.coalindia.in), CMPDI (www.cmpdi.co.in) and the

concerned coal companies in public domain. Detail report to be submitted to Coal India and respective subsidiaries.

1.3 Land reclamation monitoring of all opencast coal mining projects would also comply the statutory requirements of Ministry of Environment, Forest & Climate Change (MoEF & CC). Such monitoring would not only facilitate in taking timely mitigation measures against environmental degradation, but would also enable coal companies to utilize the reclaimed land for larger socio-economic benefits in a planned way.

1.4 Present report is embodying the finding of the study based on satellite data of the year 2024 carried out for the 5 OC projects producing less than 5 mcm (Coal+OB) for Western Coalfields Ltd.

2.0 Objective

Objective of the land reclamation/restoration monitoring is to assess the area under backfilling, plantation, OB dumps, social forestry, active mining area, settlements, water bodies, distribution of wasteland, agricultural land and forest land in the leasehold area of the project. This is an important step taken up for assessing the progressive status of mined land reclamation and for taking up remedial measures, if any, required for environmental protection.

3.0 Methodology

There are number of steps involved between raw satellite data procurement and preparation of final map. Bhoonidhi Portal of ISRO alongside National Remote Sensing Centre (NRSC) Hyderabad, being the nodal agency for satellite data supply in India, provides only raw digital satellite data, which needs further digital image processing for extracting the information and map preparation before uploading the same in the website. Methodology for land reclamation monitoring is given in given in figure-3. Following steps are involved in land reclamation /restoration monitoring:

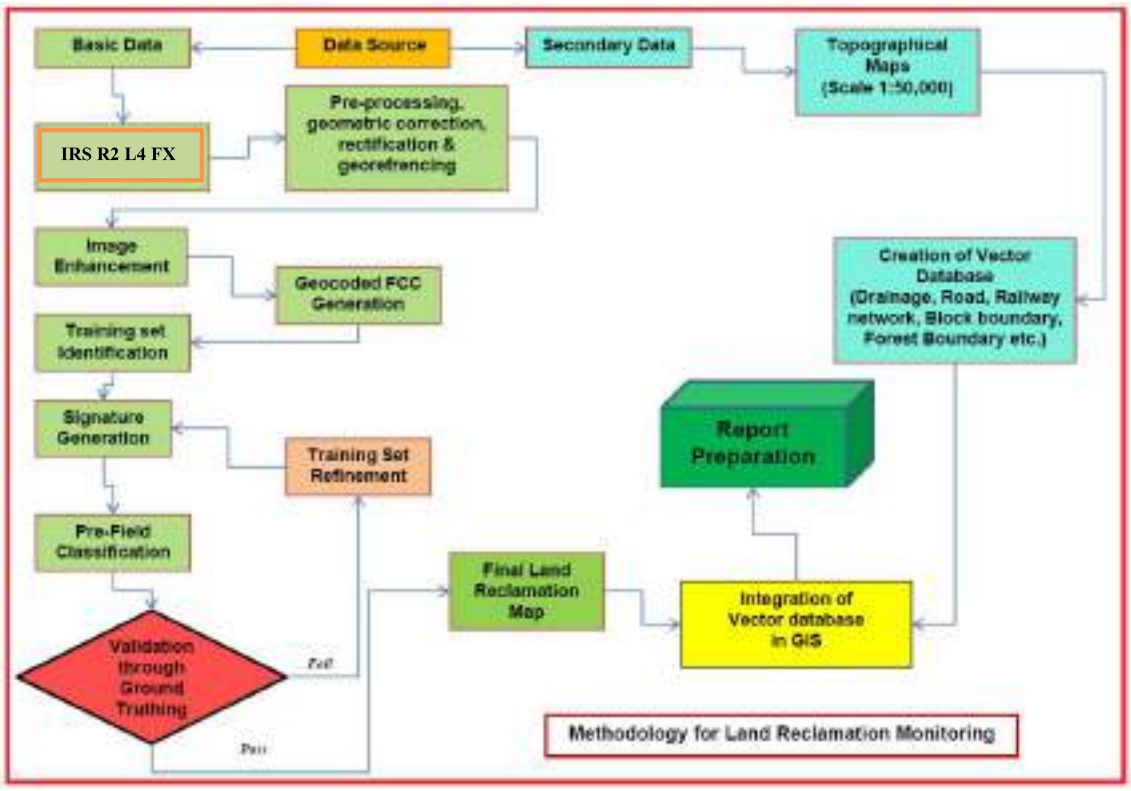


Figure :3 Methodology for Land Reclamation Monitoring

3.1 Data Procurement: After browsing the data quality and date of pass on internet, supply order for data is placed to NRSC or if available downloaded directly from the Bhoonidhi portal. Secondary data like leasehold boundary, topo sheets are procured for creation of vector database.

3.2 Satellite Data Processing: Satellite data are processed using ERDAS IMAGINE version 2022 digital image processing s/w & ArcMap10.8 s/w. Methodology involves the following major steps:

- **Rectification & Geo-referencing:** Inaccuracies in digital imagery may occur due to 'systematic errors' attributed to earth curvature and rotation as well as 'non-systematic errors' attributed to satellite receiving station itself. Raw digital images contain geometric distortions, which make them unusable as maps. Therefore, geo-

referencing is required for correction of image data using ground control points (GCP) to make it compatible to SoI toposheet.

- **Image enhancement:**

  To improve the interpretability of the raw data, image enhancement is necessary. local operations modify the value of each pixel based on brightness value of neighbouring pixels using ERDAS IMAGINE 2022 s/w. and enhance the image quality for interpretation.

- **Training set selection**

  Training set requires to be selected, so that software can classify the image data accurately. The image data are analysed based on the interpretation keys. These keys are evolved from certain fundamental image-elements such as tone/colour, size, shape, texture, pattern, location, association and shadow. Based on the image-elements and other geo-technical elements like land form, drainage pattern and physiography; training sets were selected/identified for each land use/cover class. Field survey was carried out by taking selective traverses in order to collect the ground information (or reference data) so that training sets are selected accurately in the image. This was intended to serve as an aid for classification.

- **Classification and Accuracy assessment**

  Image classification is carried out using the maximum likelihood algorithm. The classification proceeds through the following steps: (a) calculation of statistics [i.e. signature generation] for the identified training areas, and (b) the decision boundary of maximum probability based on the mean vector, variance, covariance and correlation matrix of the pixels. After evaluating the statistical parameters of the training sets, reliability test of training sets is conducted by measuring the statistical separation between the classes that resulted from computing divergence matrix. The overall accuracy of the classification was finally assessed with reference to ground truth data.

- **Area calculation**

  The area of each land use class in the leasehold is determined using ERDAS IMAGINE v. 2022 software.

- **Overlay of Vector data base**

  Vector data base created based on secondary data. Vector layer like drainage, railway line, leasehold boundary, forest boundary etc. are superimposed on the image as vector layer in the Arc GIS database.

- **Pre-field map preparation**

  Pre-field map is prepared for validation of the classification result

3.3 Ground Truthing:

Selective ground verification of the land use classes is carried out in the field and necessary corrections if required, are incorporated before map finalization.

3.4 Land reclamation database on GIS:

Land reclamation database is created on GIS platform to identify the temporal changes identified from satellite data of different cut-of dates.

4.0 Land Reclamation Status in Western Coalfields Ltd.

4.1 Following 5 opencast projects producing less than 5 million cubic m. (Coal + OB) together of Western Coalfields Ltd. have been taken up for land reclamation monitoring during the year 2024-25:

- Gouri Deep
- Ghonsa
- Kolegaon
- Urdhan
- Chhinda

4.2 Area statistics of different land use class present in the mine leasehold of the above projects for the year 2024 are shown in the Table - 2. Land use maps derived from satellite data of year 2024 are shown in Plate 1 - 5. This time both local grid and UTM grid is used for map preparation along with all essential boundaries shape file such as Quarry limit line, Sump, OB Dump, EC Boundary, Plantation area etc. as per the work order from CIL. Changes in the different land use classes based on satellite data are depicted in Bar Charts in Fig. 4- 8.

4.3 Study reveals that out of total mine leasehold area of 1436.98 Hectare of the 5 projects viz, Gauri Deep, Ghonsa, Kolegaon, Urdhan and Chhinda considered for monitoring during year 2024-25; total excavated area is 374.98 Ha, out of which 25.67 Ha (6.85%) area is under backfilling (Technically Reclaimed) and balance 349.31 Ha (93.15%) area is under active mining. It is evident from analysis that there is no biological reclamation i.e. plantation on backfill. Project wise details area given in Table 1.

4.4 From analysis it is revealed that total area under technical reclamation (area under backfilling) has also increased from 16.29 Ha (5.31%) in the year 2023 to 25.67 Ha (6.85%) area in the year 2024.

4.5 Study indicates that overall the projects of WCL considered for this study indicate increase in technical reclamation i.e. area under backfilling.


4.6 After analyzing the satellite data of year 2023 vs. 2024 it is evident that total area under plantation (Green cover) carried out under social forestry in above OC mines of WCL has increased from 171.82 Ha (Year 2023) to 223.43 Ha (Year 2024) in the span of one years. This increase of 51.61 Ha area under total plantation in one-year time is due to the sincere efforts made by WCL towards generation of green cover in leasehold area of the 5 opencast projects considered for land reclamation in the year 2024-25.

4.7 Out of 5 projects of WCL, maximum land reclamation has been carried out in Ghonsa OCP (13.41%) followed by Urdhan OCP (12.65%).

Table 2:
Status of Land Use/Reclamation in OC Mines (<5 M.Cu.M) Of Western Coalfield Ltd based on Satellite Data of the Year 2024

(Area in Hectare)

		Gauri Deep		Ghonsa		Kolegaon		Urdhan		Chhinda		Total	
		Area	%	Area	%	Area	%	Area	%	Area	%	Area	%
FORESTS	Dense Forest	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
	Open Forest	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
	Total Forest	0.00	0.00	0.00	0.00	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**	**0.00**
SCRUBS	Scrubs	**31.69**	**9.35**	**46.72**	**16.76**	**26.08**	**6.56**	**22.96**	**7.29**	**10.28**	**9.64**	**137.73**	**9.58**
PLANTATION	Social Forestry	10.42	3.07	10.80	3.88	29.70	7.47	11.13	3.53	4.68	4.39	62.05	4.32
	Plantation on OB Dump	14.46	4.26	8.61	3.09	96.67	24.32	15.44	4.90	20.74	19.44	155.92	10.85
	Plantation on Backfill (Biological Reclamation)	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
	Total Plantation	**24.88**	**7.34**	**19.41**	**6.96**	**126.37**	**31.79**	**26.57**	**8.43**	**25.42**	**23.83**	**222.65**	**15.49**
	Total Vegetation	**56.57**	**16.68**	**66.13**	**23.73**	**152.45**	**38.35**	**49.53**	**15.72**	**35.70**	**33.46**	**360.38**	**25.08**
ACTIVE MINING	Coal Quarry	64.34	18.97	104.75	37.59	72.84	18.32	37.04	11.76	25.22	23.64	304.19	21.17
	Coal Dump	6.60	1.95	7.32	2.63	4.71	1.18	12.79	4.06	0.83	0.78	32.25	2.24
	Advance Quarry Site	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
	Quarry Filled With Water	0.00	0.00	6.05	2.17	5.23	1.32	1.13	0.36	0.46	0.43	12.87	0.90
	Total Area under *Active Mining*	**70.94**	**20.92**	**118.12**	**42.39**	**82.78**	**20.82**	**50.96**	**16.18**	**26.51**	**24.85**	**349.31**	**24.31**
	Barren OB Dump	92.93	27.40	20.52	7.36	71.49	17.98	76.81	24.38	15.96	14.96	277.71	19.33
	Barren Backfilled Area (Technical Reclamation)	0.00	0.00	18.29	6.56	0.00	0.00	7.38	2.34	0.00	0.00	25.67	1.79
	Total Area	**92.93**	**27.40**	**38.81**	**13.93**	**71.49**	**17.98**	**84.19**	**26.73**	**15.96**	**14.96**	303.38	21.11
	Total Area Under Mine Operation	**163.87**	**48.32**	**156.93**	**56.31**	**154.27**	**38.81**	**135.15**	**42.90**	**42.47**	**39.81**	**652.69**	**45.42**
WASTE LANDS	Waste Lands	13.11	3.87	34.12	12.24	44.62	11.22	14.84	4.71	2.35	2.20	109.04	7.59
	Fly Ash Pond / Sand Body	0.24	0.07	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.24	0.02
	Total Wasteland	**13.35**	**3.94**	**34.12**	**12.24**	**44.62**	**11.22**	**14.84**	**4.71**	**2.35**	**2.20**	**109.28**	**7.60**
WATERBODIES	Reservoir, nallah, ponds	1.70	0.50	0.33	0.12	0.93	0.23	0.00	0.00	0.00	0.00	2.96	0.21
	Total Waterbodies	**1.70**	**0.50**	**0.33**	**0.12**	**0.93**	**0.23**	**0.00**	**0.00**	**0.00**	**0.00**	2.96	0.21
AGRICULTURE	Crop Lands	2.94	0.87	0.00	0.00	0.00	0.00	25.00	7.94	1.56	1.46	29.50	2.05
	Fallow Lands	99.48	29.34	20.39	7.32	42.50	10.69	87.34	27.73	23.54	22.07	273.25	19.02
	Total Agriculture	**102.42**	**30.20**	**20.39**	**7.32**	**42.50**	**10.69**	**112.34**	**35.66**	**25.10**	**23.53**	**302.75**	**21.07**
SETTLEMENTS	Urban Settlement	0.53	0.16	0.08	0.03	0.98	0.25	0.92	0.29	1.06	0.99	3.57	0.25
	Rural Settlement	0.00	0.00	0.00	0.00	0.00	0.00	1.67	0.53	0.00	0.00	1.67	0.12
	Industrial Settlement	0.66	0.19	0.70	0.25	1.77	0.45	0.55	0.17	0.00	0.00	3.68	0.26
	Total Settlement	**1.19**	**0.35**	**0.78**	**0.28**	**2.75**	**0.69**	**3.14**	**1.00**	**1.06**	**0.99**	8.92	0.62
	Grand Total	**339.10**	**100.00**	**278.68**	**100.00**	**397.52**	**100.00**	**315.00**	**100.00**	**106.68**	**100.00**	**1436.98**	**100.00**

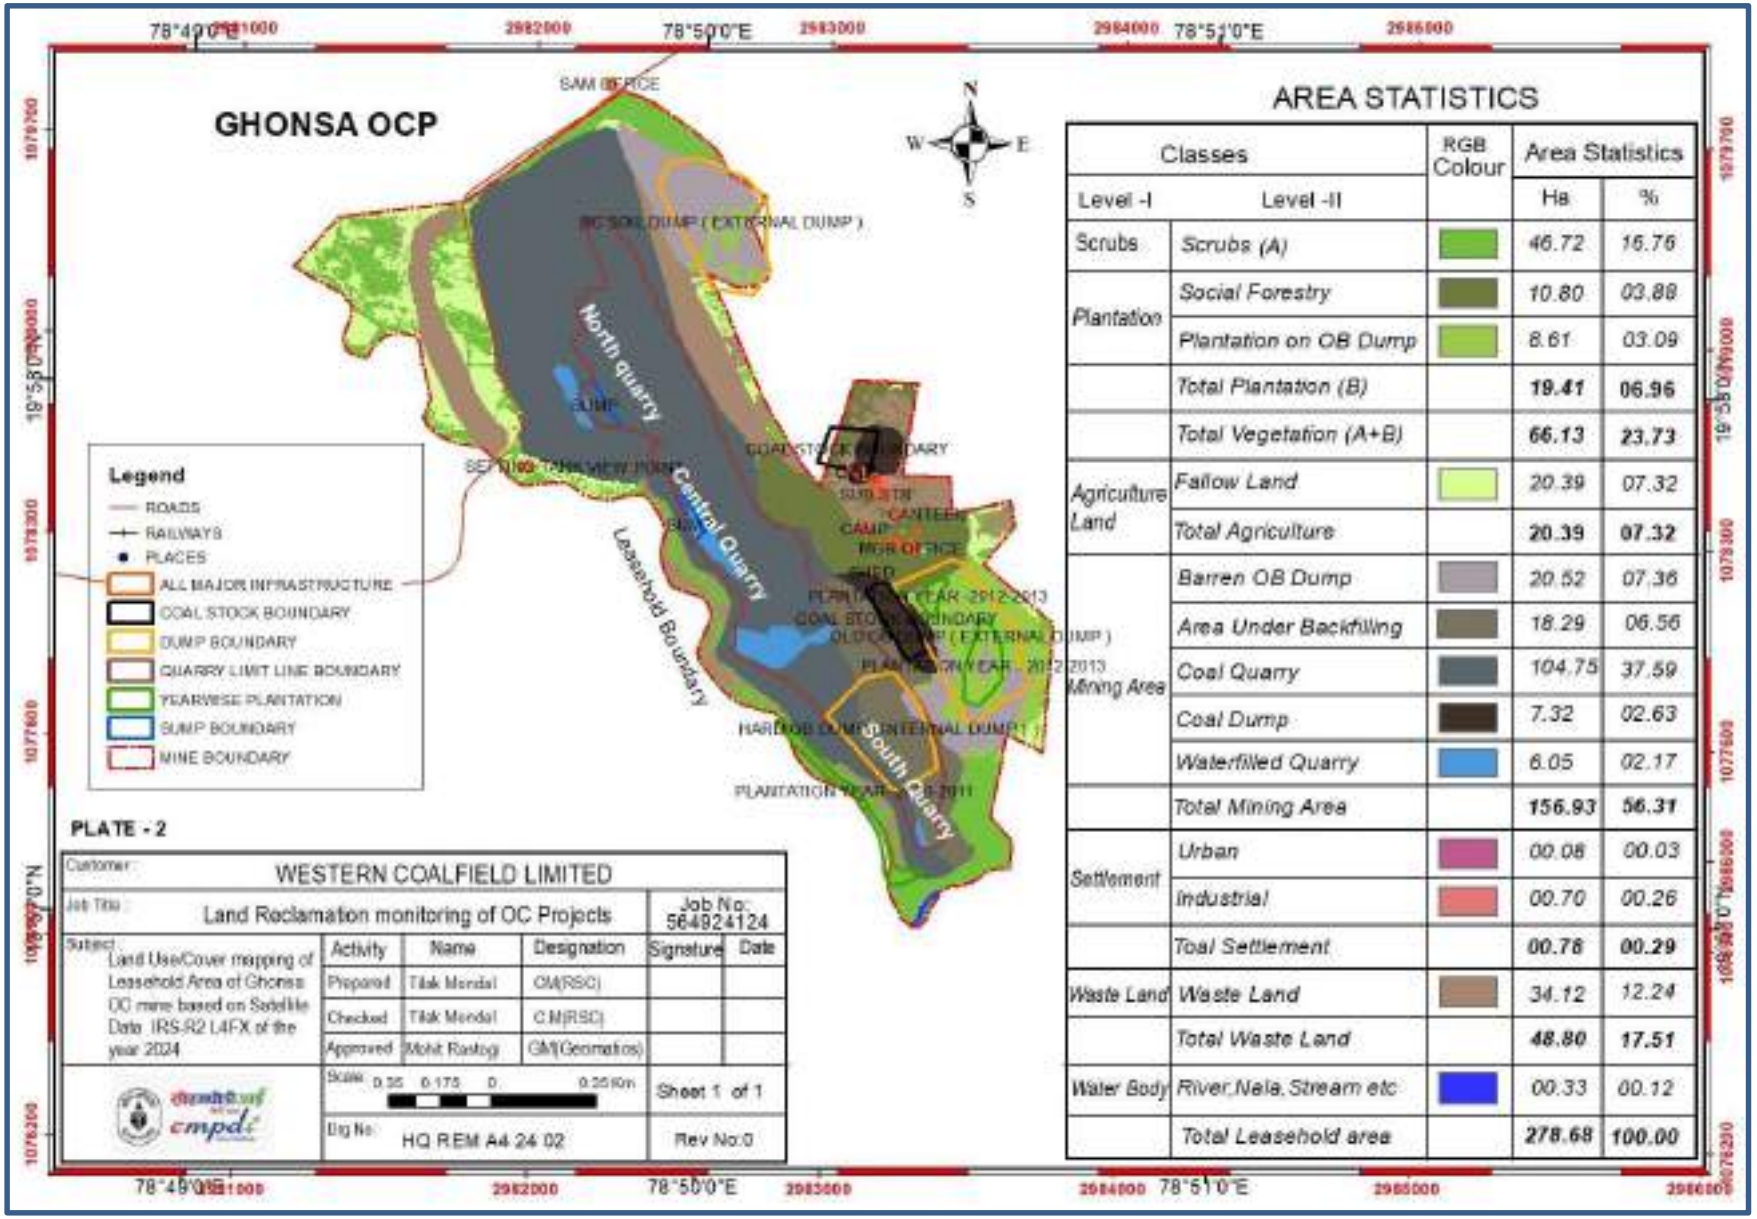

AREA STATISTICS

Classes		RGB Colour	Area Statistics	
Level -I	Level -II		Ha	%
Scrubs	Scrubs (A)		46.72	16.76
Plantation	Social Forestry		10.80	03.88
	Plantation on OB Dump		8.61	03.09
	Total Plantation (B)		**19.41**	**06.96**
	Total Vegetation (A+B)		**66.13**	**23.73**
Agriculture Land	Fallow Land		20.39	07.32
	Total Agriculture		**20.39**	**07.32**
Mining Area	Barren OB Dump		20.52	07.36
	Area Under Backfilling		18.29	06.56
	Coal Quarry		104.75	37.59
	Coal Dump		7.32	02.63
	Waterfilled Quarry		6.05	02.17
	Total Mining Area		**156.93**	**56.31**
Settlement	Urban		00.08	00.03
	Industrial		00.70	00.26
	Toal Settlement		**00.78**	**00.29**
Waste Land	Waste Land		34.12	12.24
	Total Waste Land		**48.80**	**17.51**
Water Body	River,Nala, Stream etc		00.33	00.12
	Total Leasehold area		**278.68**	**100.00**

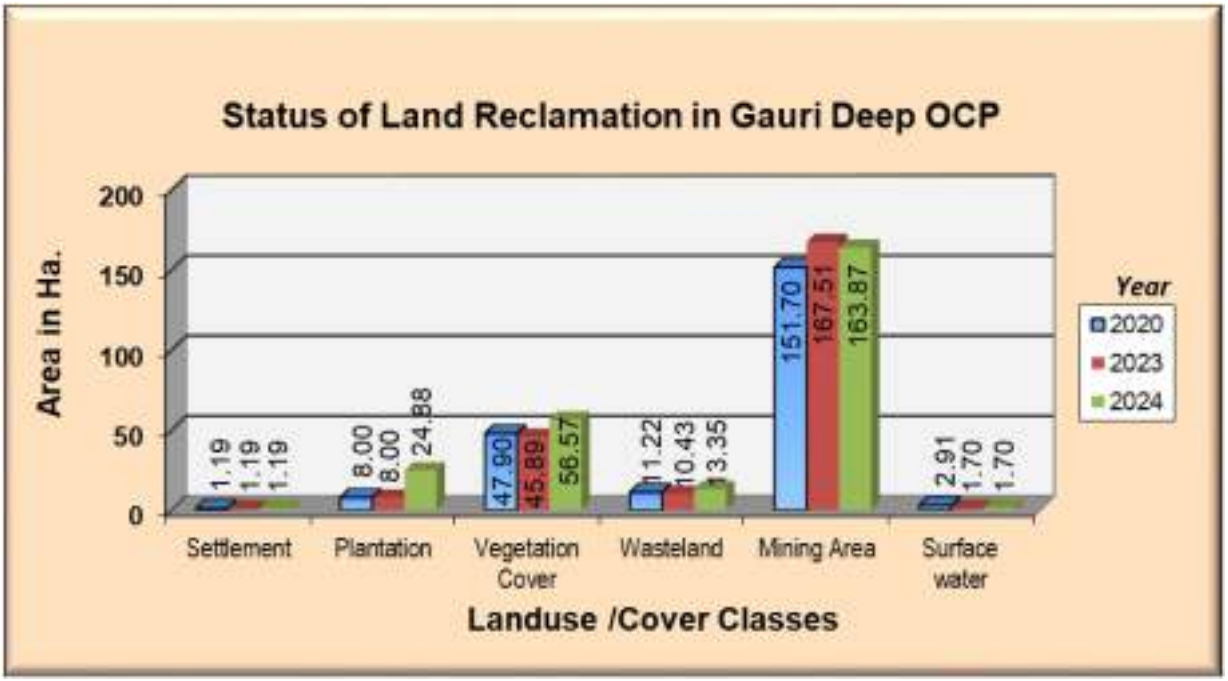


Figure-4

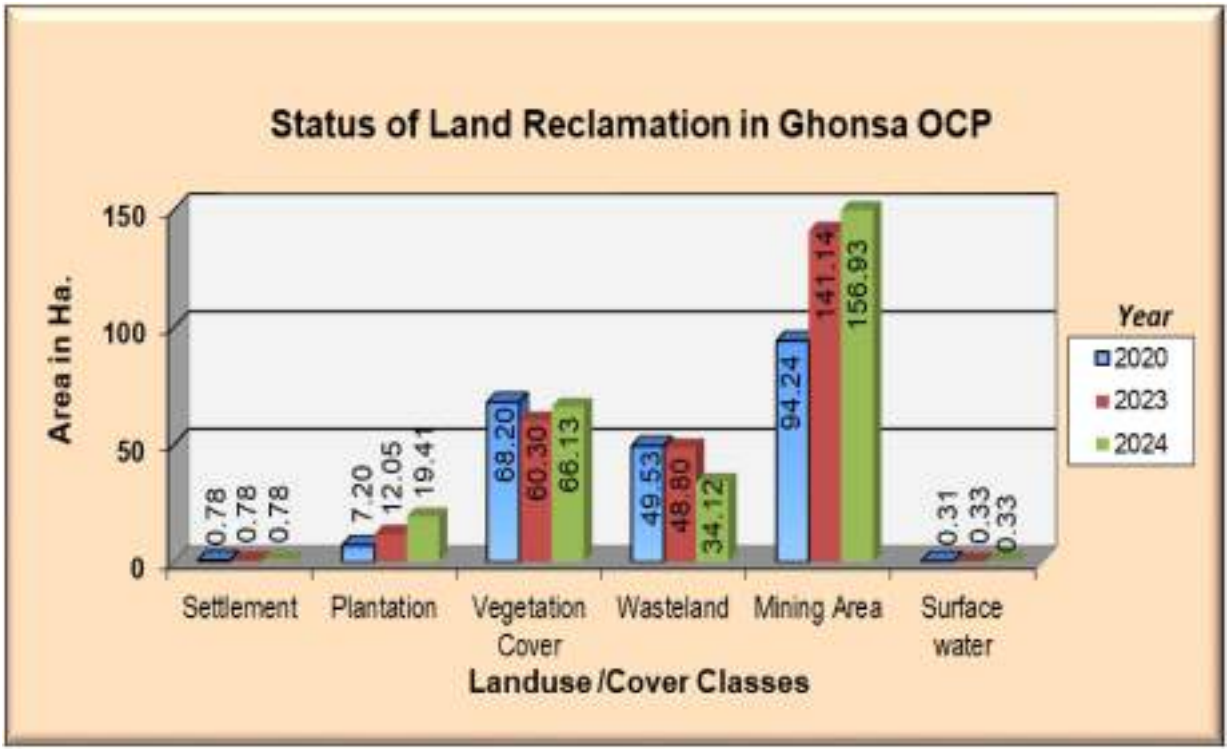


Figure-5

शब्द-कोष		
1	Land Reclamation	भूमि पुनरुद्धार
2	Over Burden	अधिभार
3	Monitoring	निगरानी
4	Report	प्रतिवेदन
5	Executive Summary	कार्यकारी सारांश
6	Opencast Mine	खुली खदान
7	Objective	उद्देश्य
8	Methodology	कार्य प्रणाली अथवा प्रक्रिया
9	Table	तालिका
10	List of Tables	तालिकाओं की सूची
11	Map	मानचित्र
12	Social Forestry	सामाजिक वानिकी
13	Plantation	पौधारोपण
14	Million	घनमीटर
15	Background	पृष्टभूमि
16	Planning	योजनाबद्ध
17	Asses	आकलन
18	Status	स्थिति
19	Regularly	निरंतर
20	Satellite	उपग्रह
21	Subsidiary	अनुषांगिक
22	Production	उत्पादन
23	Biological Reclamation	जैविक पुनरुद्धार
24	Technical Reclamation	तकनिकी पुनरुधार
25	Leasehold Area	पट्टाक्षेत्र
26	Excavated Area	उत्खनन क्षेत्र
27	Active mining	सक्रिय खनन
28	Environmental Protection	पर्यावरण संरक्षण
29	Remedial Measure	उपचारात्मक उपाय
30	Interval	अंतराल
31	Systematic Error	व्यवस्थित त्रुटियँ।
32	Error	अशुद्धियाँ
33	Curvature	वक्रता
34	Geometric	ज्यामितिक
35	Distortion	विरुपण
36	Plantation	पौधारोपण

37	Capacity	क्षमता
38	Software	सॉफ्टवेयर
39	Class	वर्ग
40	Accuracy	सटीकता
41	Statistical Separation	सांख्यिकीय पृथक्करण
42	Cubic meter	घनमीटर
43	Depicted	दर्शाया गया
44	Percentage	प्रतिशत
45	Salient Findings	मुख्य निष्कर्ष
46	Methodology	पद्धति
47	Data Procurement	डाटाक्रय
48	Satellite data Processing	उपग्रह डाटा प्रसंस्करण
49	Rectification and geo-referencing	सुधार और भूसन्दर्भ-
50	Image enhancement	छवि गुण वृद्धि
51	Training set selection	प्रशिक्षण सेट का चयन
52	Classification and Accuracy assessment	वर्गीकरण और मूल्यांकन की सटीकता
53	Area calculation	क्षेत्र गणना
54	Temporal	लौकिक
55	Processing	प्रसंस्करण
56	Overlay of Vector data base	वेक्टर डाटाबेस का अरोपन
57	Pre-field map preparation	क्षेत्र जाने के पहले नक्शे की त्तैयारी
58	Ground Truthing	भू-सत्यापन
59	Ground Information	भू- सुचना
60	Interpretation	व्याख्या
61	Eco-system	पारिस्थितिकी तंत्र
62	Minor	मामुली
63	Water Drainage	जलनिकाय
64	Interval	अंतराल
65	Maximum	अधिकतम
66	Coal field	कोयला क्षेत्र
67	Design	परिकल्पना
68	Superimpose	आरोपित
69	Update	अद्यतनीकरण/नवीनीकरण
70	Cumulative	संचयित
71	Embankment	तटबंध
72	Cluster	खुली तथा भूमिगत खदानों के समूह

ABBREVIATIONS

SoI	Survey of India
MoEF & CC	Ministry of Environment, Forest & Climate Change
CIL	Coal India Limited
ECL	Eastern Coalfields Limited
BCCL	Bharat Coking Coal Limited
CCL	Central Coalfields Limited
WCL	Western Coalfields Limited
SECL	South Eastern Coalfields Limited
NCL	Northern Coalfields Limited
MCL	Mahanadi Coalfields Limited
NEC	North Eastern Coalfields
CMPDIL	Central Mine Planning & Design Institute Ltd
NRSC	National Remote Sensing Centre
R2/ R2A	Resource Sat Satellites
LISS - 4	Linear Imaging and Self Scanning Sensor
FCC	False Color Composite
OCP	Opencast Project
UGP	Underground Project
OB	Over Burden
GCP	Ground Control points
GIS	Geographic Information System
WGS-84	World Geodetic System
UTM	Universal Transverse Mercator

GLOSSARY

Sl.	Term	Definition
1.	Land Reclamation	To manage, reclaim and restore mined out/ degraded land as close as possible to its original stage.
2.	Over Burden	The material that lies above the coal seam/ deposit
3.	Monitoring	A process of evaluation to check or keep record for a period of time.
4.	Opencast Coal Mine	Open-pit mining, also known as opencast mining, is a surface mining technique that extracts minerals from an open pit in the ground.
5.	Social Forestry	Social forestry is the management and protection of forests and afforestation of barren and deforested lands with the purpose of helping environmental, social and rural development. Plantation (Social/ Avenue or other) carried out outside mining area.
6.	Biological Reclamation	Plantation on Backfilled areas (Stabilized Internal Dumps)
7.	Technical Reclamation	Area under backfilling (Over burden dumped inside the mine voids) in mining area.
8.	Green Cover Generated	Total Plantation carried out in the lease area of Project. This includes Plantation on Backfill, Plantation on OB and Social Forestry.
9.	Leasehold Area	The area, for which lease is granted for the purpose of undertaking mining and allied operations.
10.	Excavated area	Mined out area which includes active mining, area under backfilling and plantation on backfilled areas
11.	Active Mining	Mining areas which include Coal Quarry, Advance Quarry, Quarry Filled with Water etc.
12.	Environmental Protection	It is the practice of protecting the natural environment by individuals, organizations and governments. Its objectives are to conserve natural resources and the existing natural environment and, where possible, to mitigate damage and reverse trends.
13.	Remedial Measure	Any measure or action required or undertaken to investigate, monitor, clean up, remove, treat, prevent, contain or otherwise remediate the presence or release of any hazardous substance or activity.
14.	Systematic Error	Every measurement differing from the true measurement in the same direction, and even by the same amount in some cases.

15.	Geometric Distortion	It refers to the improper positioning of any image with respect to their true geographic position when viewed in a properly scaled common image display plane.
16.	Land Use/ Cover Class	Land cover is what covers the surface of the earth and land use describes how the land is used.
17.	Accuracy	The closeness of agreement between a measured quantity value and a true quantity value.
18.	Environmental Clearance	Environmental Clearance (EC) for any developmental projects like coal mining projects etc. has been made mandatory by the Ministry of Environment, Forests and Climate Change (MoEF & CC) through its Notification issued on 27.01.1994 under the provisions of Environment (Protection) Act, 1986.
19.	Rectification and Geo-referencing	Geo-referencing is the assigning of absolute location of a data point or data points. Geo-rectification refers to the removal of geometric distortions between sets of data points, most often the removal of terrain, platform, and sensor induced distortions from remote sensing imagery.
20.	Image Enhancement	It is the process of modifying digital images so that the results are more suitable for processing or further image analysis.
21.	Training set selection	It is a portion of a data set used to fit or train a model for prediction or classification of values that are known in the training set, but unknown in other (future) data.
22.	Image Classification	It refers to the task of extracting information classes from a multiband raster image. The resulting raster from image classification can be used to create thematic maps.
23.	Temporal Changes	The 'temporal change' means the change in any entity with a period of time.
24.	Ground Truthing	Collection of primary/ basic information from ground realities for satellite image interpretation and thematic mapping.
25.	Cluster	Group of opencast and/ or underground mines clubbed together for administrative purposes.
26.	Arc GIS	GIS Software used for Map preparation
27.	ERDAS IMAGINE	Satellite Image Data Classification Software

Central Mine Planning & Design Institute Ltd.
(A Subsidiary of Coal India Ltd.)
Gondwana Place, Kanke Road, Ranchi 834031, Jharkhand
Phone: (+91) 651 2230001, 2230002, 2230483, FAX (+91) 651 2231447, 2231851
Website : www.cmpdi.co.in, Email : cmpdihq@cmpdi.co.in

Maharashtra Pollution Control Board

महाराष्ट्र प्रदूषण नियंत्रण मंडळ

FORM V

(See Rule 14)

Environmental Audit Report for the financial Year ending the 31st March 2024

Unique Application Number	***Submitted Date***
MPCB-ENVIRONMENT_STATEMENT-0000073400	28-09-2024

PART A

Company Information

Company Name	***Application UAN number***
Western Coalfields Limited, Ghonsa Opencast Mine	-

Address

Office of the Sub Area Manager, Ghonsa-Kumbharkhani, Po.- Rasa, Tal.- Wani, Distt. - Yavatmal, Maharashtra

Plot no	***Taluka***	***Village***
25/1,2,3	Wani	-
Capital Investment (In lakhs)	***Scale***	***City***
12357.61	L.S.I	Yavatmal
Pincode	***Person Name***	***Designation***
445304	sayyed Nazimuddhin	Sub Area Manager, Ghonsa Sub Area
Telephone Number	***Fax Number***	***Email***
9112330975	07239241357	samghonsa@gmail.com
Region	***Industry Category***	***Industry Type***
SRO-Chandrapur	Red	R35 Mining and ore beneficiation
Last Environmental statement submitted online	***Consent Number***	***Consent Issue Date***
yes	Format1.0/CAC/UAN No.MPCBCONSENT-0000107029/CR/2203000019	2022-03-01
Consent Valid Upto	***Establishment Year***	***Date of last environment statement submitted***
2023-03-31	2008	Sep 21 2023 12:00:00:000AM

Industry Category Primary (STC Code) & Secondary (STC Code)

Product Information

Product Name	***Consent Quantity***	***Actual Quantity***	***UOM***
Coal	0.60	0.60	MT/A

By-product Information

By Product Name	***Consent Quantity***	***Actual Quantity***	***UOM***
NA	0	0	MT/A

Part-B (Water & Raw Material Consumption)

1) Water Consumption in m3/day

Water Consumption for	Consent Quantity in m3/day	Actual Quantity in m3/day
Process	652.00	652.00
Cooling	0.00	0.00
Domestic	18.00	18.00
All others	50.00	0.00
Total	720.00	670.00

2) Effluent Generation in CMD / MLD

Particulars	Consent Quantity	Actual Quantity	UOM
Daily Trade Effluent (including mine discharge)	4363	3711	CMD

2) Product Wise Process Water Consumption (cubic meter of process water per unit of product)

Name of Products (Production)	During the Previous financial Year	During the current Financial year	UOM
Mining	0.5316	0.407	CMD

3) Raw Material Consumption (Consumption of raw material per unit of product)

Name of Raw Materials	During the Previous financial Year	During the current Financial year	UOM
Explosive	2.58	1.651	Kg/Annum

4) Fuel Consumption

Fuel Name	Consent quantity	Actual Quantity	UOM
Diesel	0	0	KL/A

Part-C

Pollution discharged to environment/unit of output (Parameter as specified in the consent issued)

[A] Water

Pollutants Detail	Quantity of Pollutants discharged (kL/day)	Concentration of Pollutants discharged(Mg/Lit) Except PH,Temp,Colour	Percentage of variation from prescribed standards with reasons		
	Quantity	Concentration	%variation	Standard	Reason
-	0	0	-	-	-

[B] Air (Stack)

Pollutants Detail	Quantity of Pollutants discharged (kL/day)	Concentration of Pollutants discharged(Mg/NM3)	Percentage of variation from prescribed standards with reasons		
	Quantity	Concentration	%variation	Standard	Reason
-	0	0	-	-	-

Part-D

HAZARDOUS WASTES

1) From Process

Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
5.1 Used or spent oil	10.365	0.847	KL/A

5.2 Wastes or residues containing oil	0.2	0	Ton/Y

2) From Pollution Control Facilities

Hazardous Waste Type	*Total During Previous Financial year*	*Total During Current Financial year*	*UOM*
0	0	0	Ton/Y

Part-E

SOLID WASTES

1) From Process

Non Hazardous Waste Type	*Total During Previous Financial year*	*Total During Current Financial year*	*UOM*
-	0	0	Ton/Y

2) From Pollution Control Facilities

Non Hazardous Waste Type	*Total During Previous Financial year*	*Total During Current Financial year*	*UOM*
-	0	0	Ton/Y

3) Quantity Recycled or Re-utilized within the unit

Waste Type	*Total During Previous Financial year*	*Total During Current Financial year*	*UOM*
0	0	0	Ton/Y

Part-F

Please specify the characteristics(in terms of concentration and quantum) of hazardous as well as solid wastes and indicate disposal practice adopted for both these categories of wastes.

1) Hazardous Waste

Type of Hazardous Waste Generated	*Qty of Hazardous Waste*	*UOM*	*Concentration of Hazardous Waste*
5.1 Used or spent oil	0.847	KL/A	-
5.2 Wastes or residues containing oil	0	Ton/Y	-

2) Solid Waste

Type of Solid Waste Generated	*Qty of Solid Waste*	*UOM*	*Concentration of Solid Waste*
-	0	Ton/Y	-

Part-G

Impact of the pollution Control measures taken on conservation of natural resources and consequently on the cost of production.

Description	*Reduction in Water Consumption (M3/day)*	*Reduction in Fuel & Solvent Consumption (KL/day)*	*Reduction in Raw Material (Kg)*	*Reduction in Power Consumption (KWH)*	*Capital Investment(in Lacs)*	*Reduction in Maintenance(in Lacs)*
Impact of the pollution control measures taken	0	5.890	0	0	0	0

Part-H

Additional measures/investment proposal for environmental protection abatement of pollution, prevention of pollution.

[A] Investment made during the period of Environmental Statement

Detail of measures for Environmental Protection	Environmental Protection Measures	Capital Investment (Lacks)
Revenue Expenditure on pollution control measures	-	0.92

[B] Investment Proposed for next Year

Detail of measures for Environmental Protection	Environmental Protection Measures	Capital Investment (Lacks)
Miscellaneous Environmental protection activities	Miscellaneous Environmental protection activities	10

Part-I

Any other particulars for improving the quality of the environment.

Particulars

-

Name & Designation

Syed Nazimuddin, Sub Area Manager, Ghonsa Sub Area

UAN No:

MPCB-ENVIRONMENT_STATEMENT-0000073400

Submitted On:

28-09-2024
